




TIME SQUARE TK TS335

Weekly Report

Date : 2026.Aug.09

SITE LOCATION

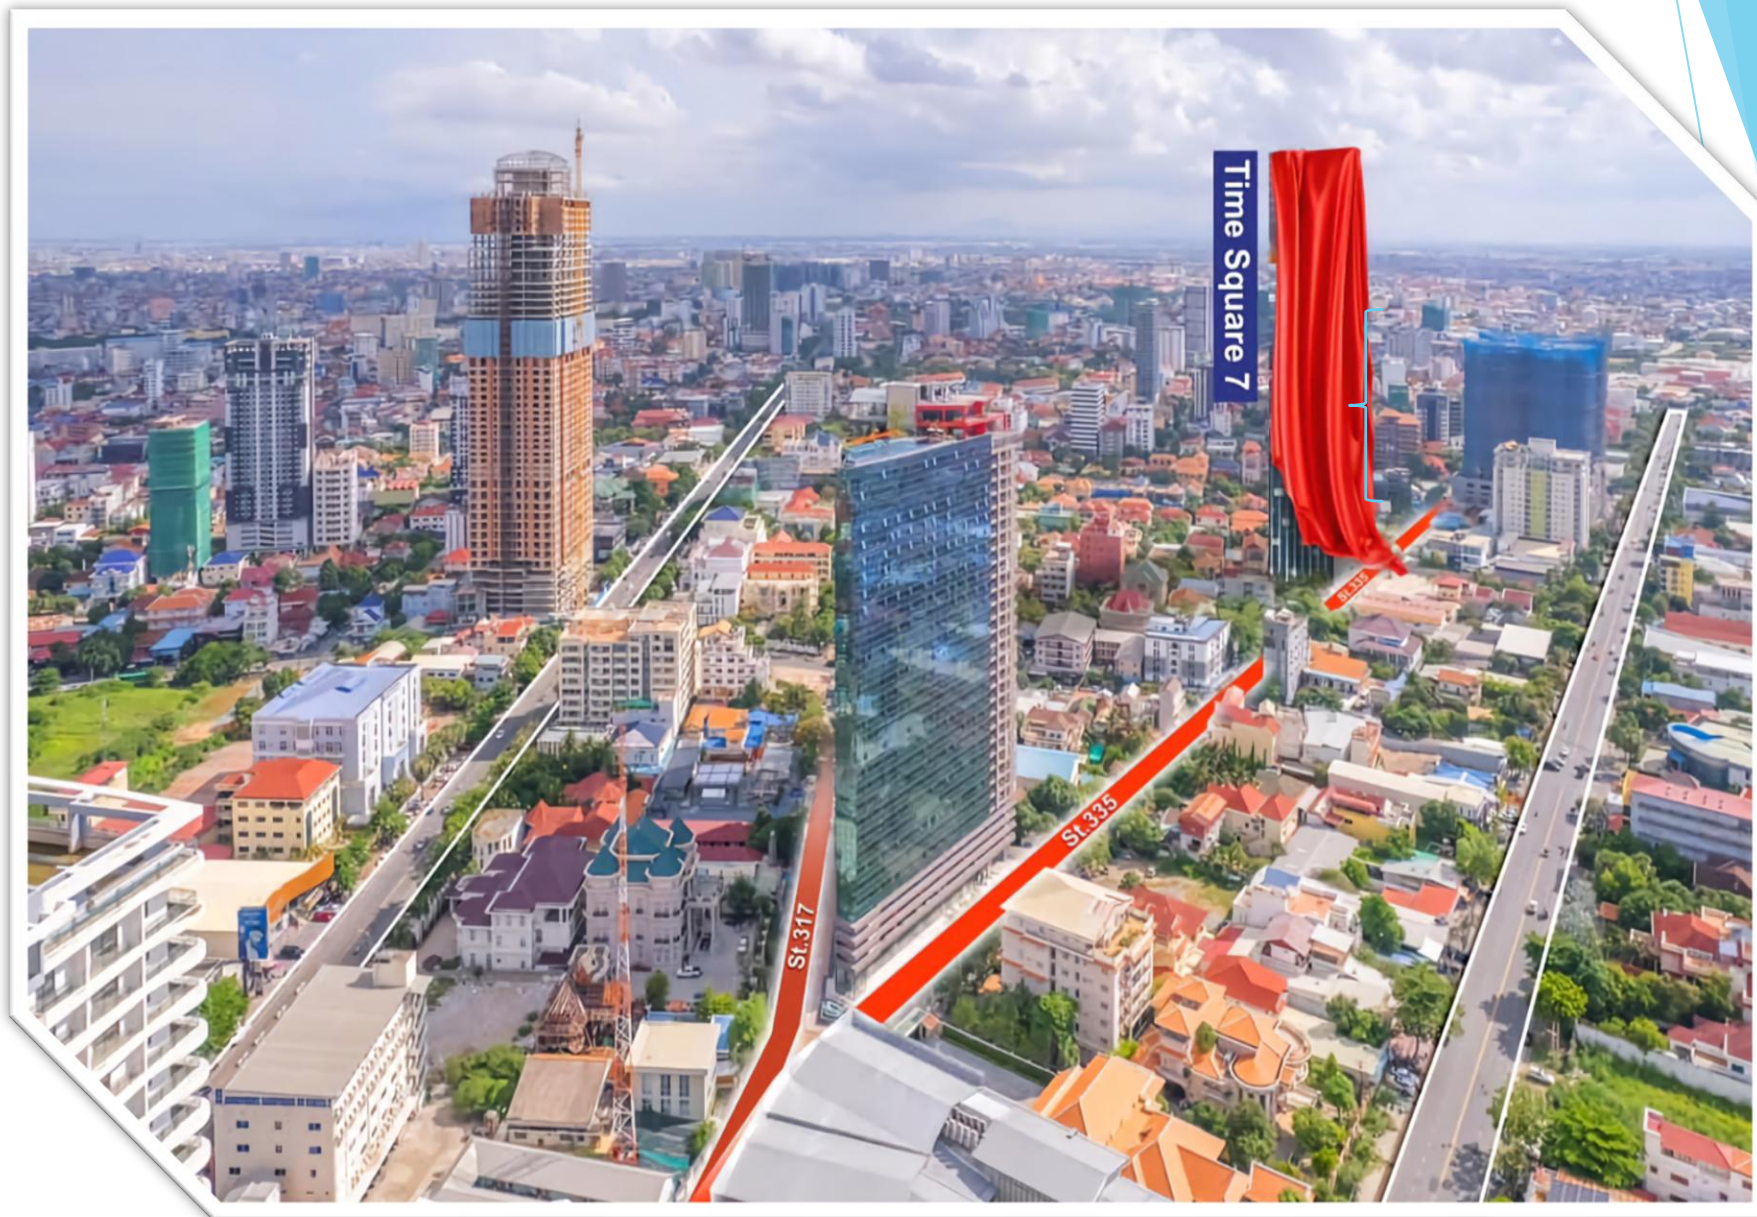

SITE LOCATION






TIME SQUARE 335 ENVIRONMENT



TOOL BOX MEETING




SITE CLEANING

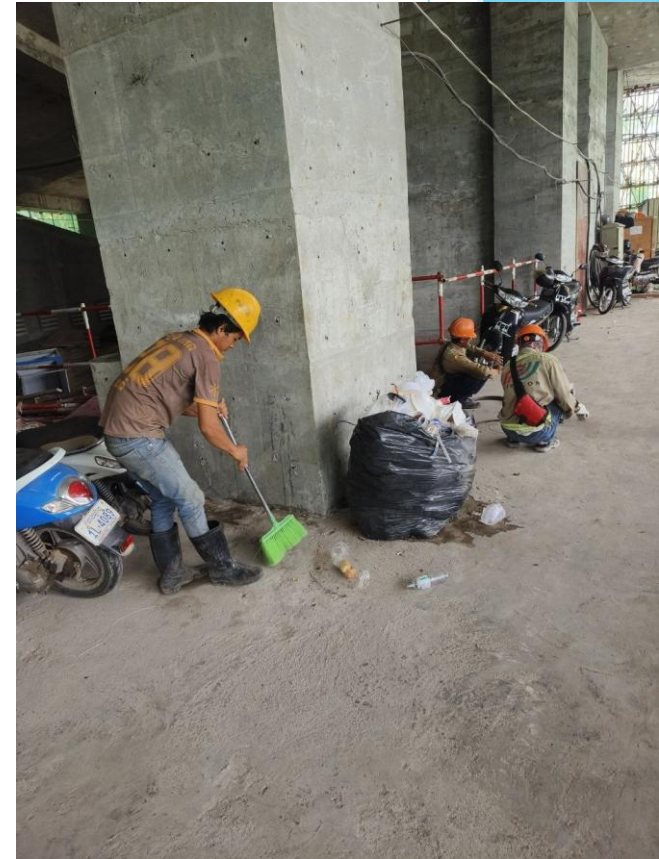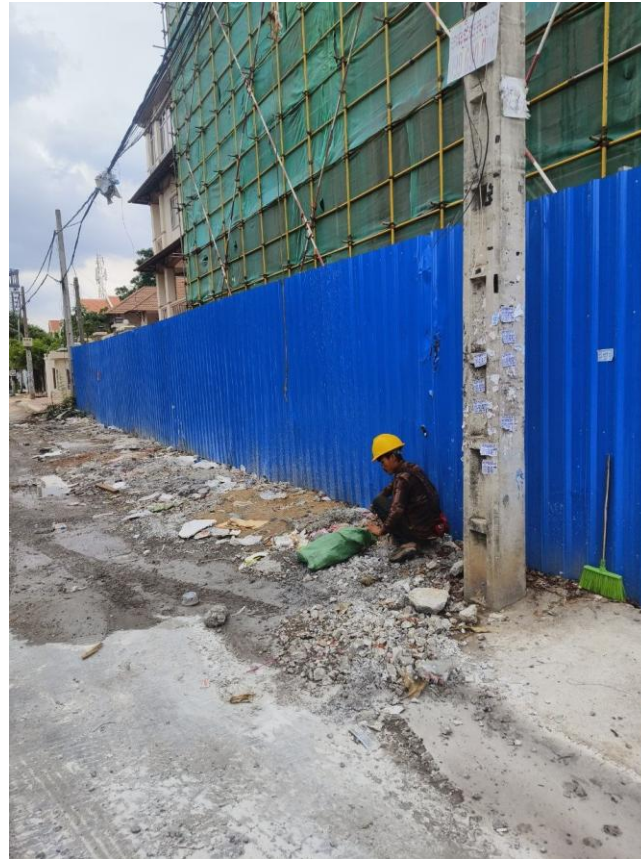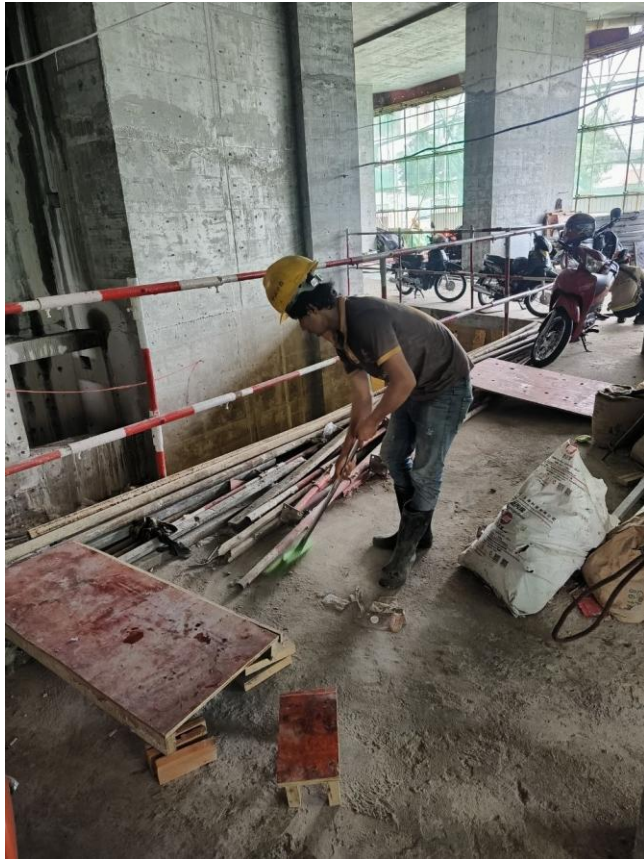

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed

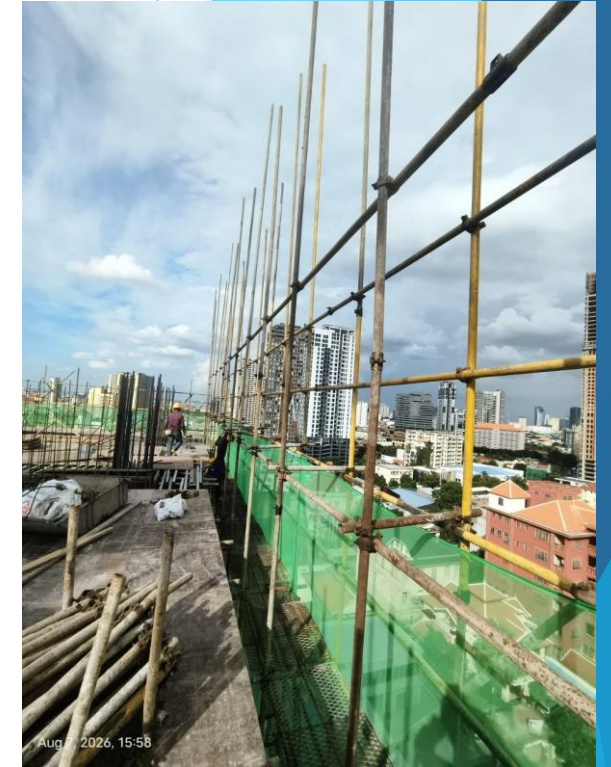

13F External safety netting scaffolding installation

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



12F Column rebar installation work (Done)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



12F Column rebar installation work (Done)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



12F Column rebar installation work (Done)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



12F Wall rebar installation work (Done)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



12F Wall rebar installation work (Done)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



12F Column & Wall Formwork installation work (Done=40%)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



12F Column & Wall Formwork installation work (Done=40%)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



13F Slab Formwork installation work (Done)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed



13F Slab Formwork installation work (Done)

13F MAIN STRUCTURE PROGRESS



Up to 09th AUG 20% completed



Slab 11F&12F PT Grouting work (Done)

13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed

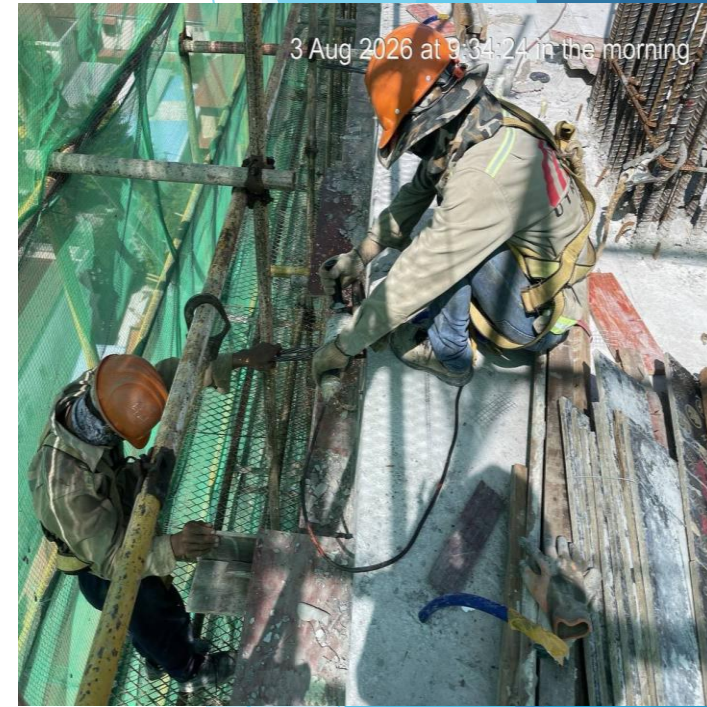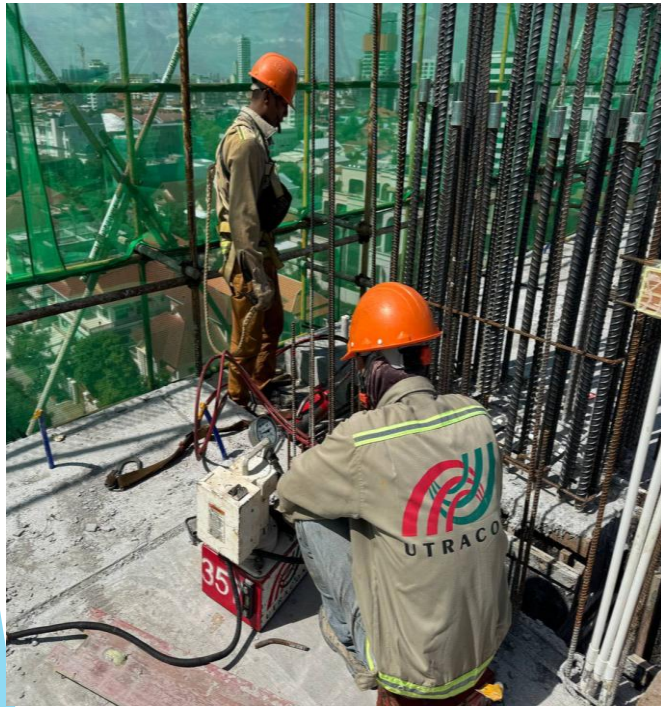

Slab 12F Stressing work (Done)

13F MAIN STRUCTURE PROGRESS


Up to 09th AUG 20% completed



13F PT Materials Arrangement work


13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed

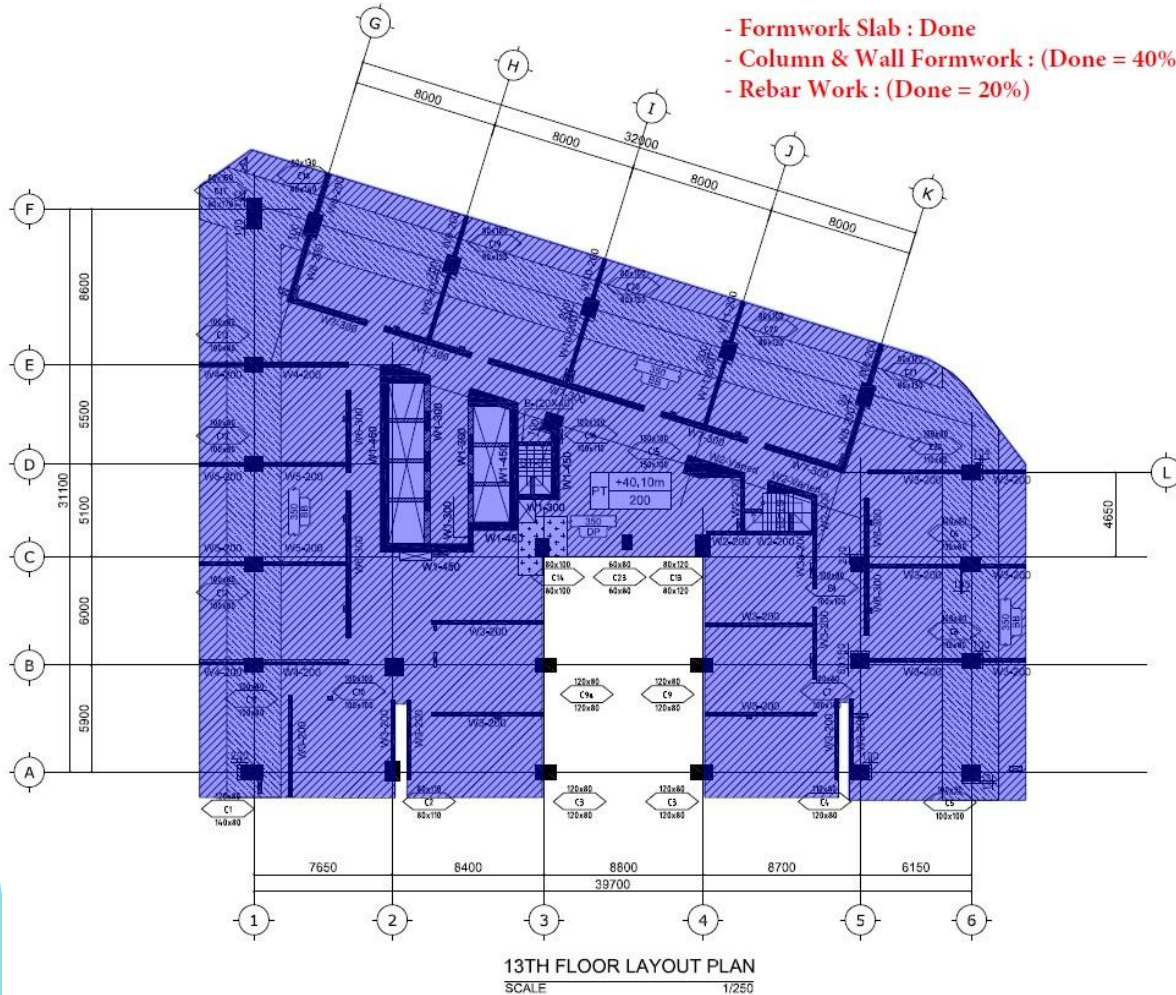


13F MAIN STRUCTURE PROGRESS

Up to 09th AUG 20% completed

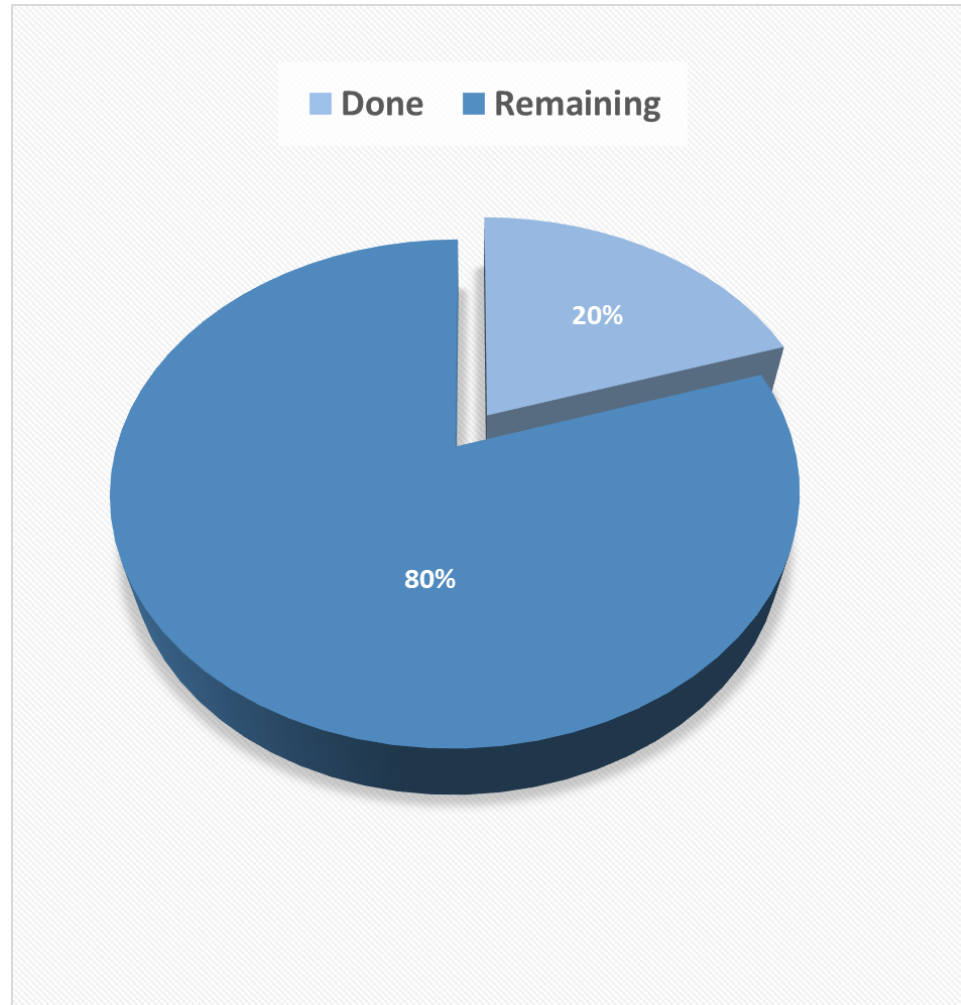

13F MEP PROGRESS

Up to 09th AUG 30% completed

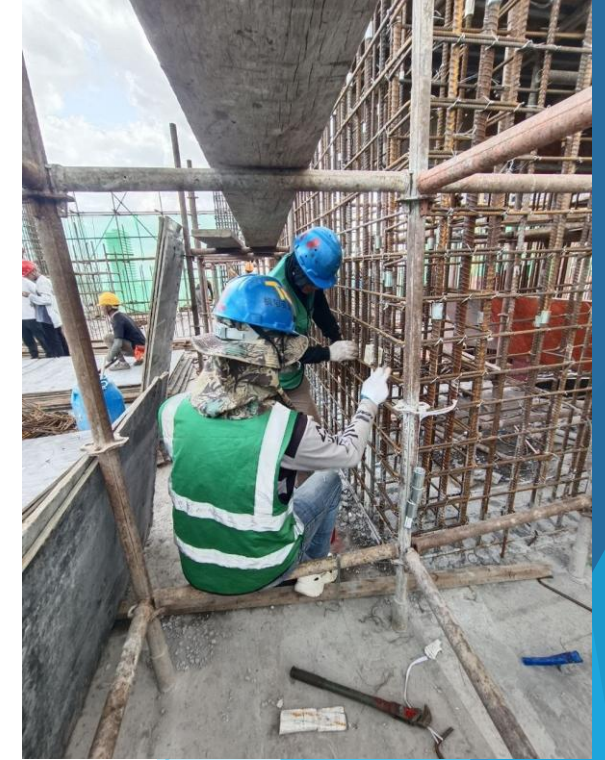

12F MEP System Installation at Column & wall (Done=60%)

13F MEP PROGRESS

Up to 09th AUG 30% completed



12F MEP System Installation at Column & wall (Done=60%)

13F MEP PROGRESS

Up to 09th AUG 30% completed



13F MEP Slab System Installation work Sleeve & Conduit (Done=40%)

13F MEP PROGRESS


Up to 09th AUG 30% completed



13F MEP Slab System Installation work Sleeve & Conduit (Done=40%)

13F MEP PROGRESS

Up to 09th AUG 30% completed

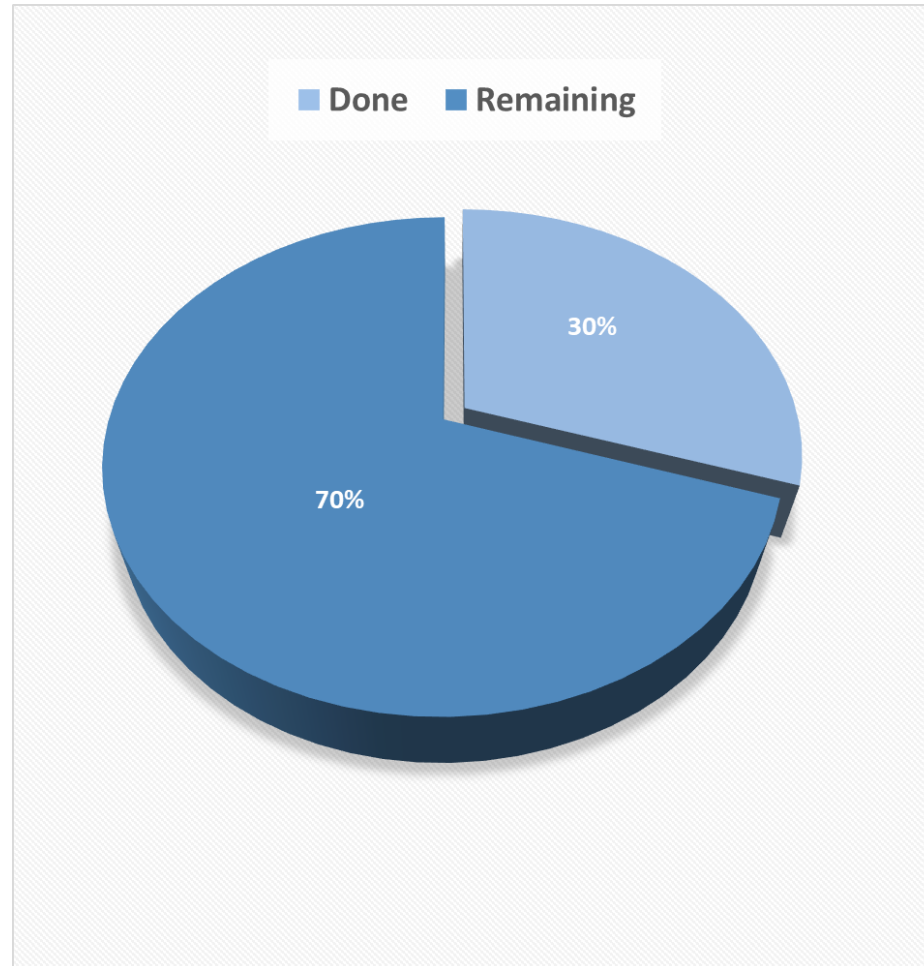


INSPECTION WORK



12F Column & Wall MEP System installation inspection

INSPECTION WORK

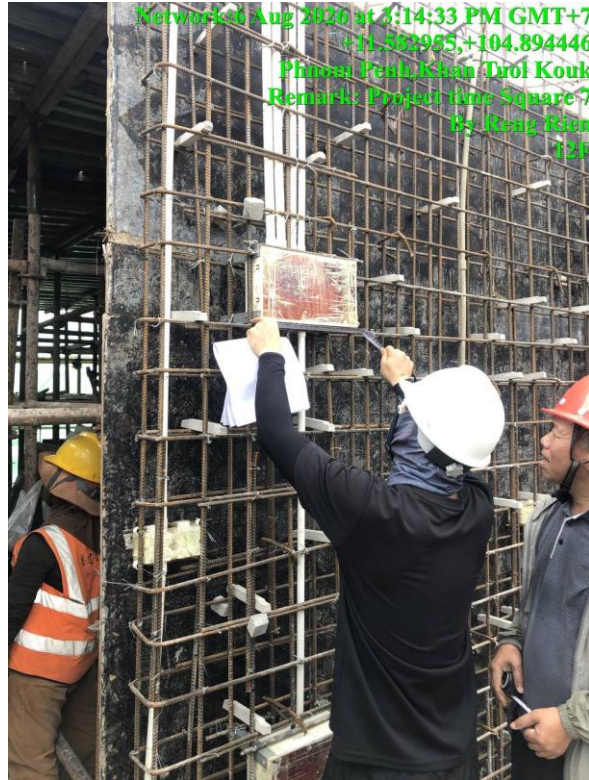

12F Column & Wall MEP System installation inspection

INSPECTION WORK




11F&12F PT Grouting Inspection

INSPECTION WORK





12F PT Elongation Inspection

INSPECTION WORK

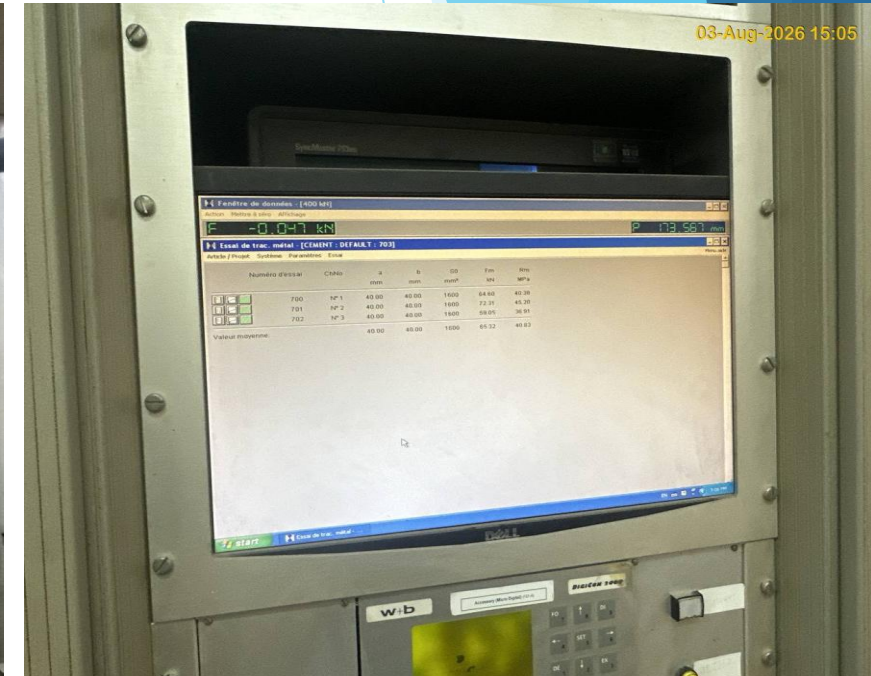

8F PT Grouting Compressive Inspection

INSPECTION WORK

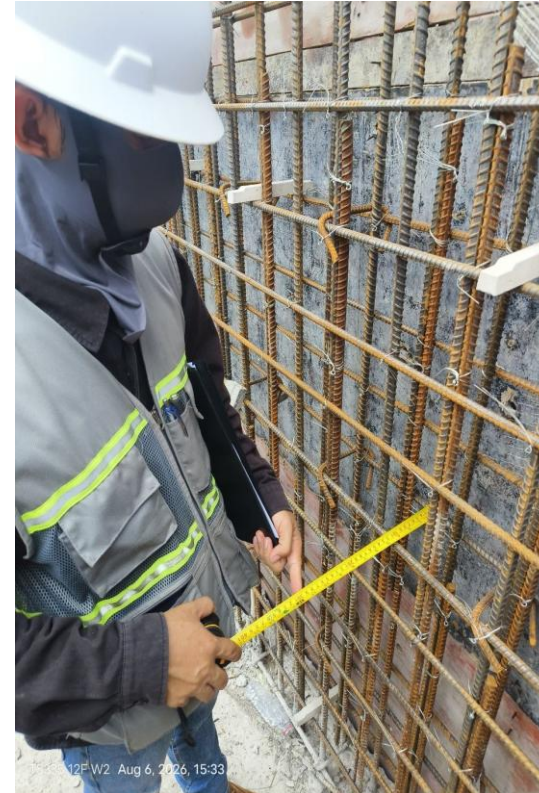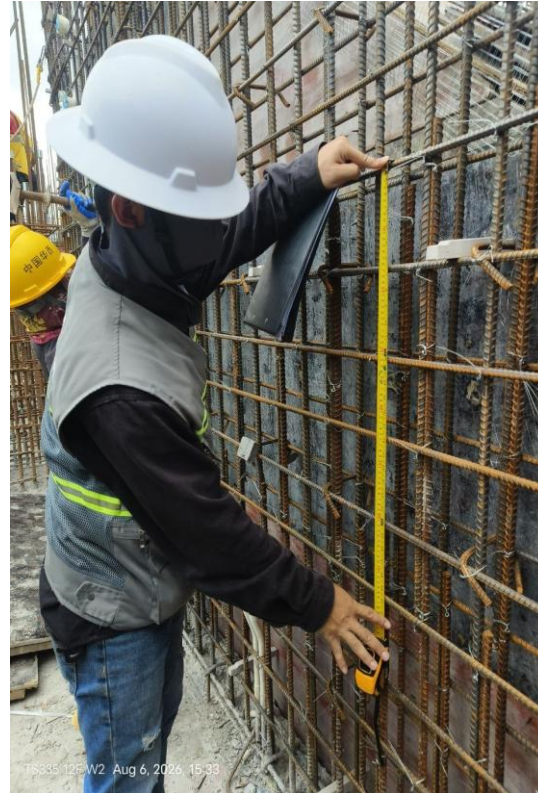


12F Column & Wall Rebar Installation Inspection

INSPECTION WORK



12F Column & Wall Rebar Installation Inspection

INSPECTION WORK

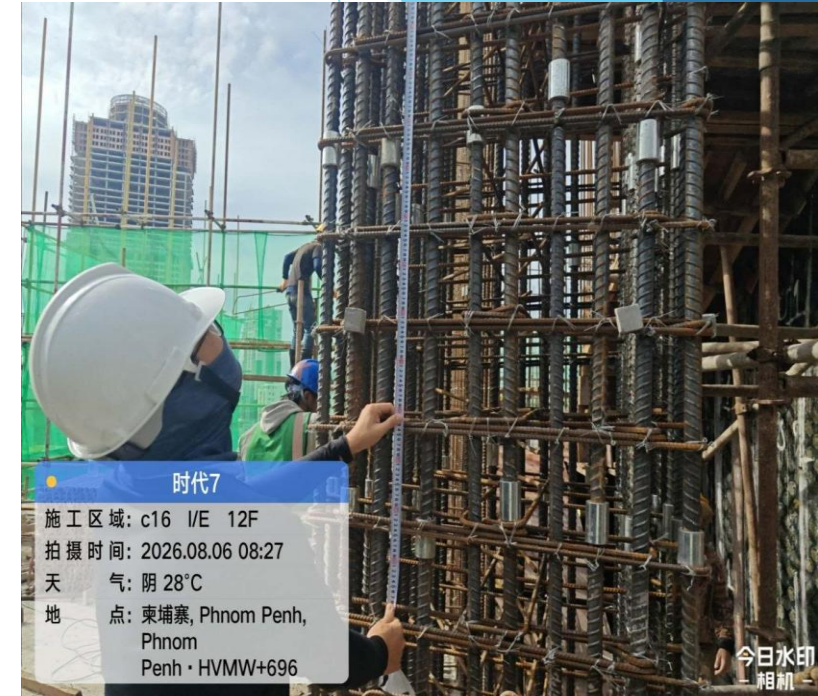


12F Column & Wall Rebar Installation Inspection

INSPECTION WORK




12F Column & Wall Rebar Installation Inspection

INSPECTION WORK

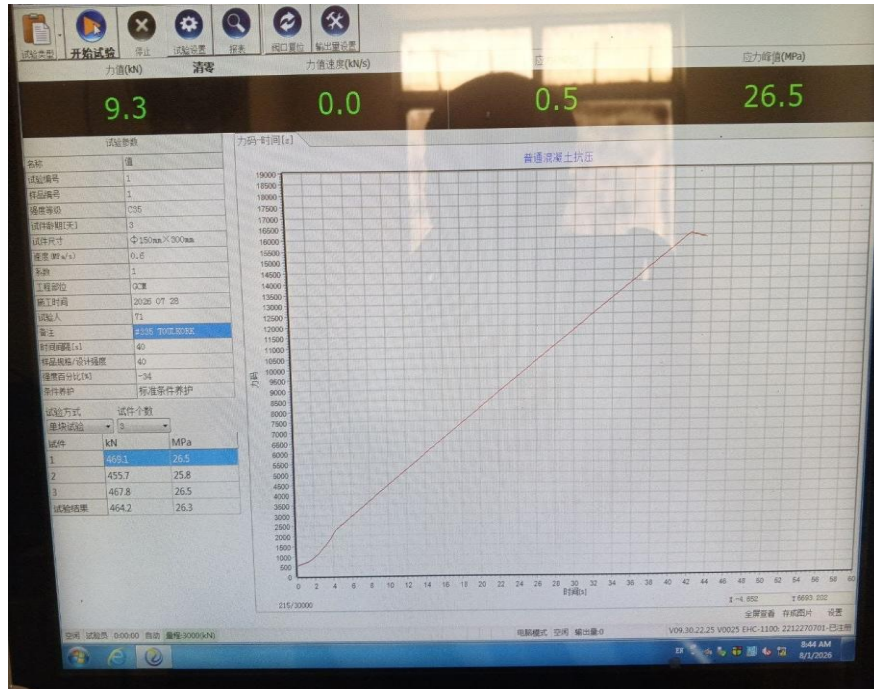


12F Concrete Compressive Inspection Report CY35

INSPECTION WORK

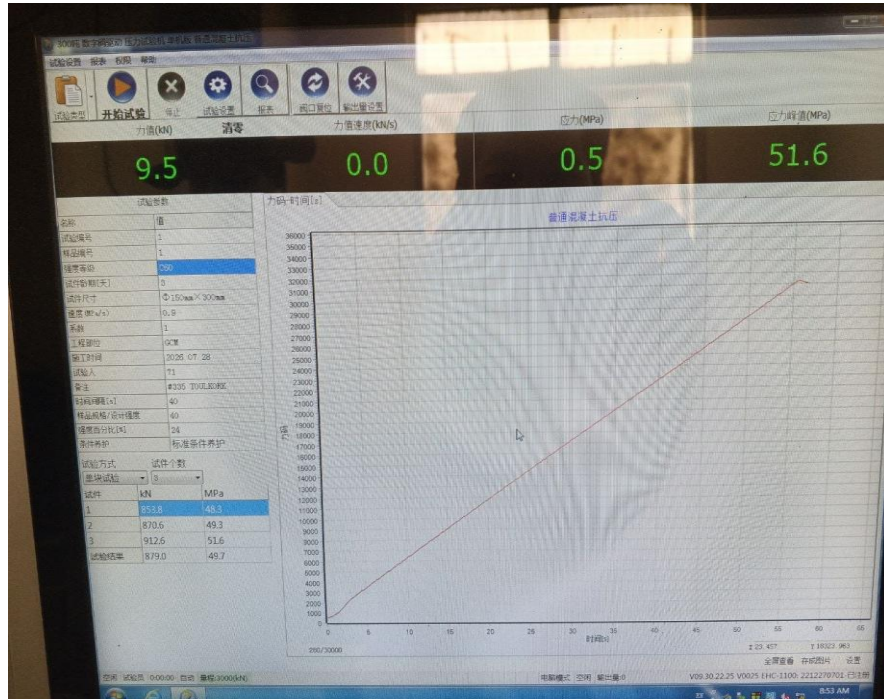

12F Concrete Compressive Inspection Report CY60

INSPECTION WORK

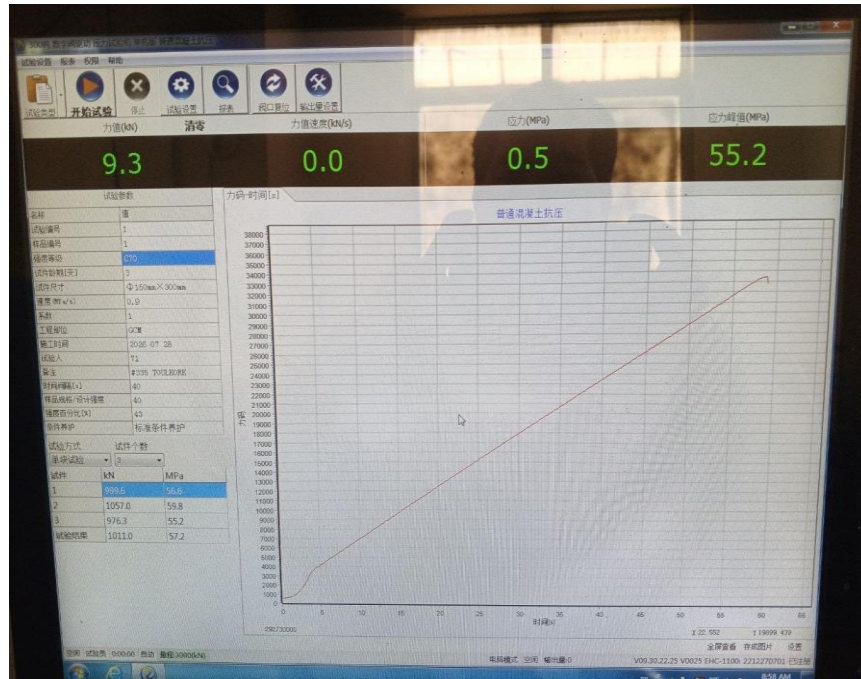

12F Concrete Compressive Inspection Report CY70

MATERIALS SUPERVISION



ផ្ទះលេខ 10 ផ្លូវ 289
 សង្កាត់បឹងកក់
 ខណ្ឌទួលគោក
 (ទល់មុខបញ្ជាការដ្ឋាន
 PM លើផ្ទៃប្រទេស)

ឆន ម៉ាច
លក់គ្រឿងសំណង់
កែប្រែ

N°: 003508
 Tel: 012 806 618
 : 011 806 618
 : 016 756 370

លេខរថយន្ត: ៤៣៣៥
 លក់ជូន: ៤៣៣៥

ល.រ	ប្រភេទសម្ភារៈ	ចំនួន	តម្លៃរាយ	តម្លៃសរុប
1	ឧស្ម័ន ២២	២៣៣	16'	32'
2				
3				
4				
			TOTAL	

ថ្ងៃទី 29 ខែ 7 ឆ្នាំ 2025

អ្នកទទួល/ The Buyer
R. fapth...

អ្នកលក់/ The Seller
[Signature]

MATERIALS SUPERVISION

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

Form 1 (1/2008) - 10/12/2008

Page 1 of 1

Handwritten notes: 30.6.2004, 30.6.2004, 30.6.2004

MATERIALS SUPERVISION





*PASSION FOR
PROGRESS*

