

49F

HIGHGROUND Omakase

48F

Time Square Facilities

38-47F

Exclusive Floor
(Duplex 3,4 Bedrooms)

37F

Time Square Lounge
Cafe Lounge / Game Room
Kid Playground / Green Park
VIP Party Room / Meeting Room
Karaoke / Cinema

8-36F

Classic Floor
(1,2 Bedrooms)

Time Square 302

2-7F

Carpark Floor


GF

Lobby Floor




2025.June.19

26F PROGRESS UP TO 19th June 2025

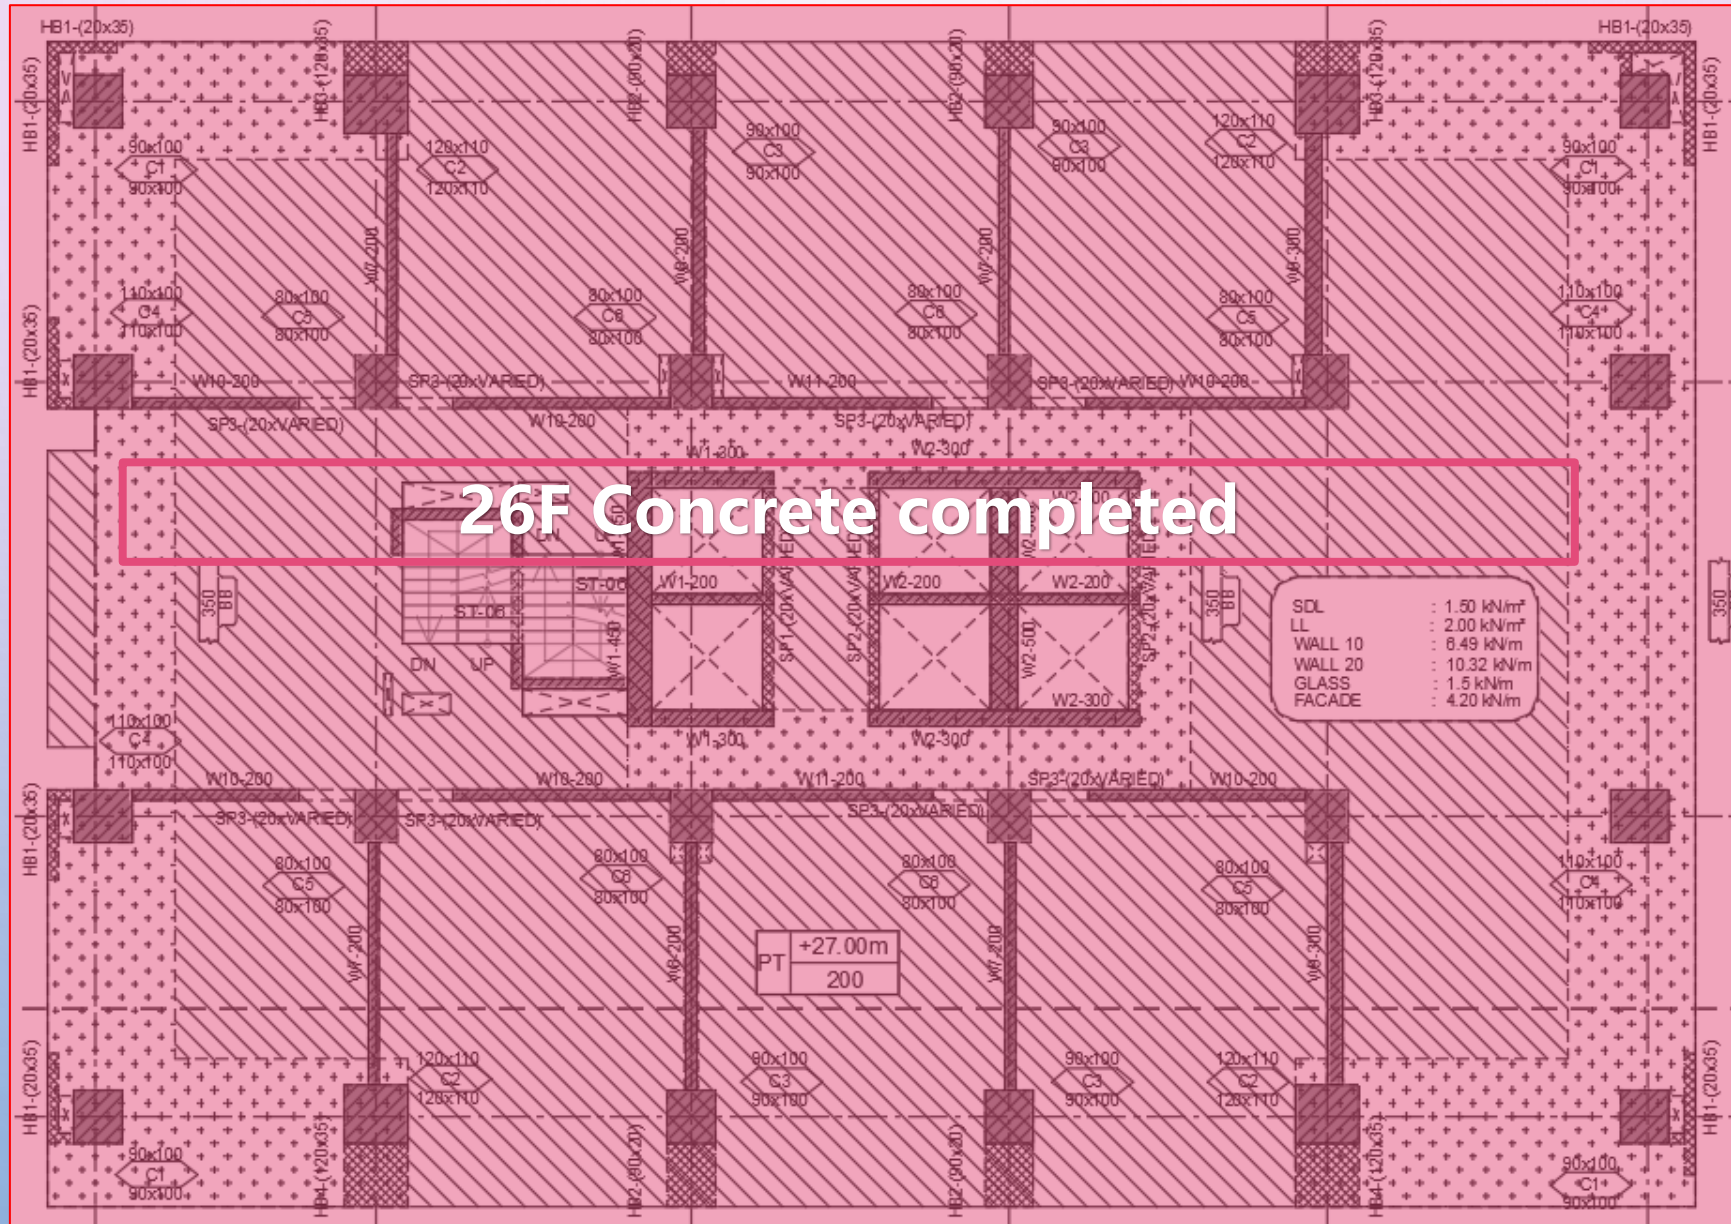


SCHEDULE OF STRUCTURE FOR WHOLE PROJECT TS302

Plan to complete the whole structure on January 2026

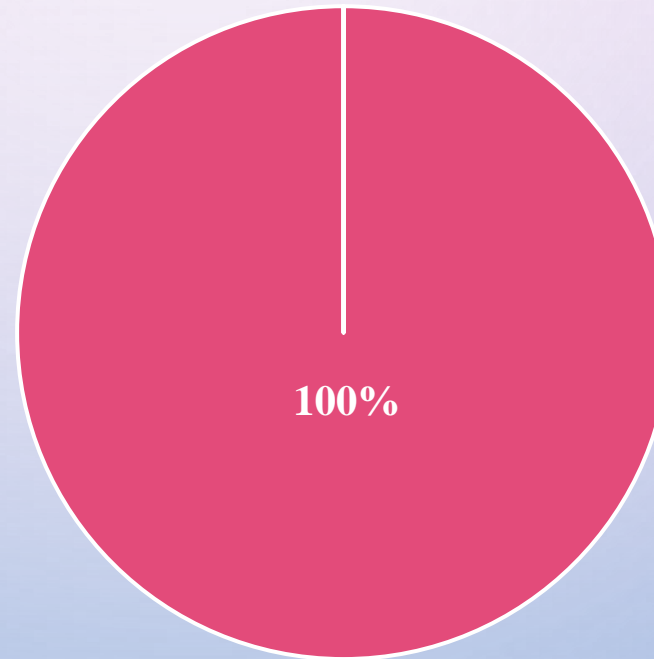

■ Completed

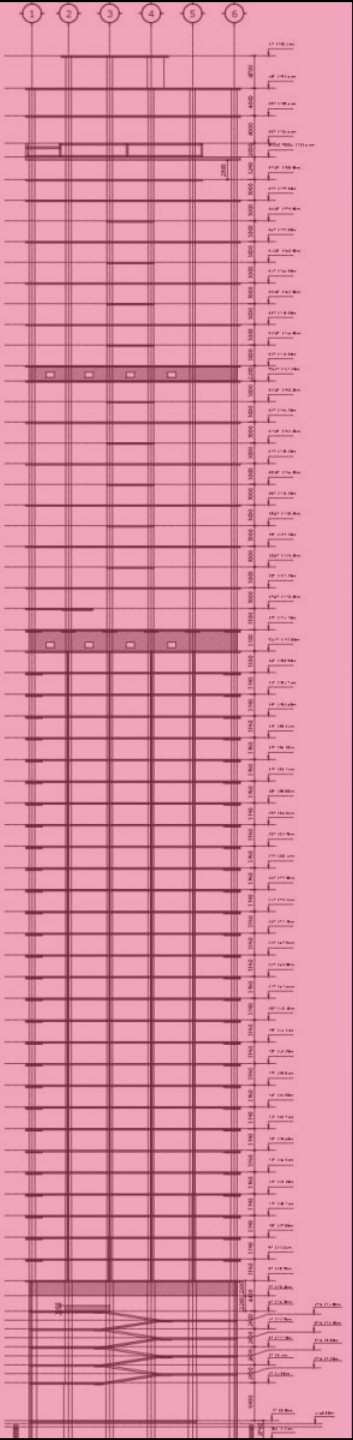


26F WORK PROGRESS UP TO 09th June 2025



**Progress
27F**

Completed

UPPER-STRUCTURE WORK PROGRESS UP TO 19th June 2025

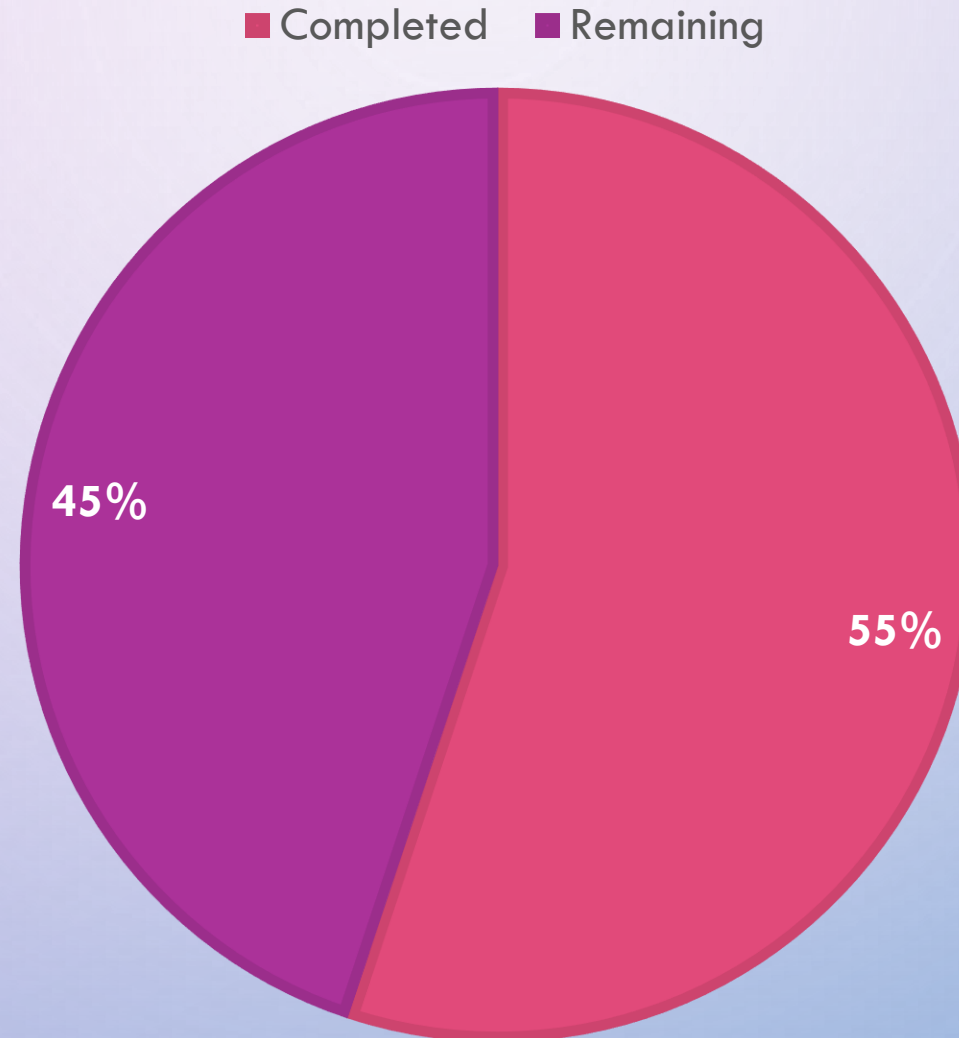


WORK PROGRESS


Schedule Plan : 2025.June.20

- + 26F & 27F: Completed
- + 28F: Prepare for Rebar

-Schedule Completion of 27F by 20th June/2025

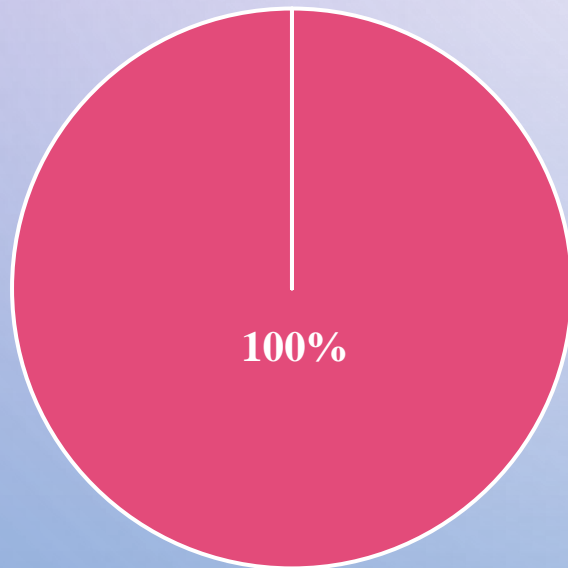

■ Completed

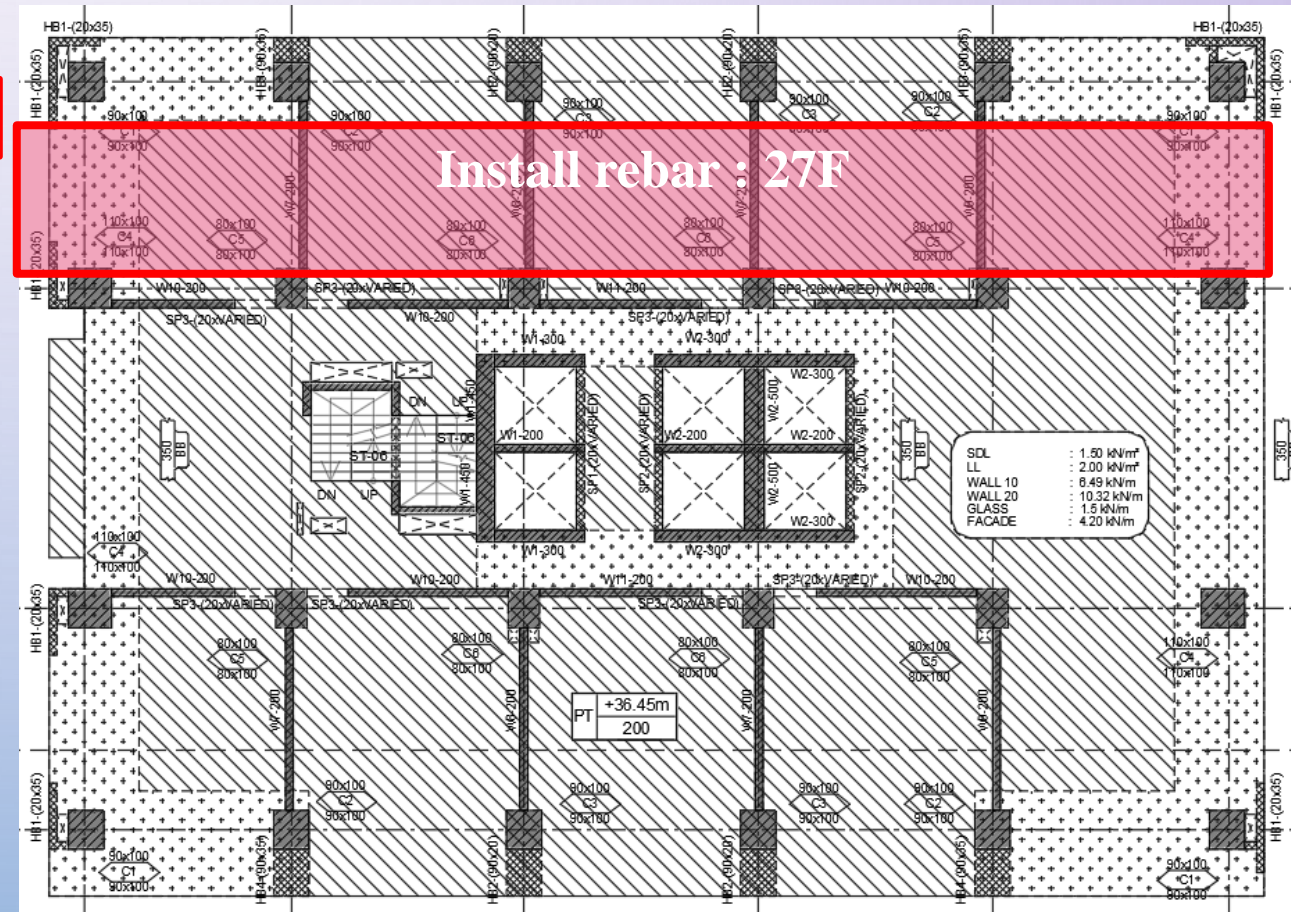

SITE TOP VIEW



SITE ENTRANCE




TOOLBOX MEETING



Explanation about safety, PPE and other issues at site environment.

STRUCTURE WORK

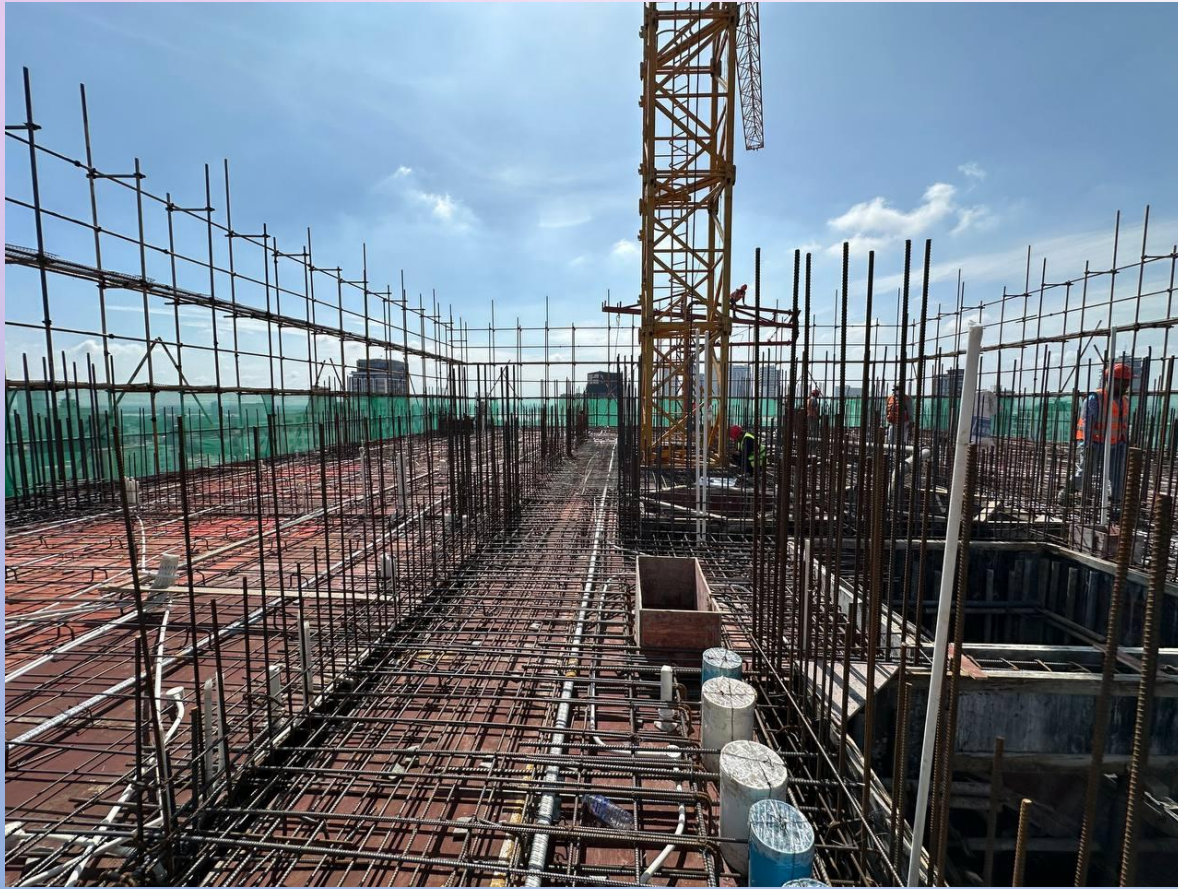

Installation the Rebar of 27F

STRUCTURE WORK



Inspection the Rebar of Slab: 27F

PT INSPECTION



Inspection the PT of Slab: 27F

STRUCTURE WORK



Testing slump before casting concrete

STRUCTURE WORK



Casting concrete of 26F

STRUCTURE WORK



Inspection the rebar of Column & Wall : 26F

MATERIALS SUPERVISION



Inspection the rebar

MASONRY WORK



Inspection of brick wall installation work

MASONRY WORK



Inspection of Plastering work

WATERPROOFING WORK



Inspection of Waterproofing work

HSE WORK



Noise Testing

HSE WORK



Site Cleaning

PASSION FOR PROGRESS

THANK YOU

