



Time Square

Time Square 11 — Report

29. AUG. 2026



Weekly Report





Time Square 11


PROJECT LOCATION





Time Square 11

Time Square 11 Point Of View





Time Square 11

Time Square 11 Point Of View







Time Square 11

CBP PROGRESS

CBP PILES (168/168 PILES)



Done
100%

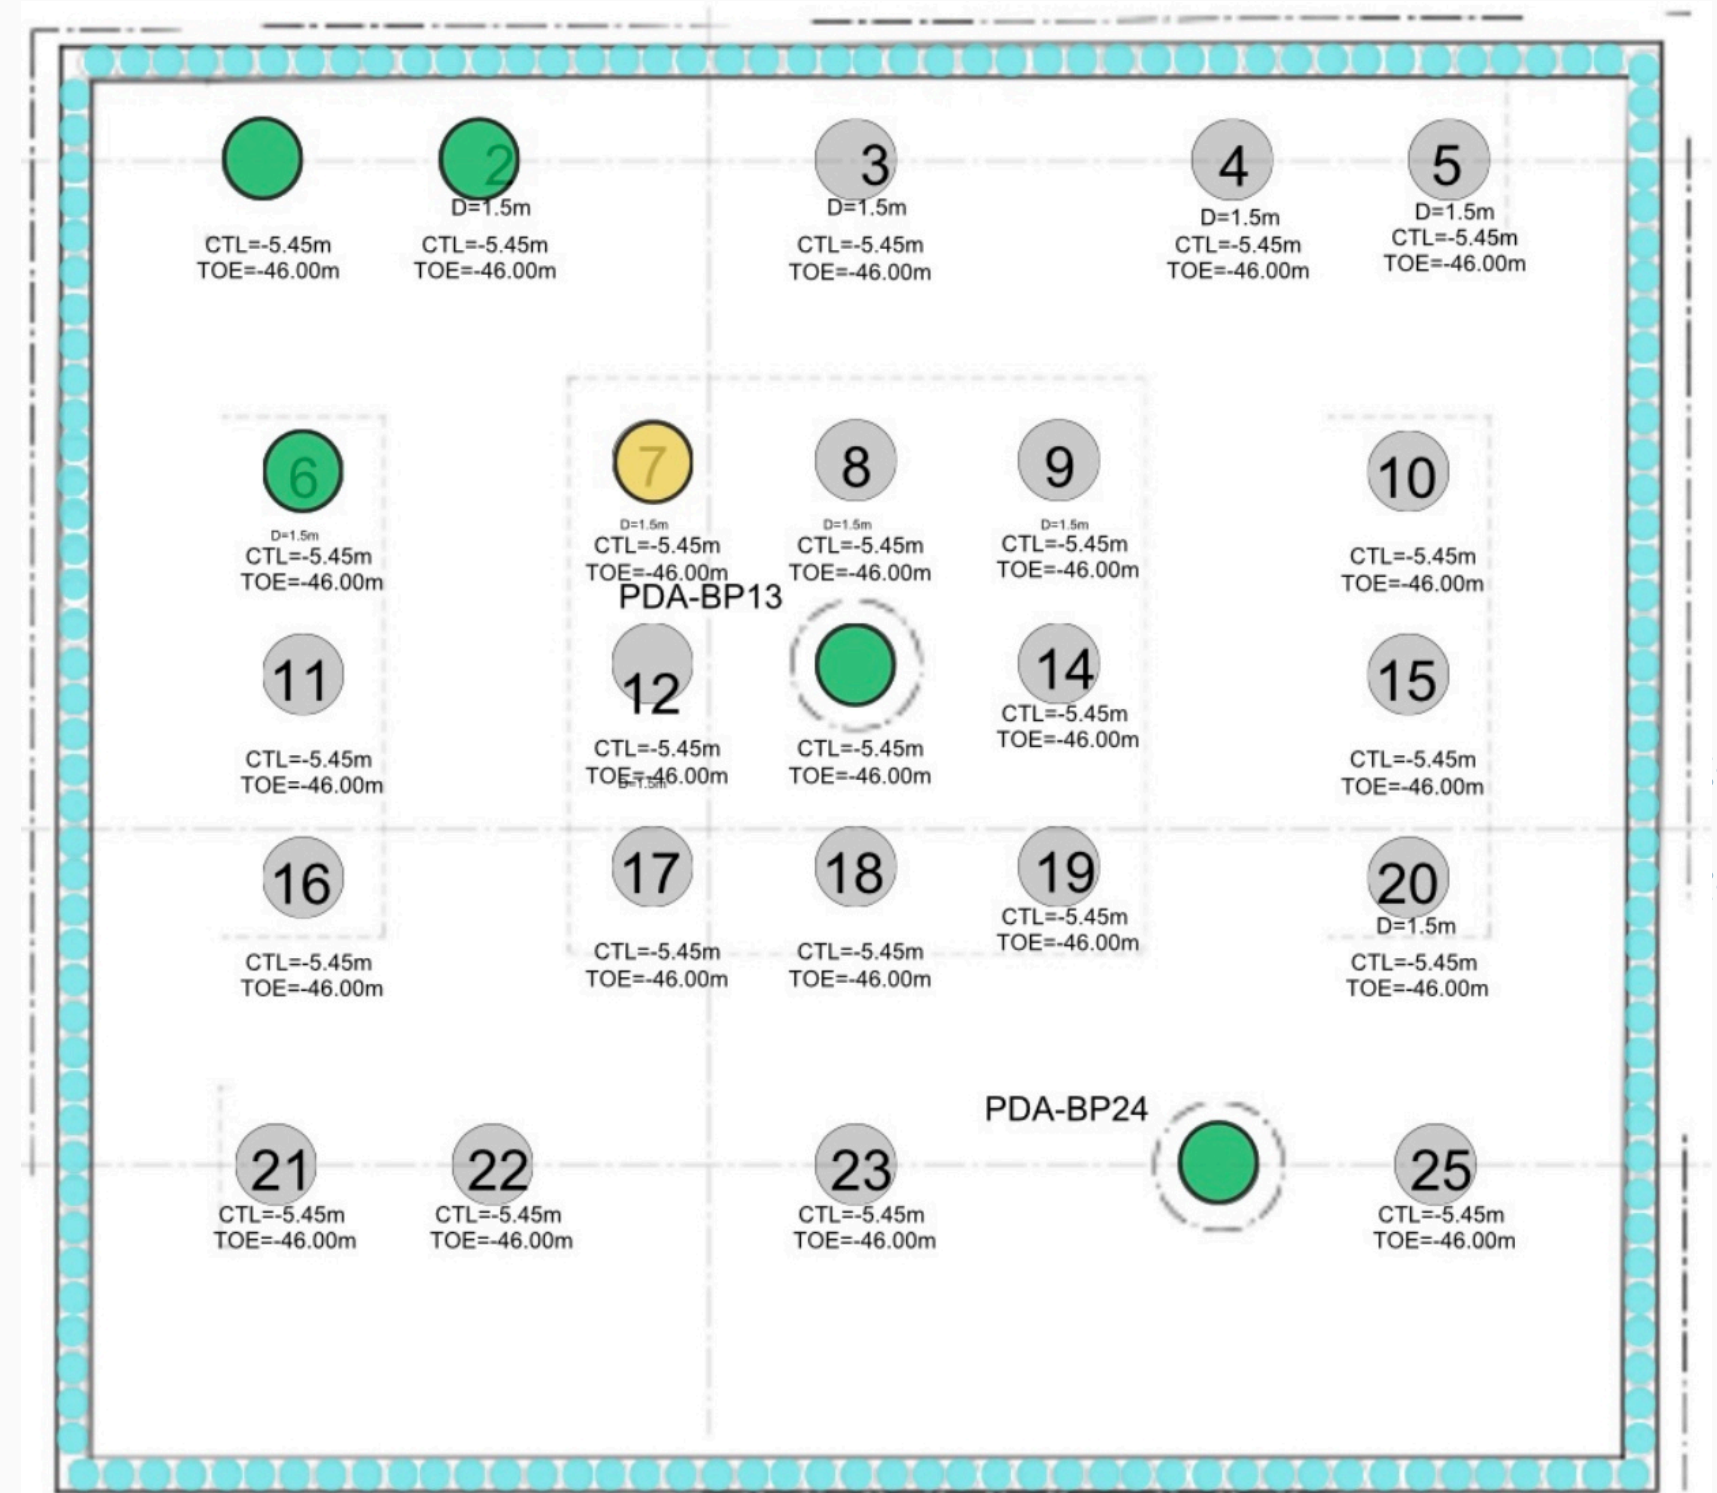





Time Square 11

PDA Test Progress

PDA PROGRESS (2/2 Piles)

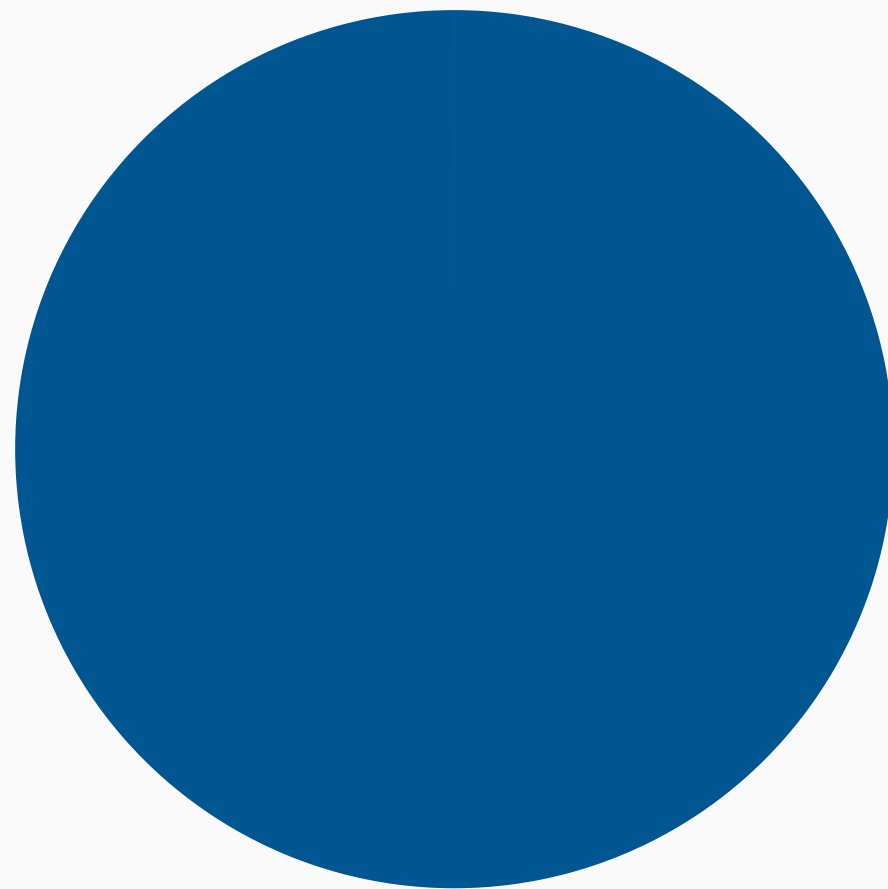

Done
100%

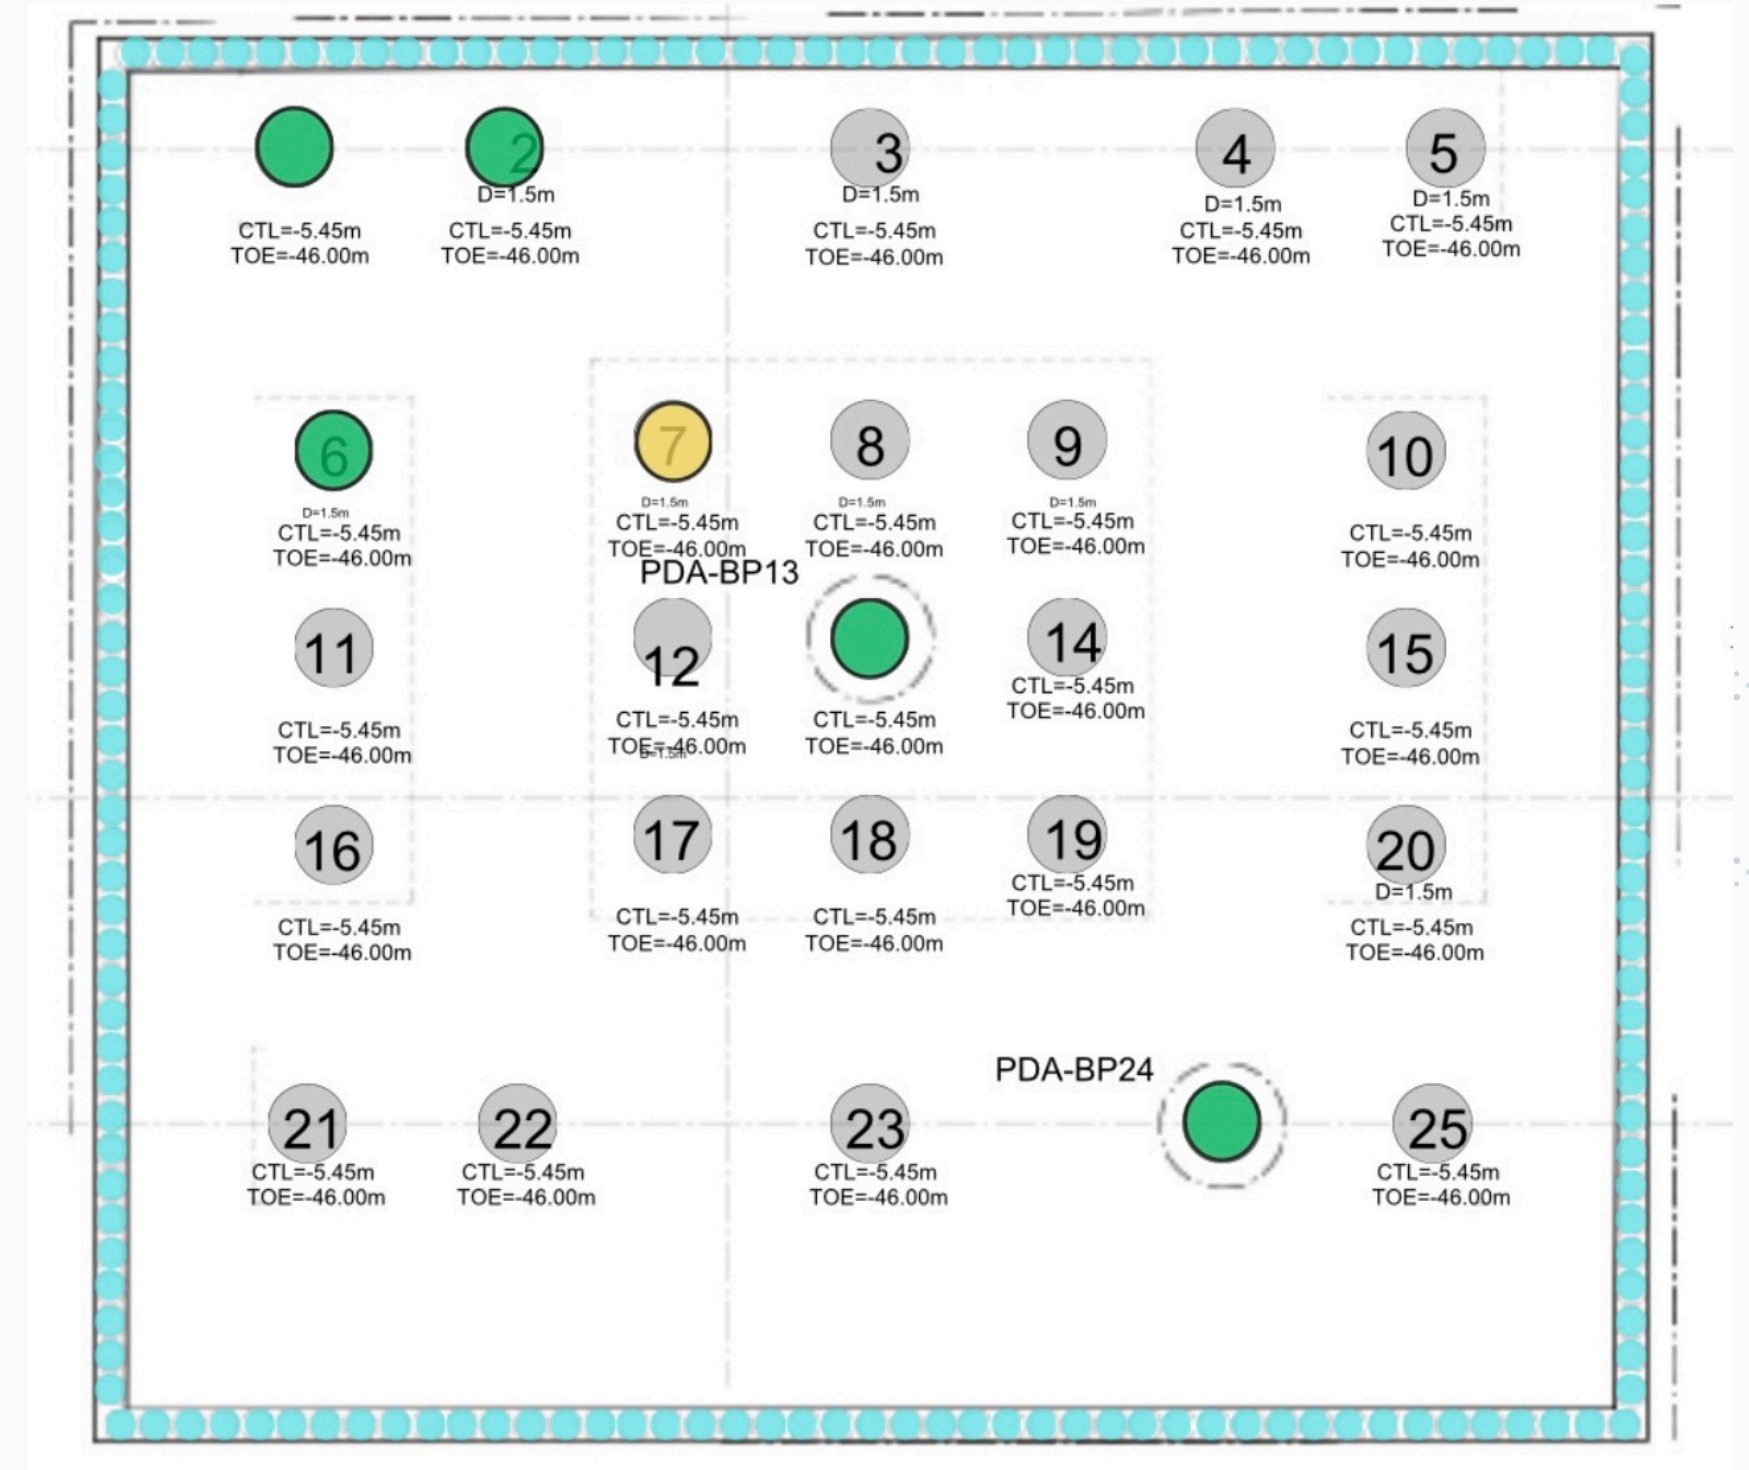




Time Square 11


Cross-hole Sonic Progress

Up to 29. AUG. 2026 (02/25 Piles)

Sonic Test PROGRESS

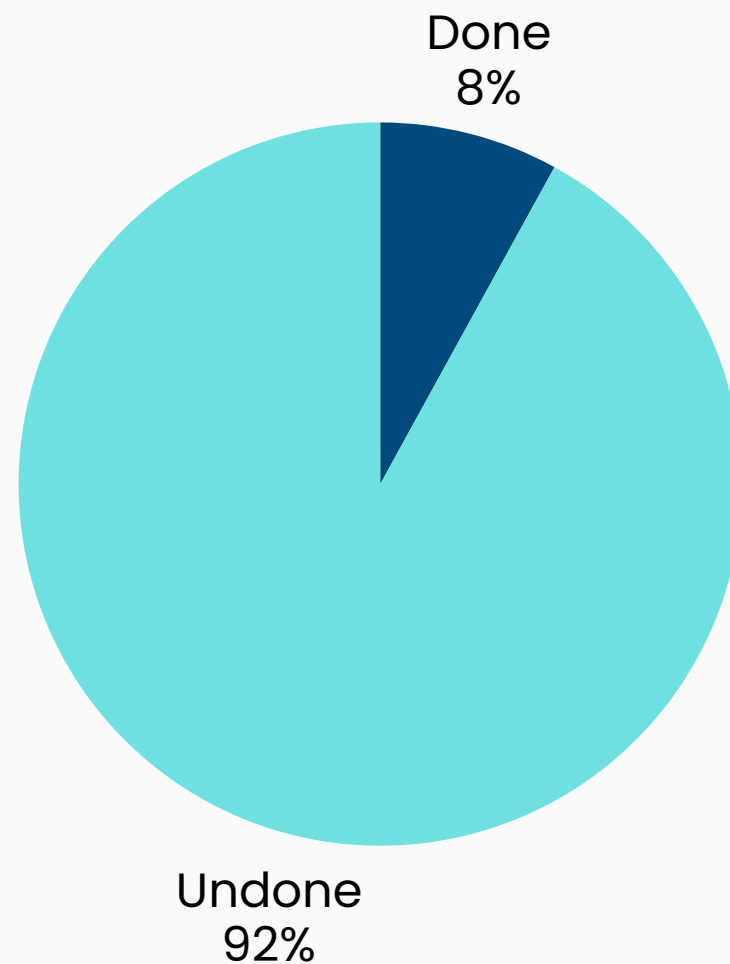

Finished Sonic testing.

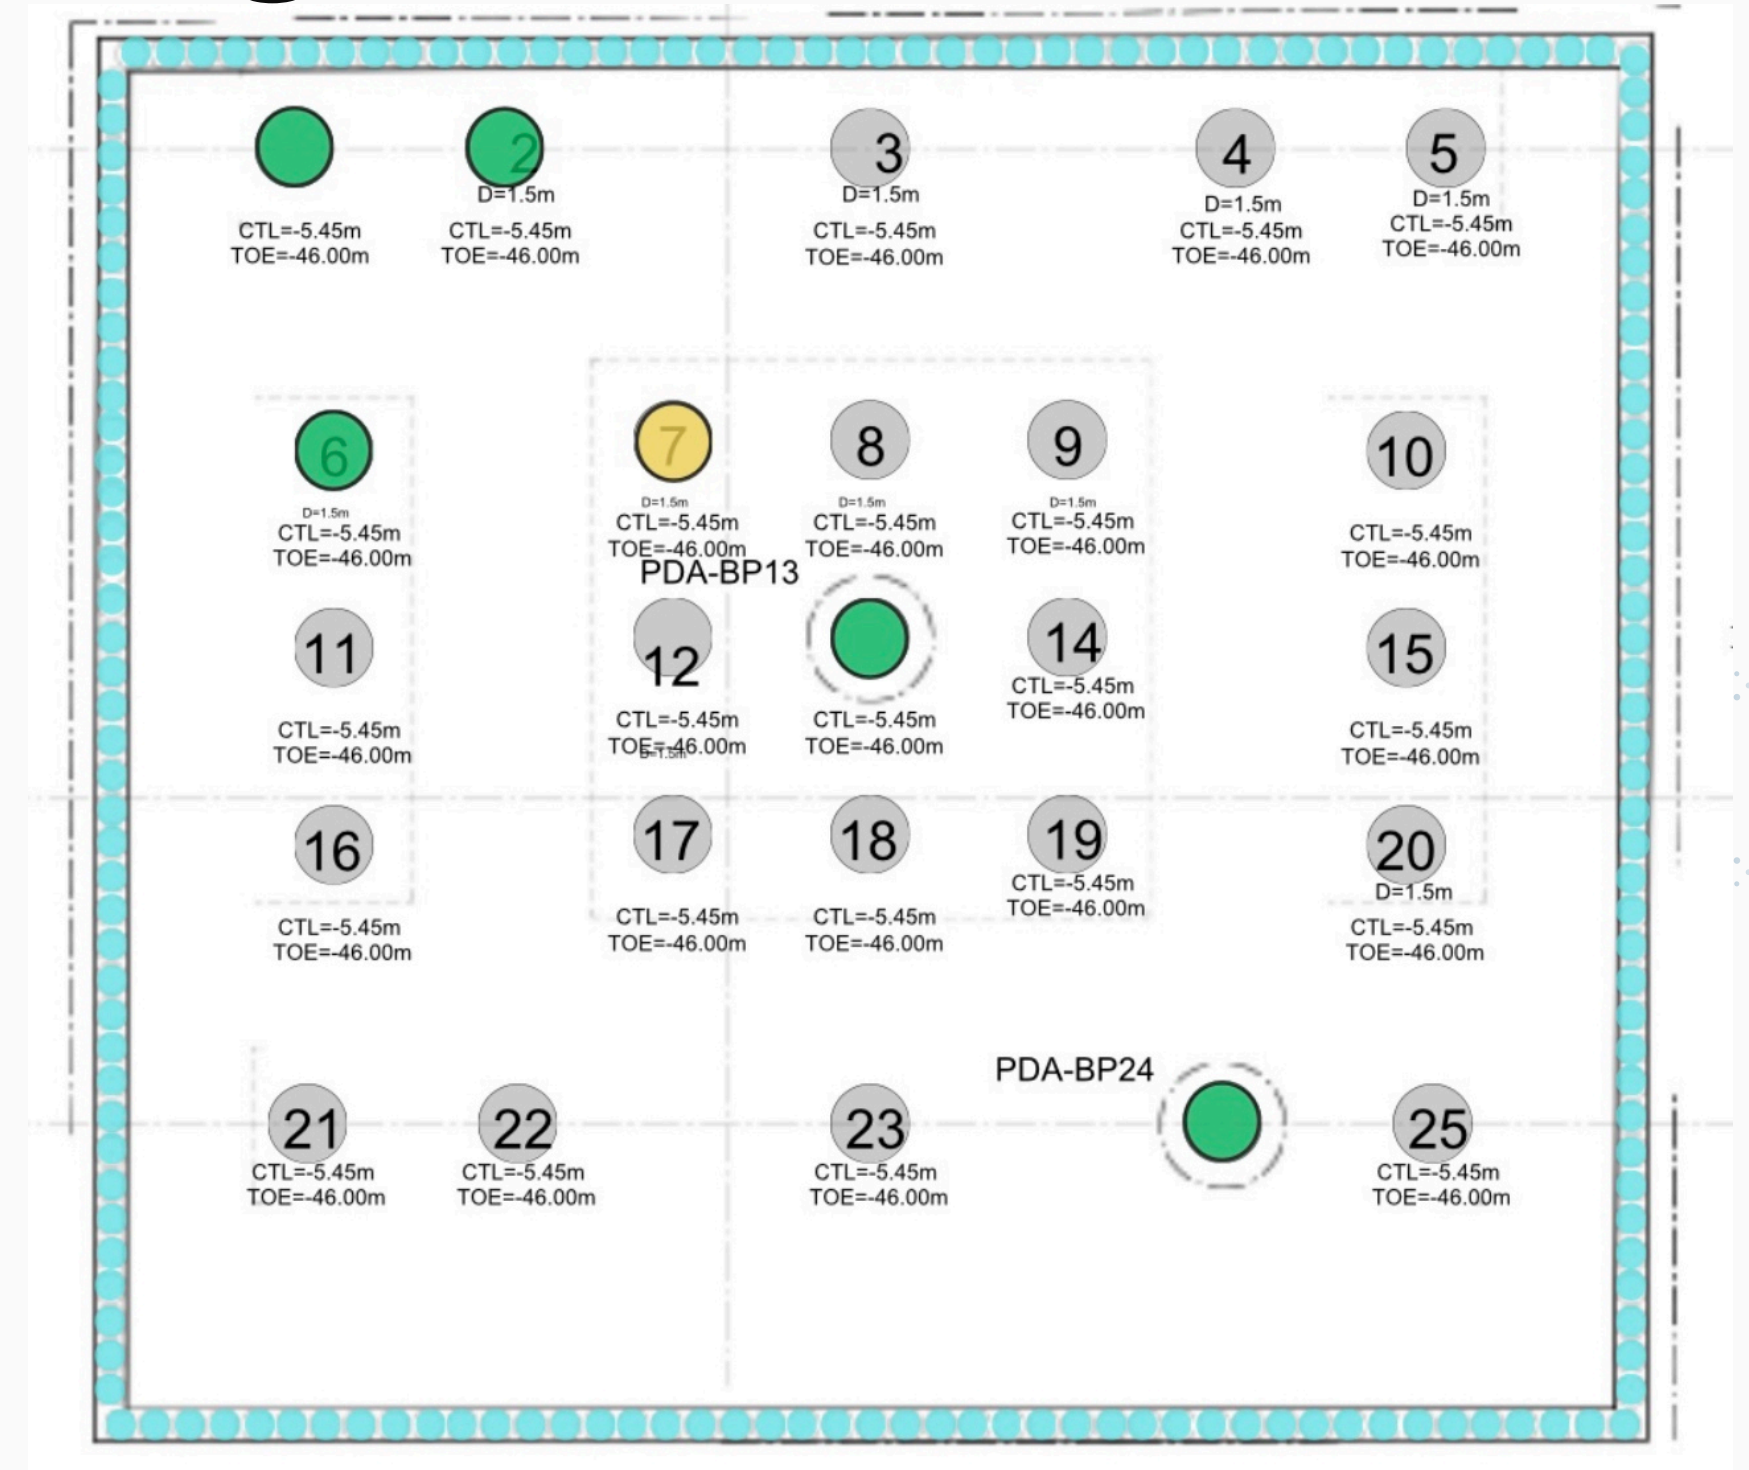




Time Square 11


Main Pile Progress

Up to 29. AUG. 2026 (05/25 Piles)

Main Pile PROGRESS

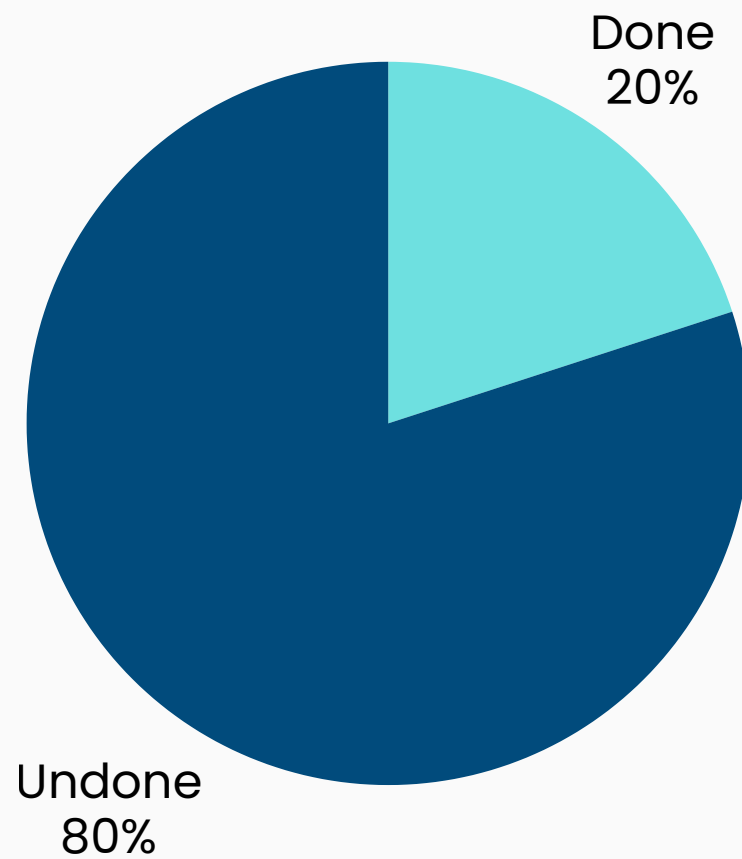


-  Finished Main Pile Concrete.
-  Unfinished Main Piles.

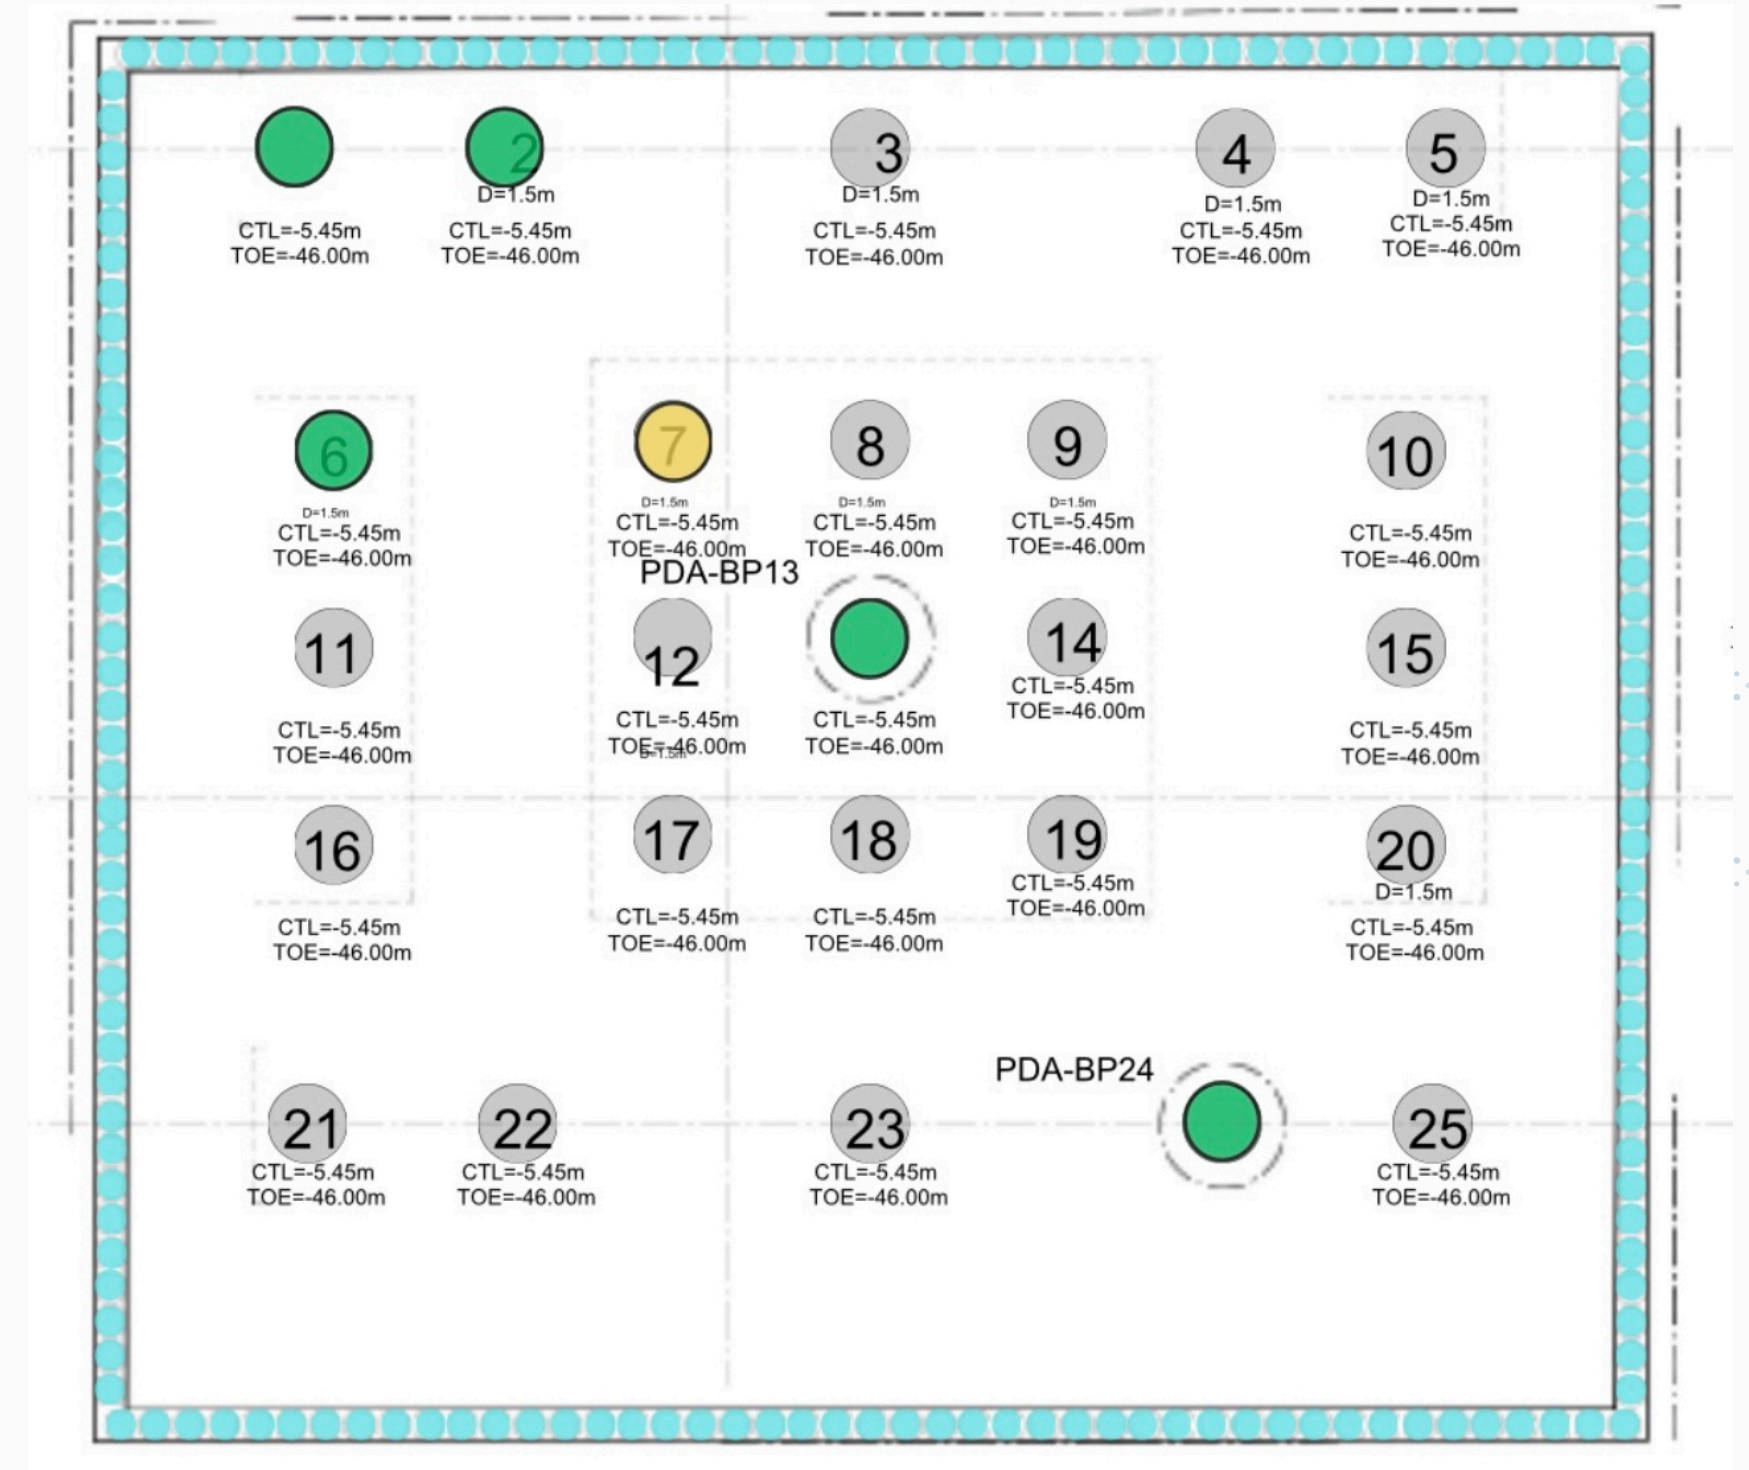



Time Square 11


Drilling Work

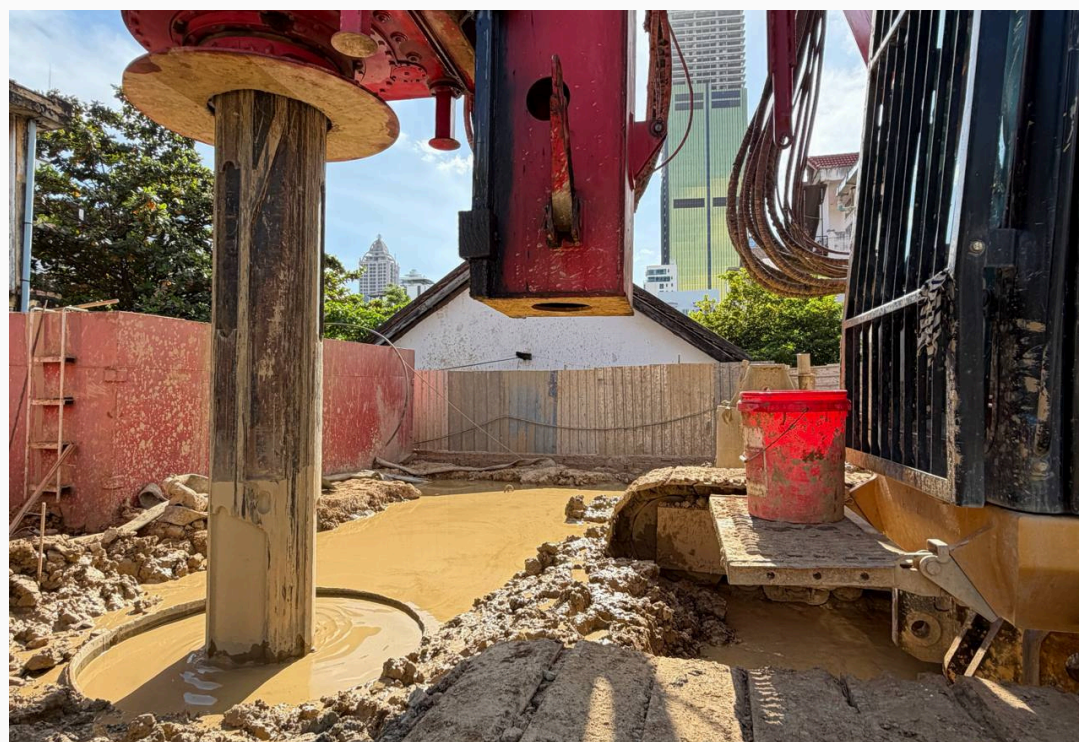



Time Square 11

Coordinate Inspection

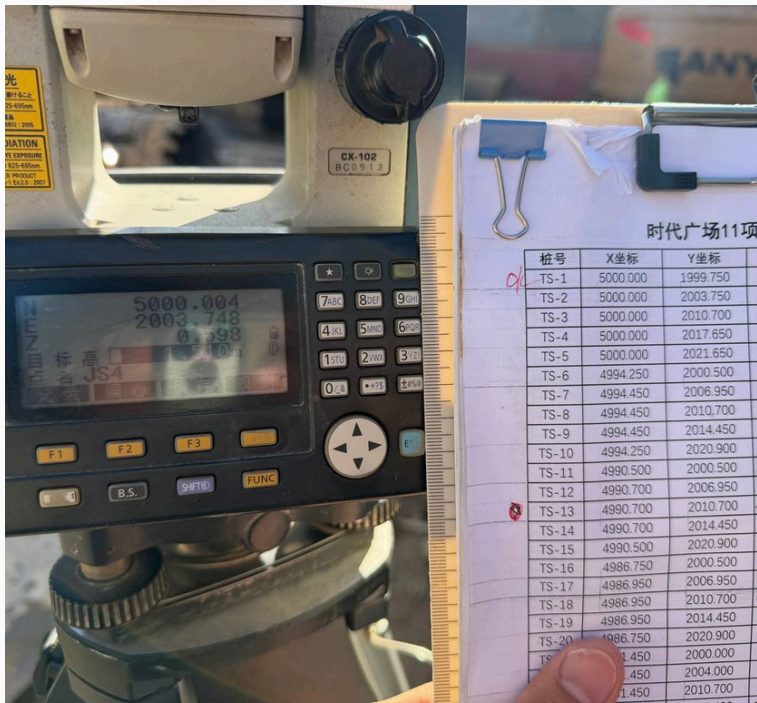


Pile ID: BP-02, BP-06, BP-07



Time Square 11


Bentonite Inspection

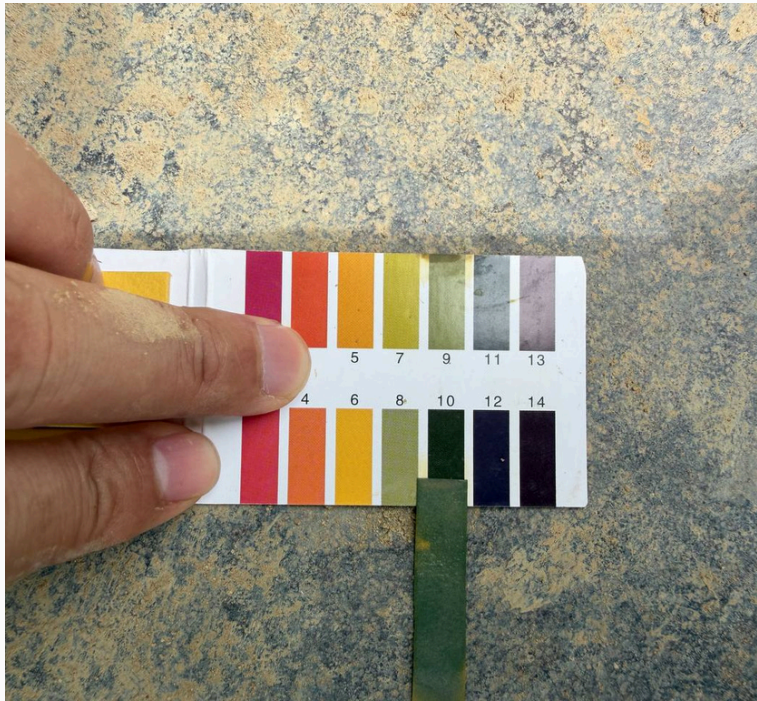



Time Square 11


Rebar Inspection

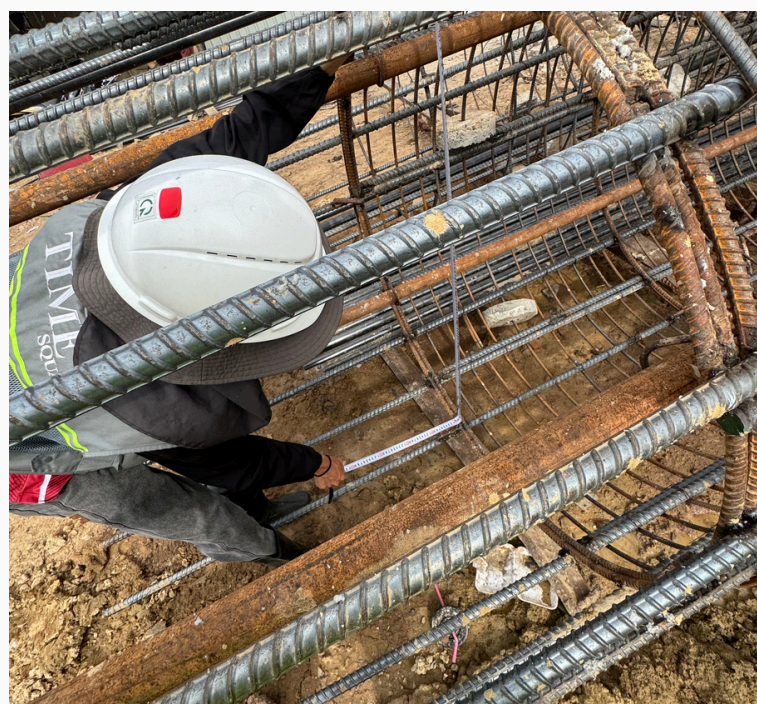



Time Square 11

Depth Inspection / Lowering Rebar

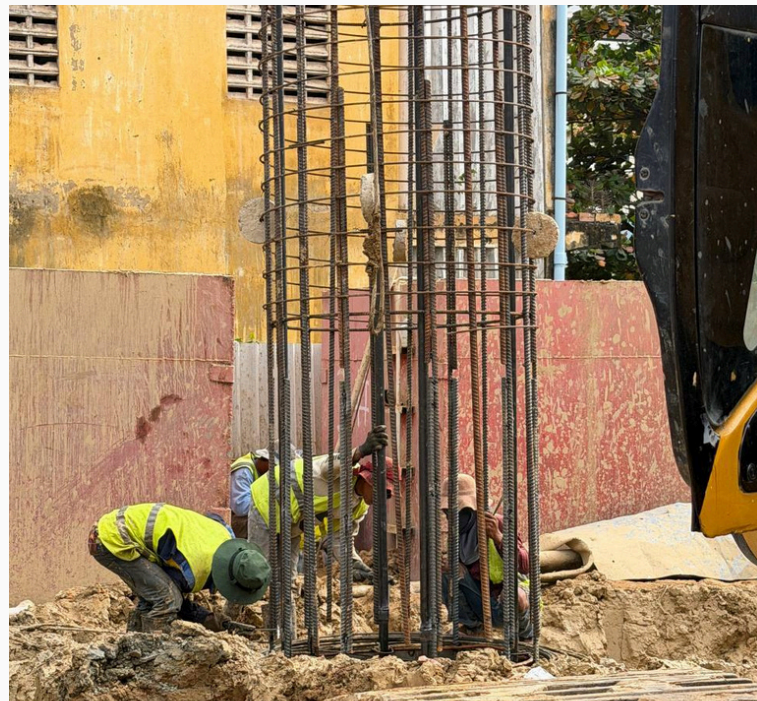



Time Square 11

Slump Inspection





Time Square 11

Rebar/ Sonic Delivery

Ship To : BKK3, St 133R (Da) Tel: 011 635 599 Project TS11 Cash to Bank		Invoiced / Invoice No : 08202605 YCG DN No : 082126-42M DN No : 082126-42M Terms : Due on receipt Invoiced : 08-08 Invoiced : 010 648 007					
No.	Item Description	Qty Ordered	Unit	Qty Delivered	WH	Qty Remain	WH Counter
1	DB 10mm, HP-SD390 7.4kg	354		354	A.7M-Mok	0	
2	DB 16mm, HP-SD390 18.9kg	48		48	A.7M-Mok	0	
3	DB 25mm, HP-SD390 46.7kg	191		191	A.7M-Mok	0	

Message:

4. All items are not the company's property until the amount is fully paid.
5. All items are not the company's property until the amount is fully paid.
6. All items are not the company's property until the amount is fully paid.
7. All items are not the company's property until the amount is fully paid.
8. All items are not the company's property until the amount is fully paid.
9. All items are not the company's property until the amount is fully paid.
10. All items are not the company's property until the amount is fully paid.
11. All items are not the company's property until the amount is fully paid.
12. All items are not the company's property until the amount is fully paid.
13. All items are not the company's property until the amount is fully paid.
14. All items are not the company's property until the amount is fully paid.
15. All items are not the company's property until the amount is fully paid.

3.70

Customer: Name: Ramook
Delivered by: Name: Ramook
WH Controller: Name: Ramook
Delivery Prepare by: Name: Ramook
Accountant: Name: Thov

No.	Description	Quantity	Unit Price	Amount
1	DB 10mm, HP-SD390 7.4kg	354	2.90	809.94
2	DB 16mm, HP-SD390 18.9kg	48	2.10	100.80
3	DB 25mm, HP-SD390 46.7kg	191	4.24	810.96

PAID

NOT FOR DECLARATION

* All items are not the company's property until the amount is fully paid.

Total: 1721.70

Deposit: 0.00

Rest: 1721.70





Time Square 11

Site Cleaning





Time Square 11

Passion For Progress!

Thank You!

