


# Time Square 11 Weekly Report

09. July. 2026



## Location of Time Square 11

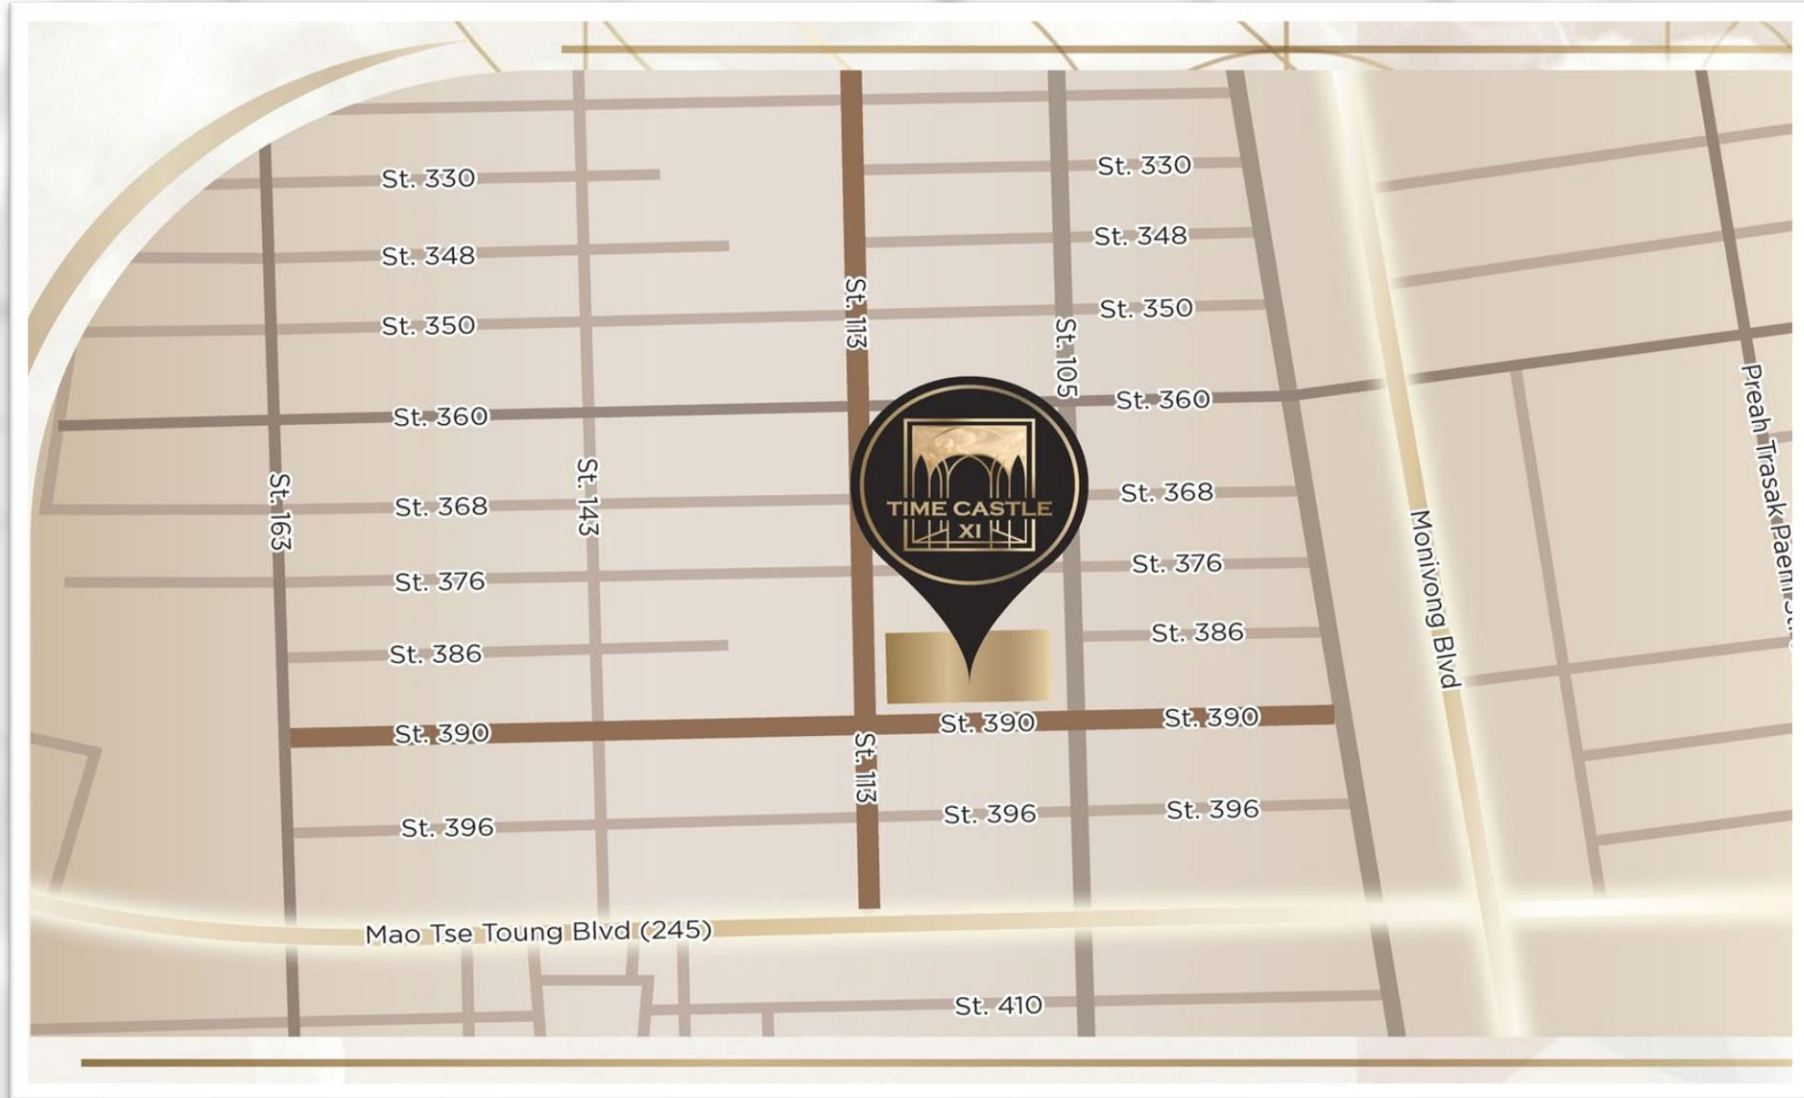




## Time Square 11 Point of View





## Time Square 11 Point of View





## Time Square 11 Point of View



# Ground Breaking Ceremony


## Time Square 11



# CBP Pile progress up to 09. July. 2026

29p/168 pile


## CBP Progress

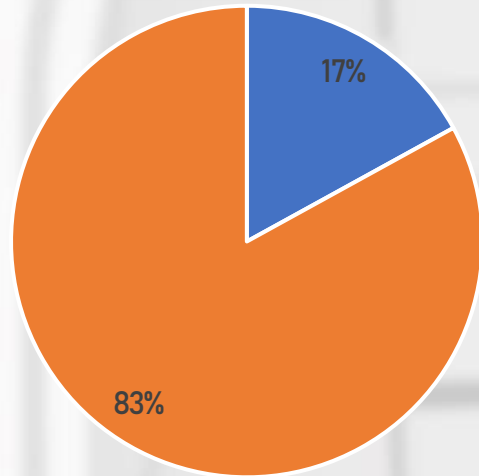

■ Done ■ Undone




CBP finished concrete work.

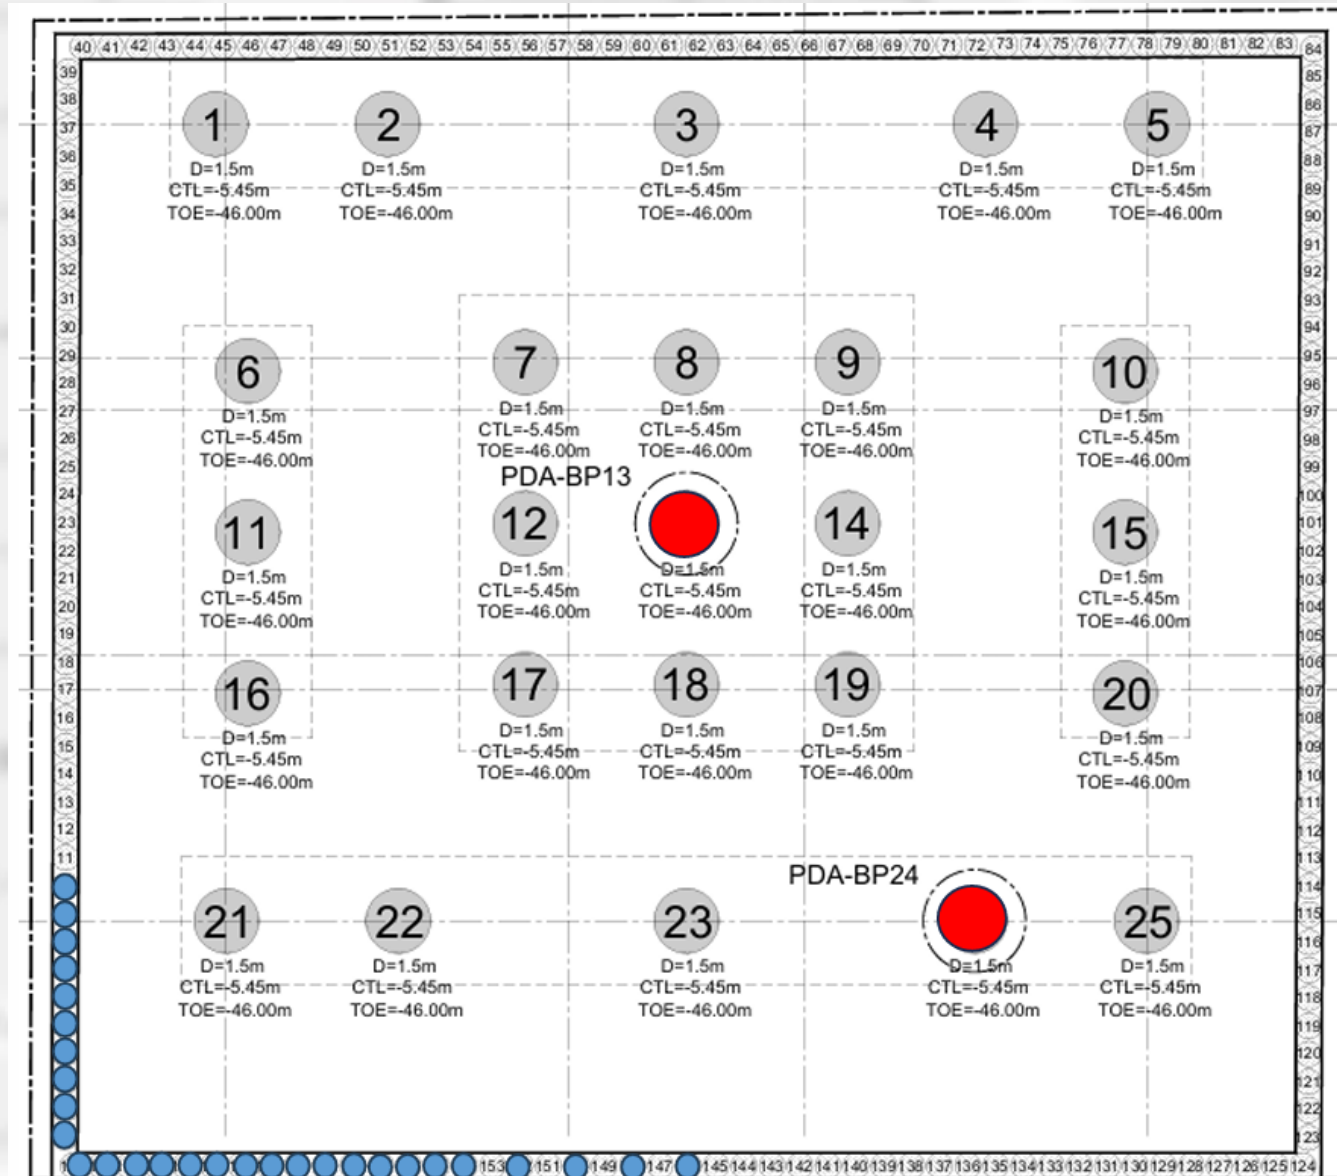

# Main Pile progress up to 09. July. 2026


## 2p/25 pile

### Main Pile Progress

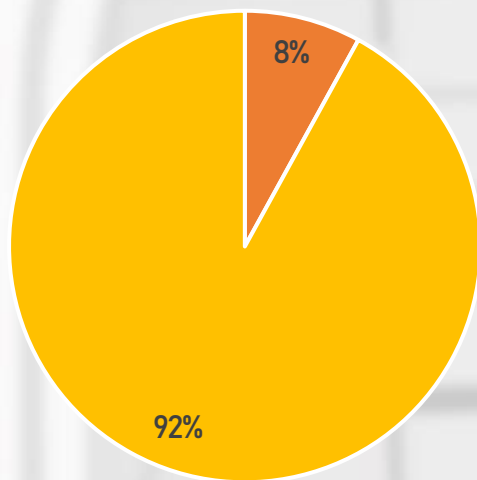

Done Undone


 Pile casted concrete.

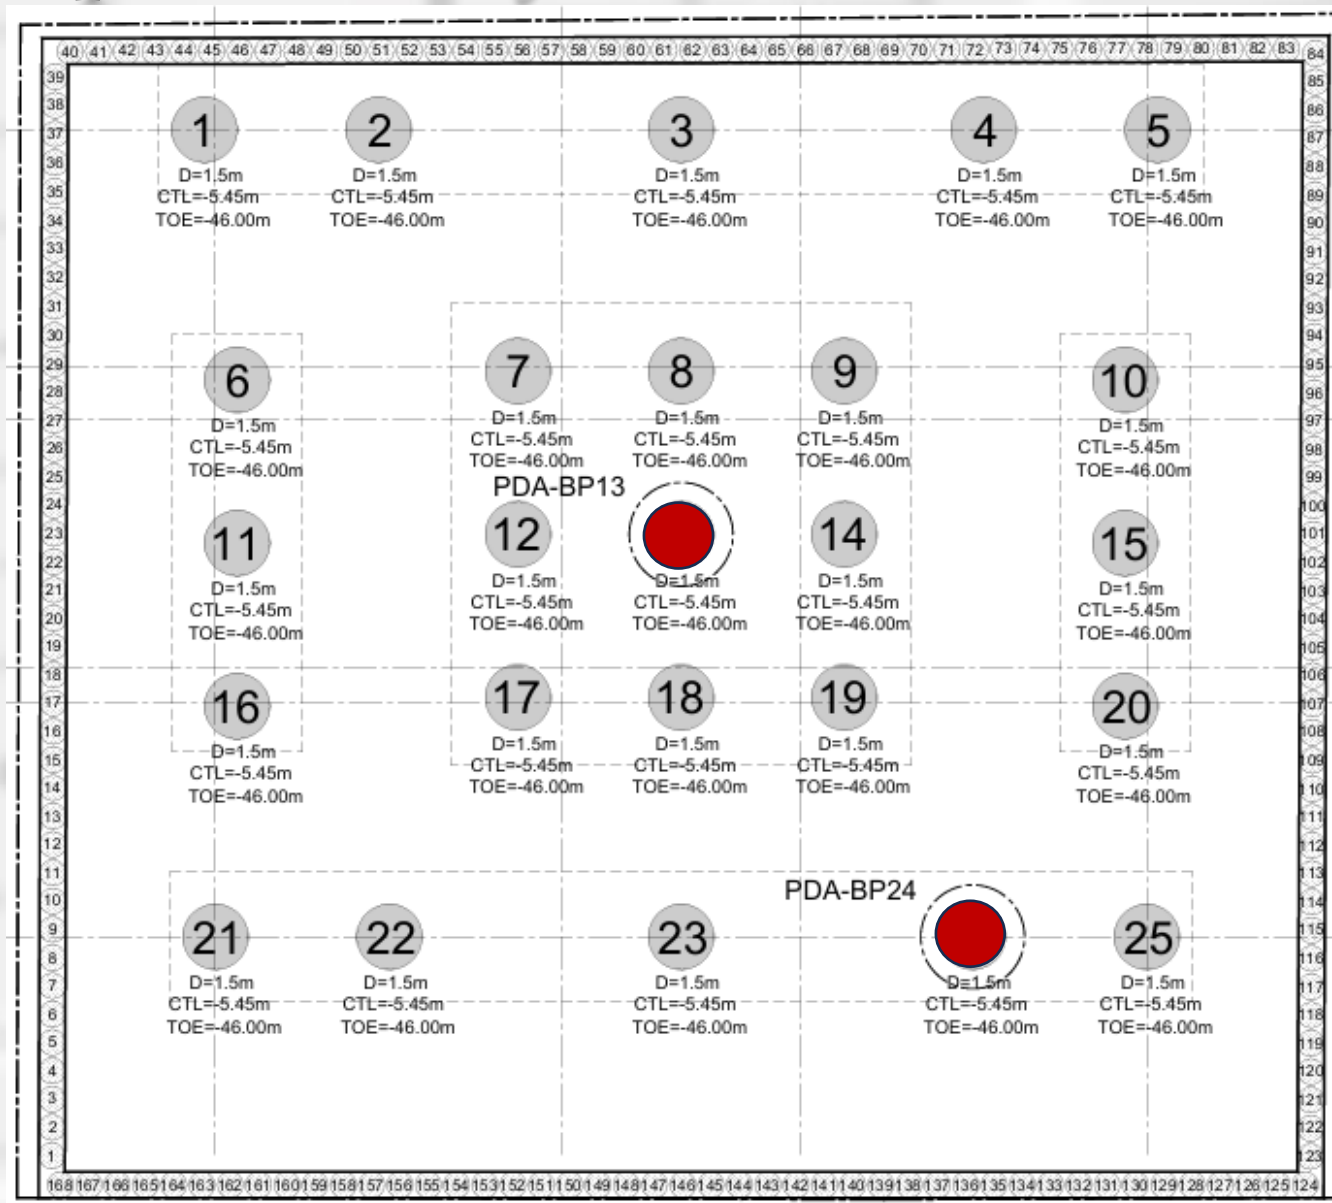

# Sonic progress up to 09. July. 2026


2p/25 pile

Main Pile Progress

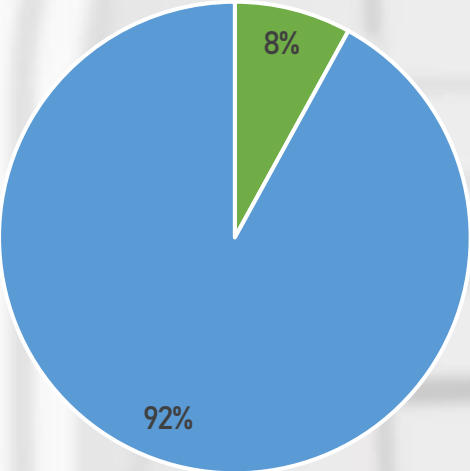


■ Done ■ Undone

● Sonic tested piles.

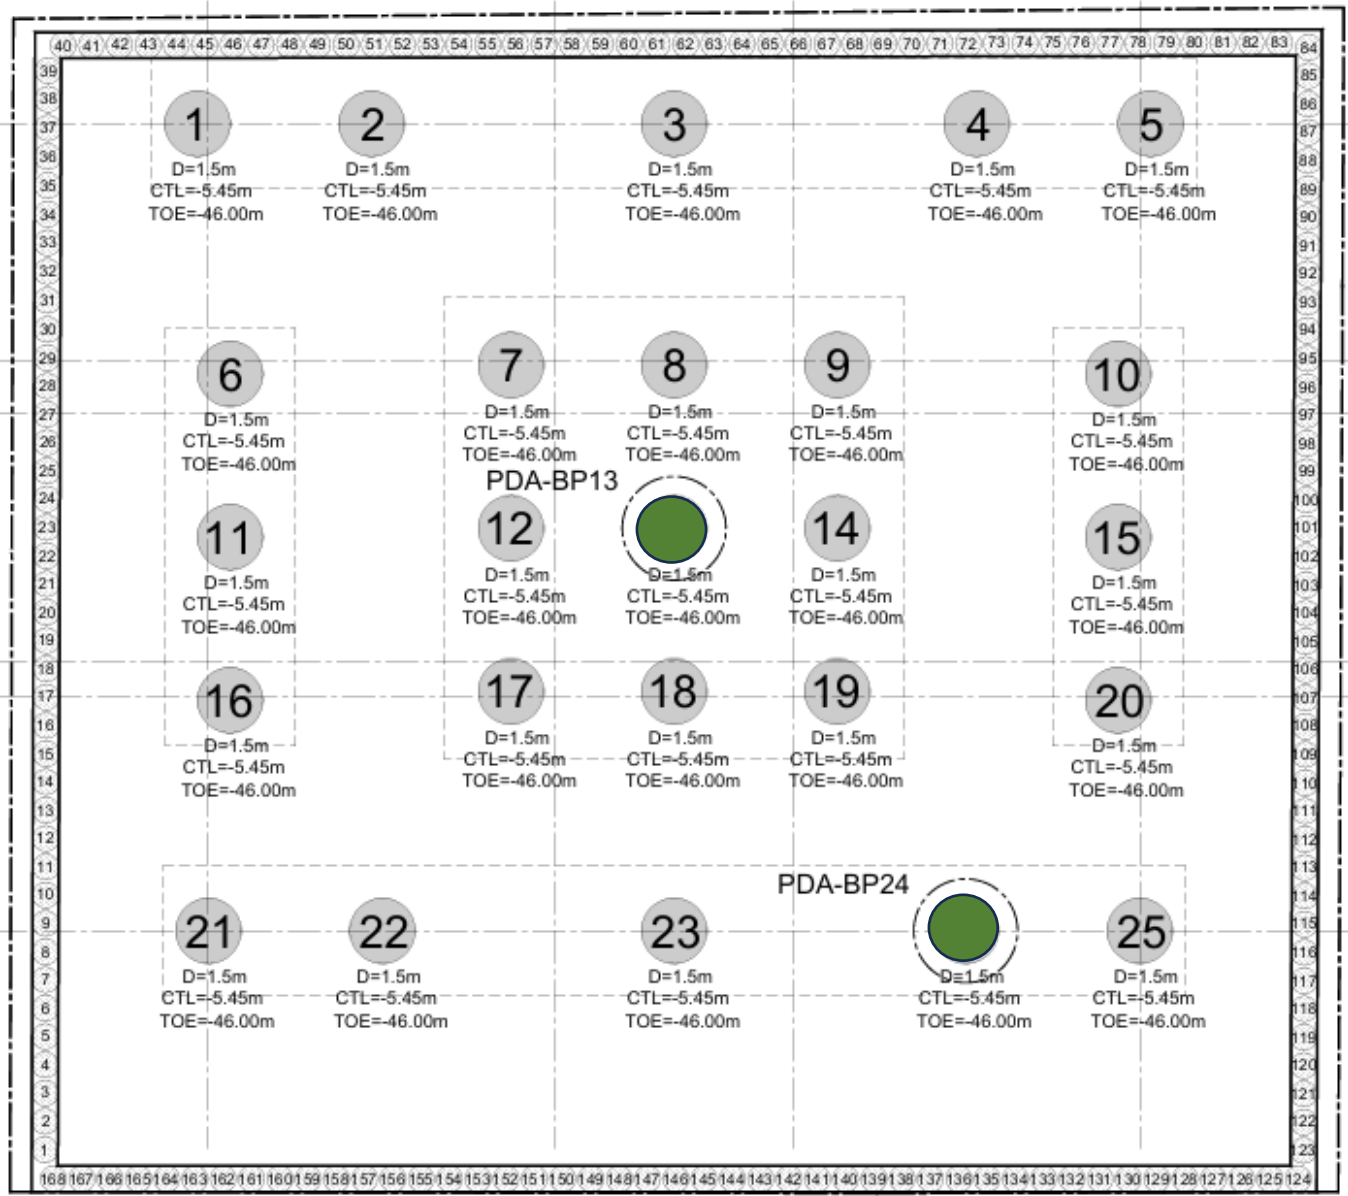

# Sonic Testing on 2 PDA Piles

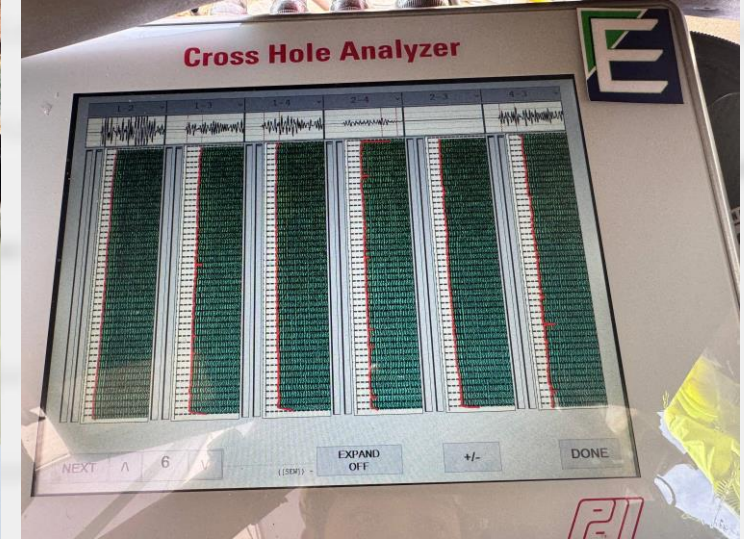


# Coordinate Inspection



# CBP Rebar Inspection



# Depth Inspection & Lowering CBP Rebar

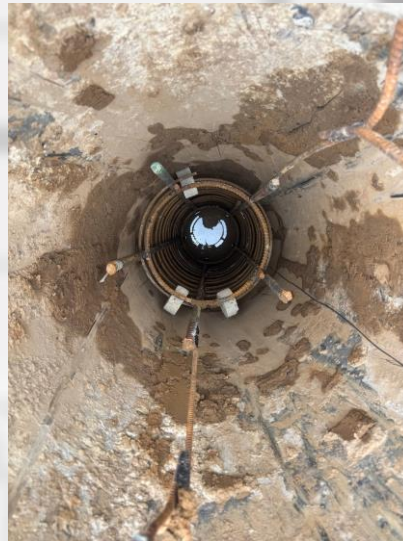


# Concrete Casting: CBP Pile



# CBP Rebar Delivery

[illegible]

# Site Cleaning

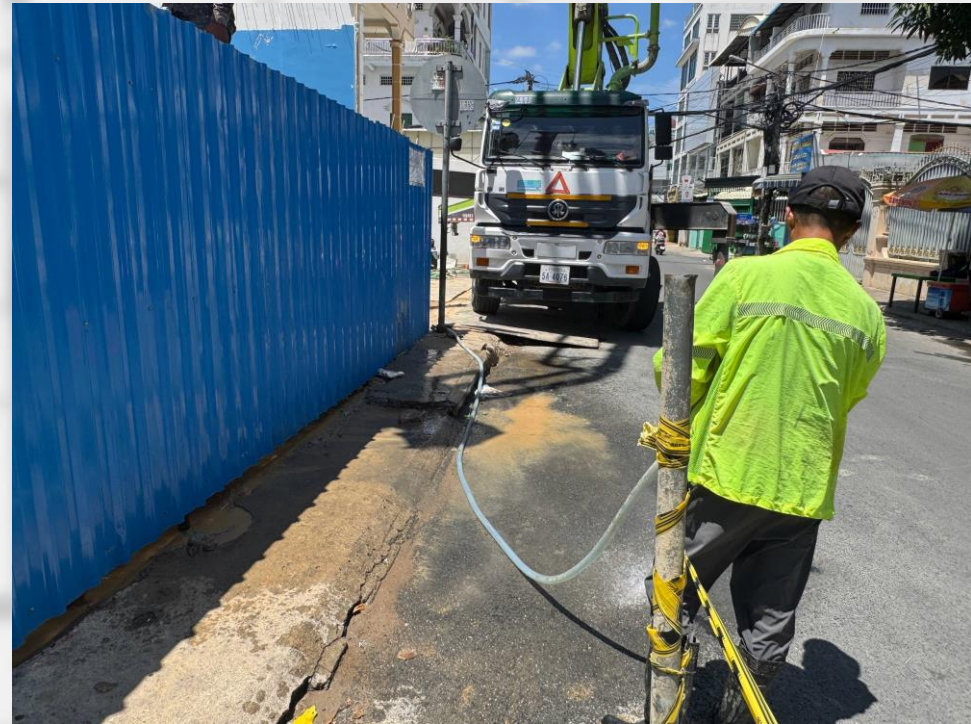

Passion For Progress!



Thank You!

# TIME SQUARE 11

Boeng Keng Kang 3, Phnom Penh



St. 113

