

TIME SQUARE 410 (8)

# MONTHLY REPORT

29.September.2025





# LOCATION OF CONSTRUCTION SITE



# PROGRESS PLAN OF PILE WORK


- Estimated to be completed on the 25<sup>th</sup> October 2025

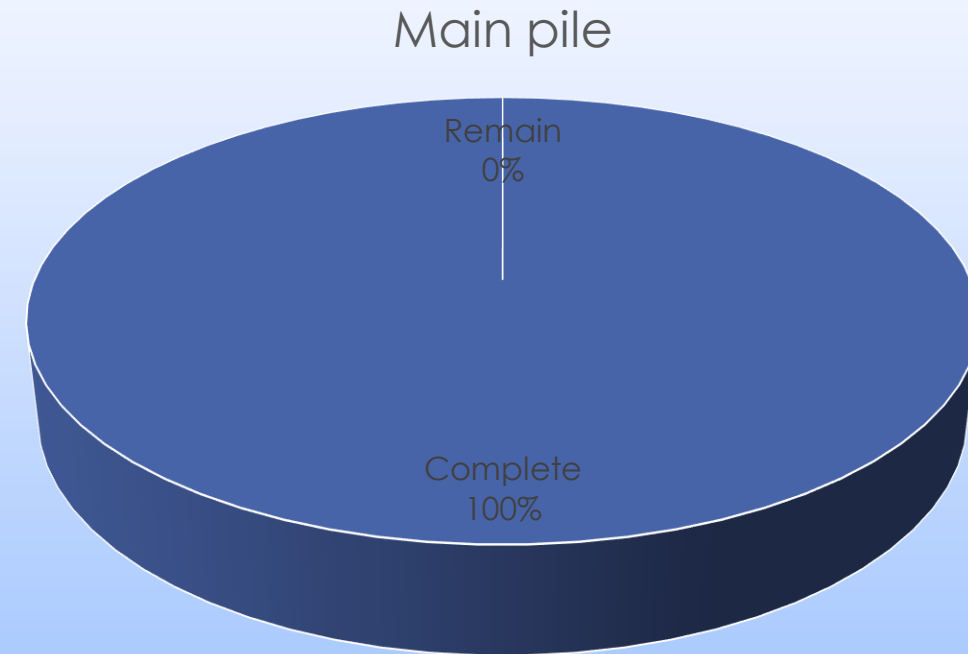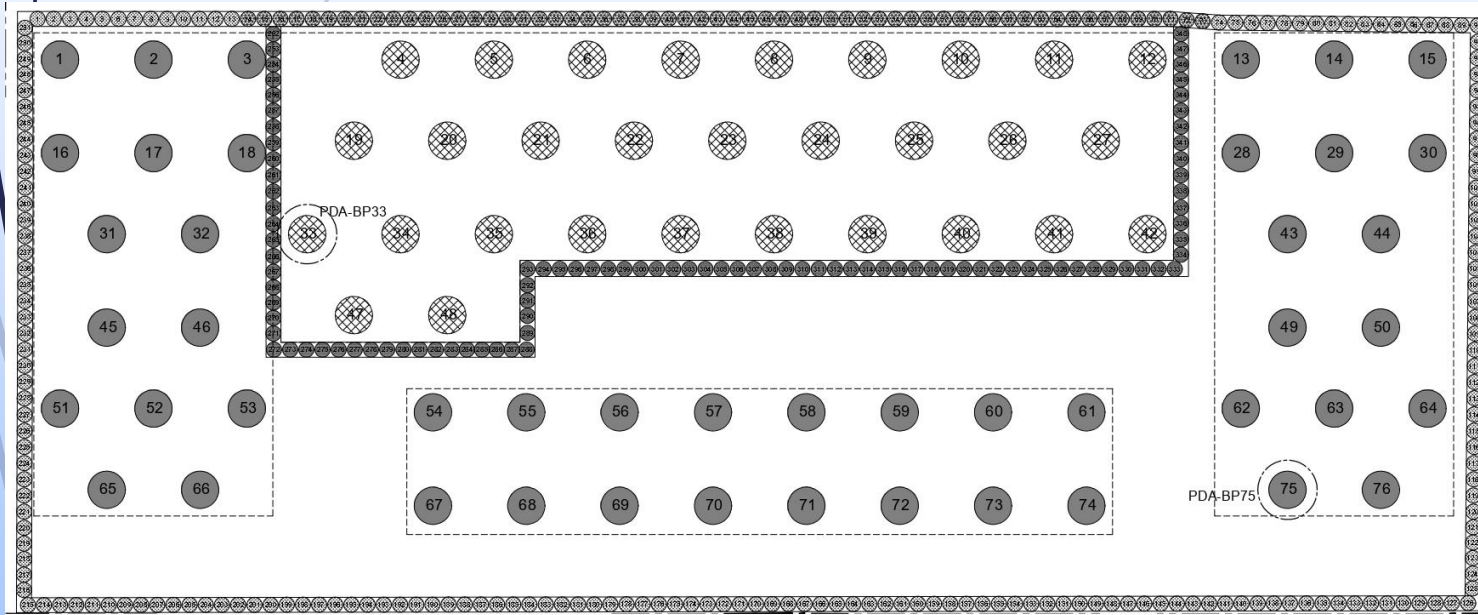

■ Complete ■ Remain

# PILE PROGRESS UP TO 29.September.2025


## Completed 39/76 Piles

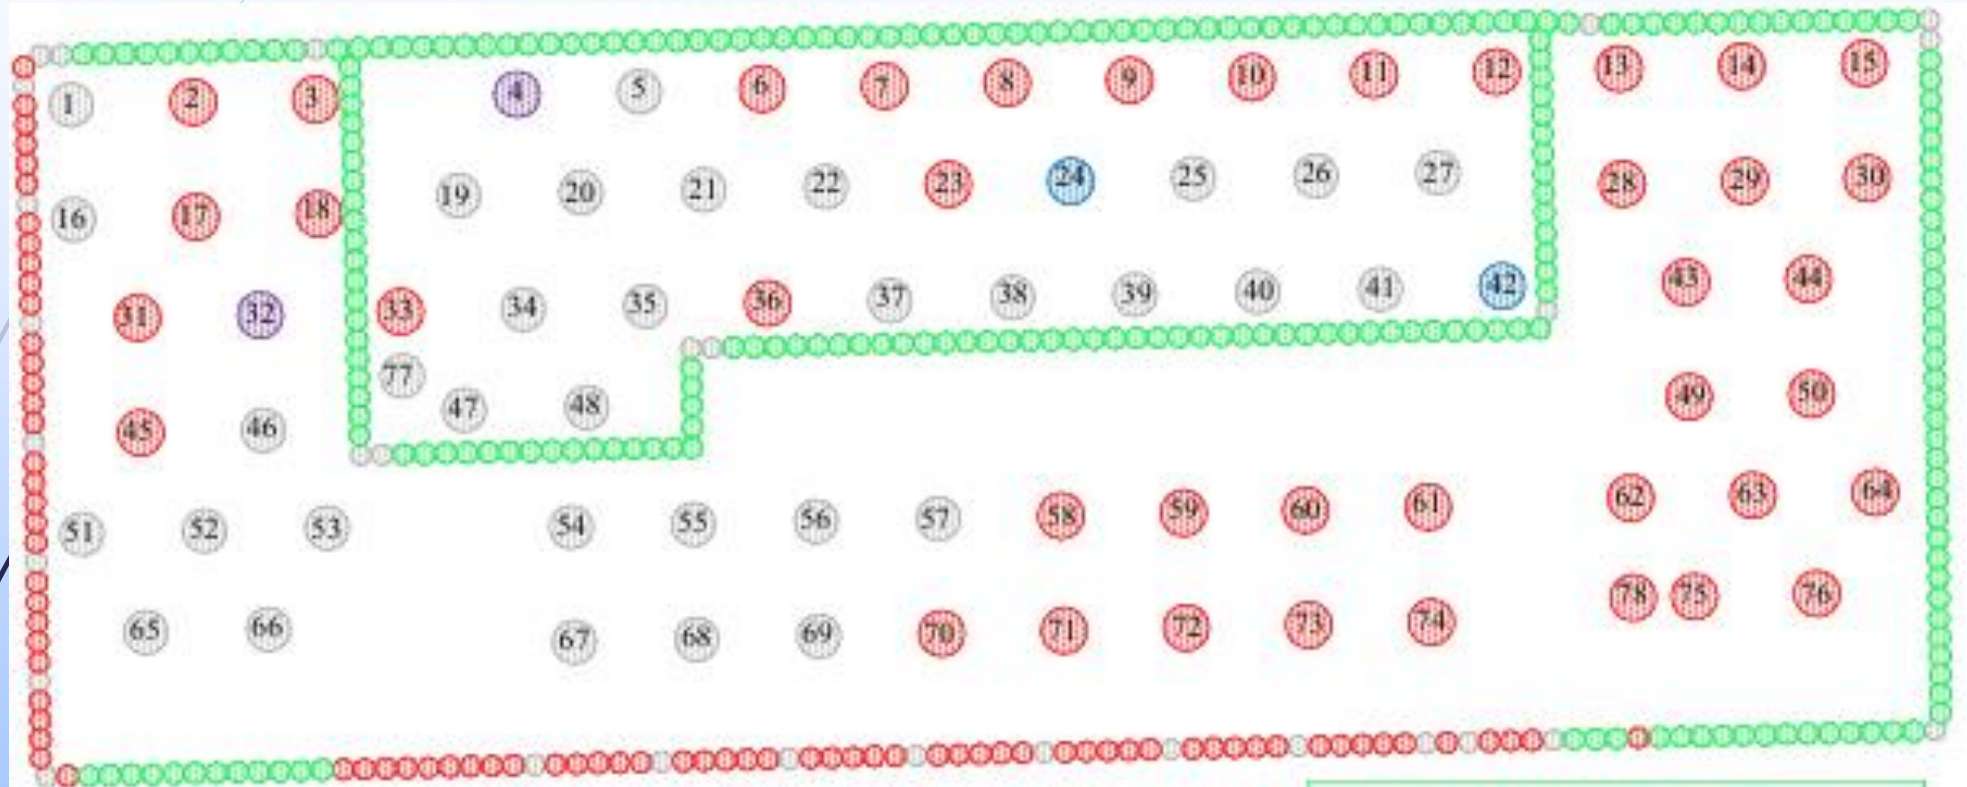

# PILE PROGRESS UP TO 29.September.2025

## Completed 39/76 Piles


Main Pile

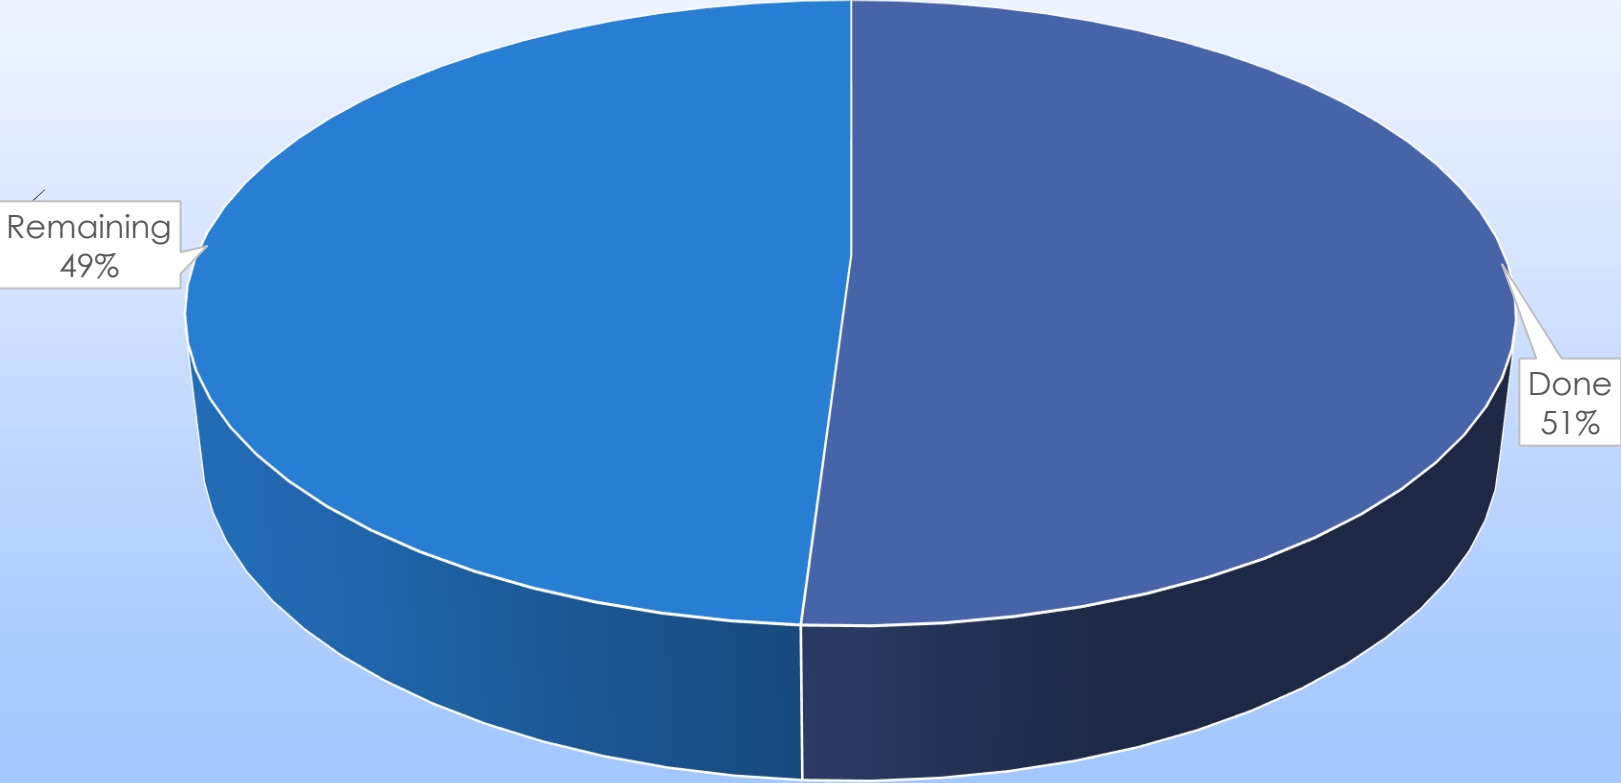

■ Done ■ Remaining


# CBP PROGRESS UP TO 29.September.2025

Completed 328p/328p (Done)

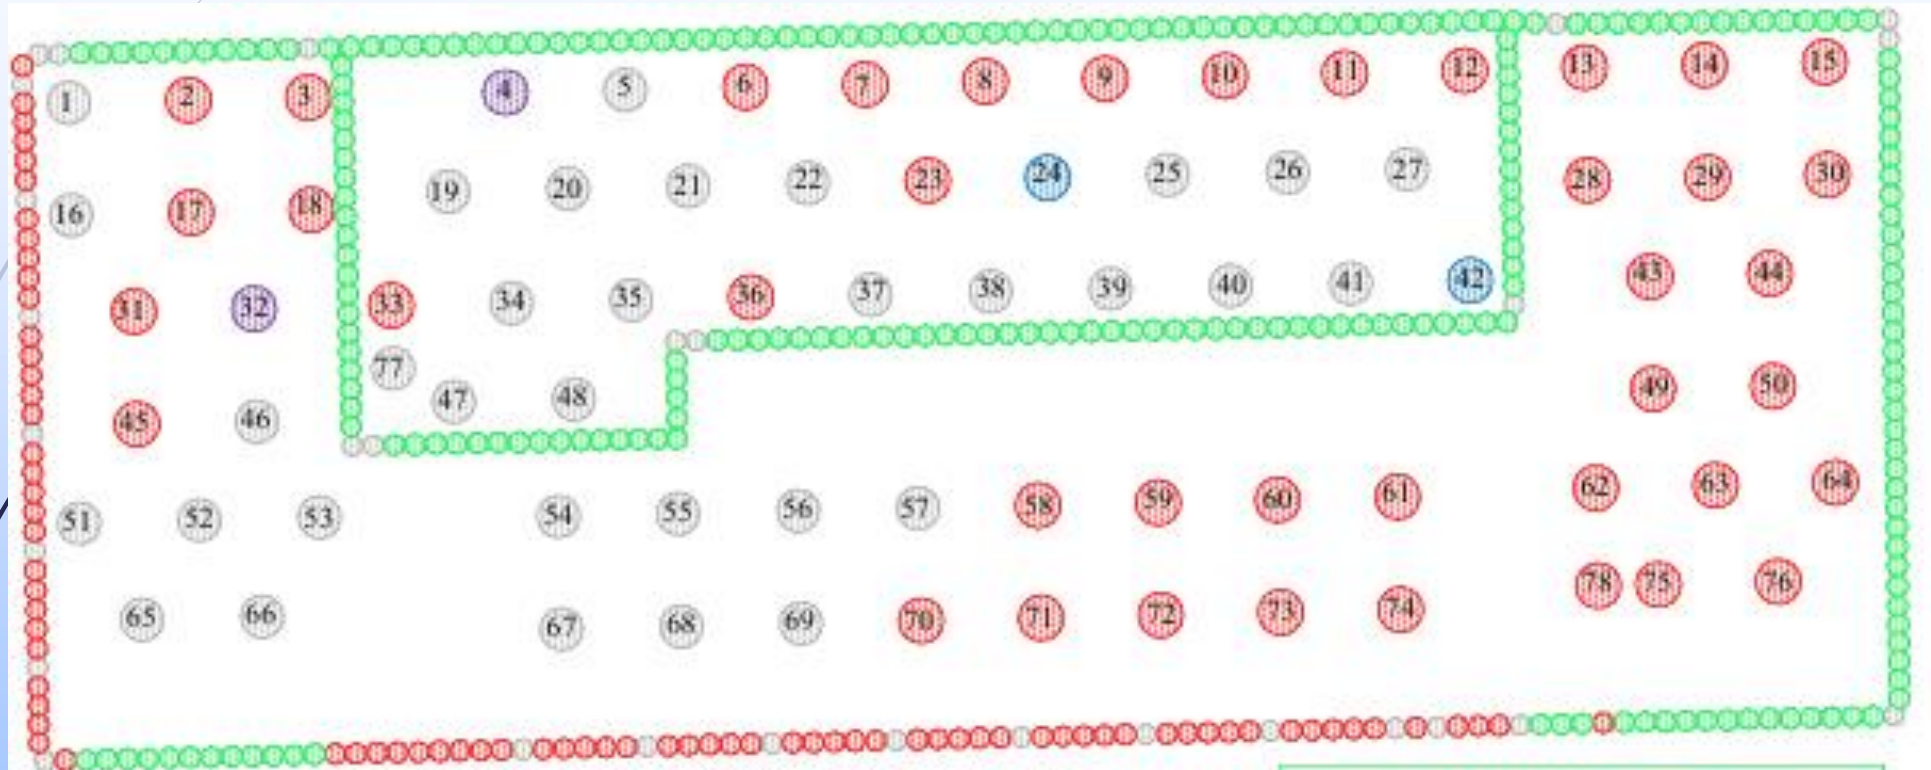

# CBP PROGRESS UP TO 29.Septemeber.2025

## Completed 328p/328p (Done)

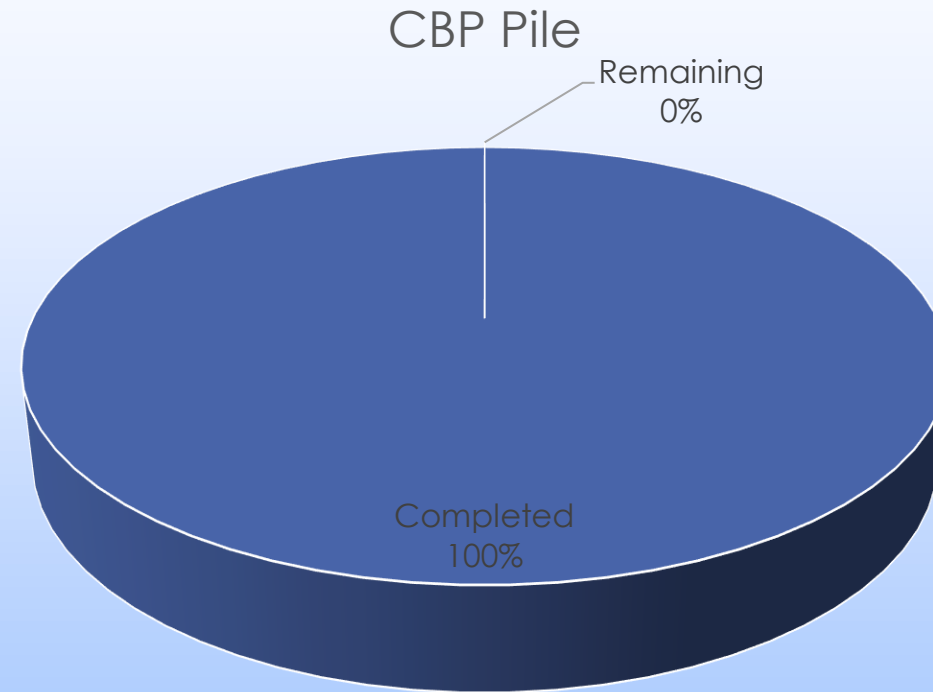

■ Completed ■ Remaining

# PILE SETTING OUT WORK




# DRILLING WORK





# BENTONITE SLURRY INSPECTION

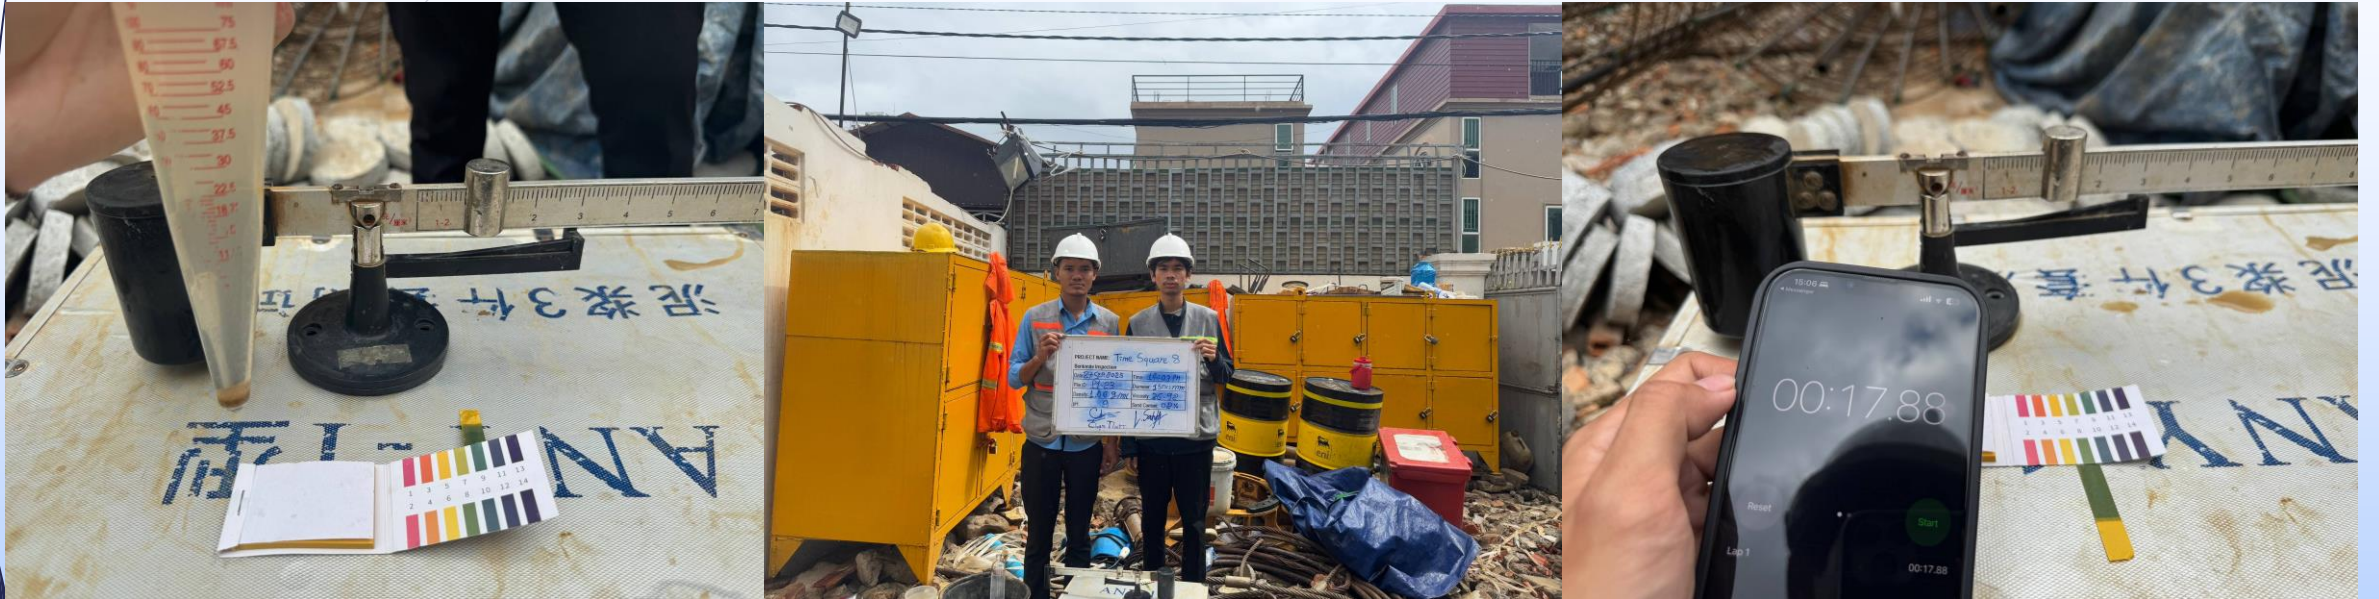

Bentonite inspection: Before drilling, before casting concrete.

# CASTING CONCRETE



# HSE INSPECTION



Toolbox meeting: Checking up on safety environment, PPE and front site cleaning .

# TOP VIEW





# Time Square 8

The Fastest Selling Project

*in Phnom Penh*



# PASSION FOR PROGRESS!

## Building Level

50F

High Ground

49F

- Tennis Court
- Sky Gym
- Sky Boxing
- Sky Yoga

48F

- 40M Infinity Skypool
- Sky Terrace
- Sky Patio
- Amphitheater
- Play Space

39F

- Art Gallery
- Floating Bar
- Meeting Room
- Co Creation Space
- Art Library
- Sky Cinema
- Sky Entertainment

GF

Lobby, Balcony Cafe

40-47F

Duplex Floor

8-38F

Classic Floor

2-7F

Carparking

B1-B2F

Carpark

# THANK YOU!
