



Report of

Time Square 8

**St. 410, Boeung Trabek,
Chamkarmon, Phnom Penh**

9th August 2026

SITE LOCATION



Koh Norea City

Mao Tse Tong BLVD


St 410



SUB-STRUCTURE WORK PROGRESS


I. Excavation Work

Overall Excavation Progress

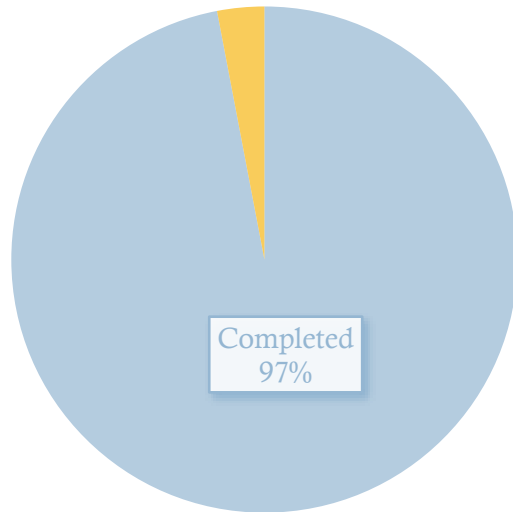

Work Schedule of August



- **To complete** soil excavation and soil backfill

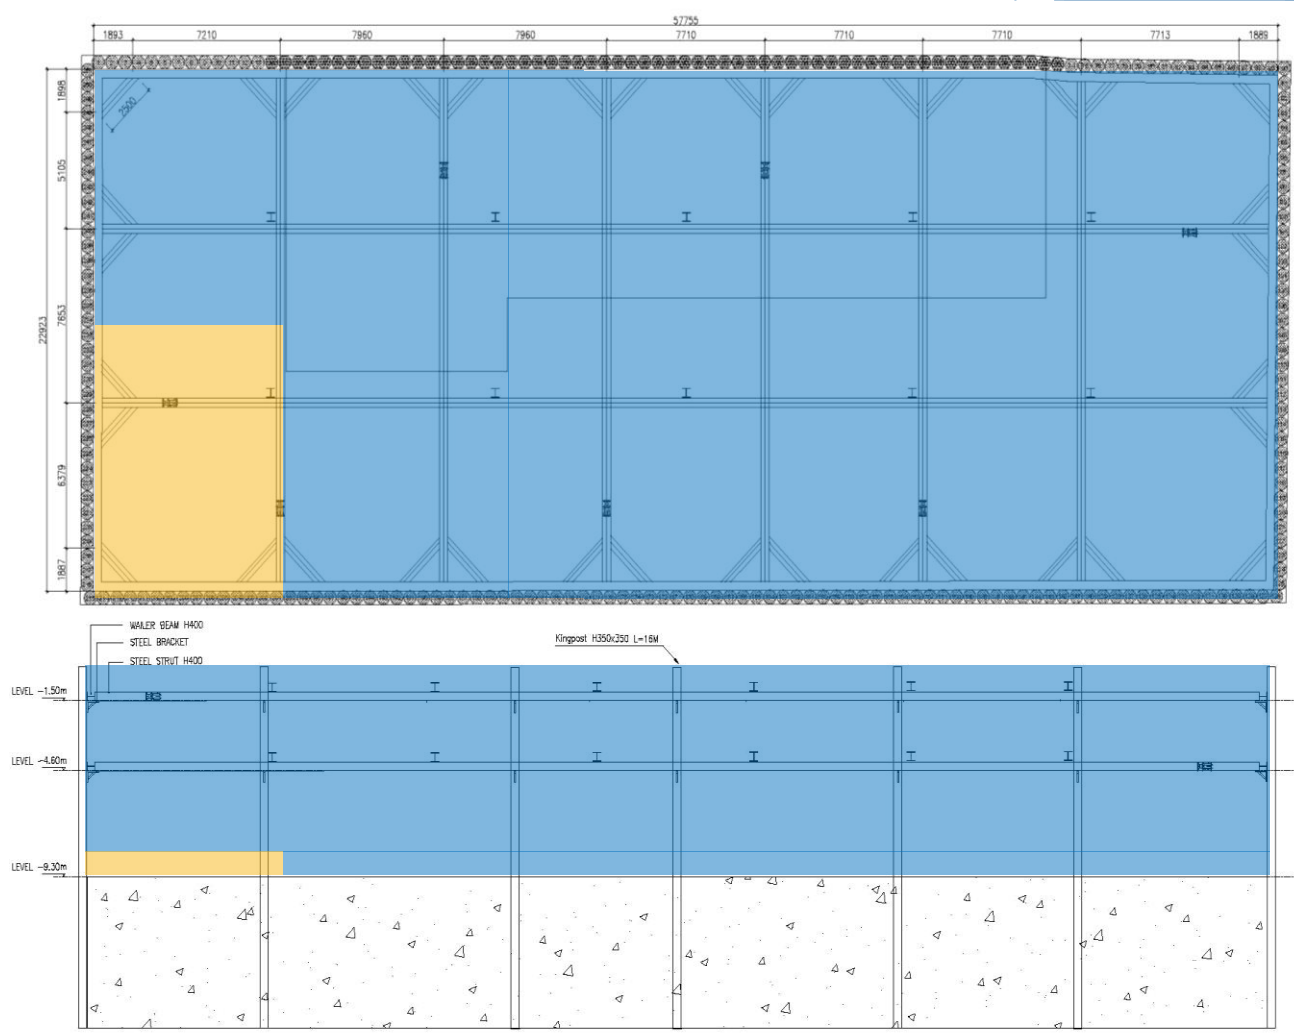

SUB-STRUCTURE WORK PROGRESS

II. Structure Work (Pile Cap)

Overall Pile Cap Progress

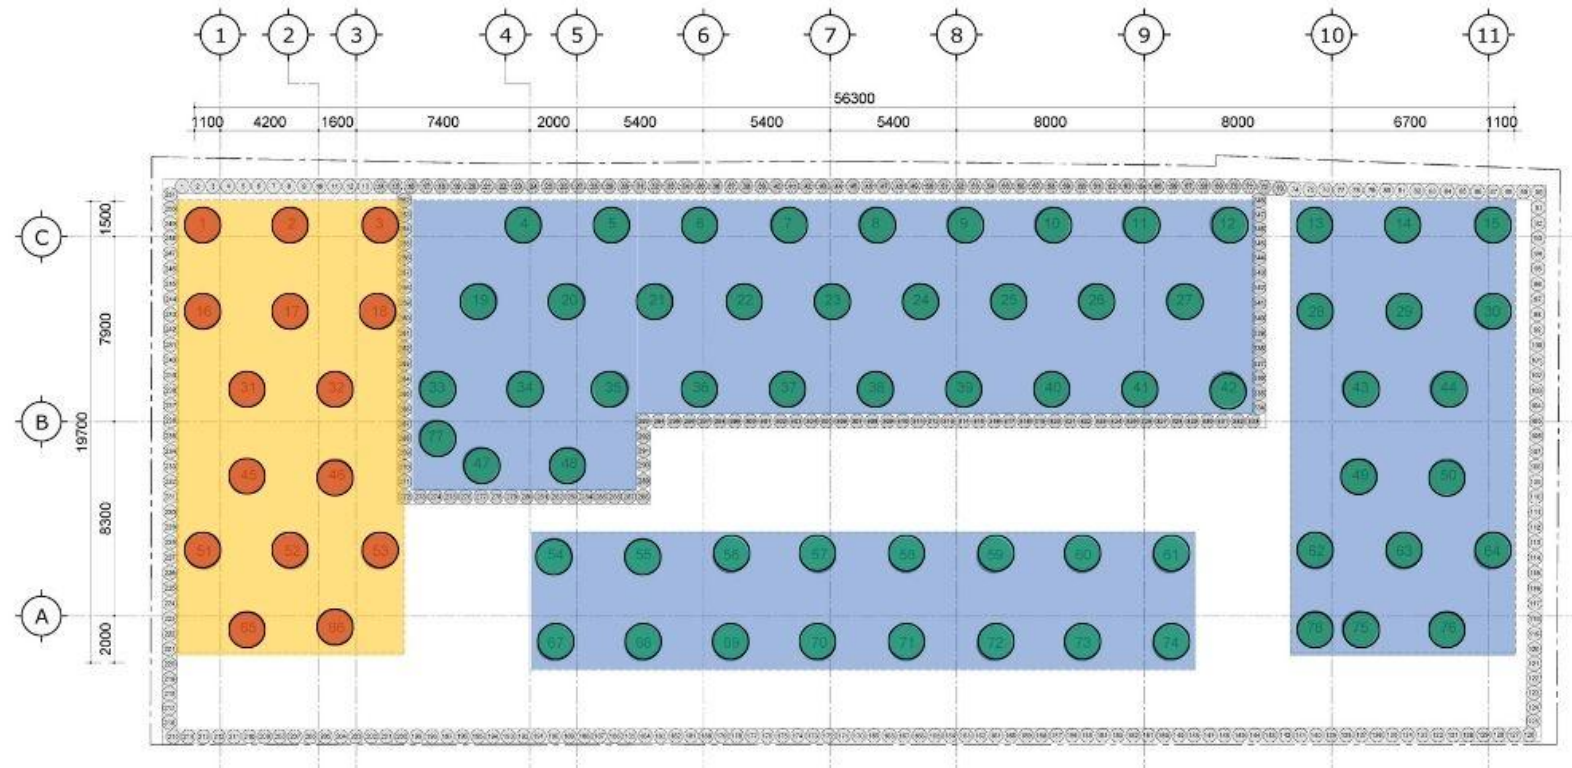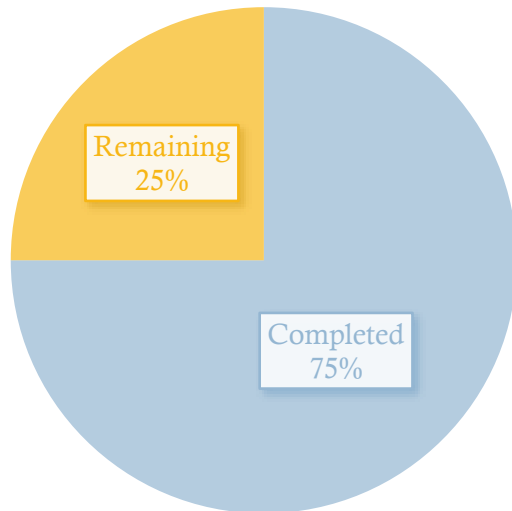

Work Schedule of August

- **16/Aug/26** : To complete PC2
- **20/Aug/26** : To complete Waste Water tank

LEGENDS	PILE CAP <u>PC2</u> :		
	Pile currently chipping	: 0 p	
	Pile 50% breaking	: 15 p	(100%)
	Pile completed breaking	: 0p / 15p	(0%)

PILE CAP		
	PC1	Completed
	PC2	Pile Chipping Work
	PC3	Completed
	PC4	Completed

SITE PHOTOS

I. Excavation work



Soil excavation of 3rd Layer (LVL -9.50M)

SITE PHOTOS



II. Structure Work



Pile chipping and breaking work

SITE PHOTOS




II. Structure Work

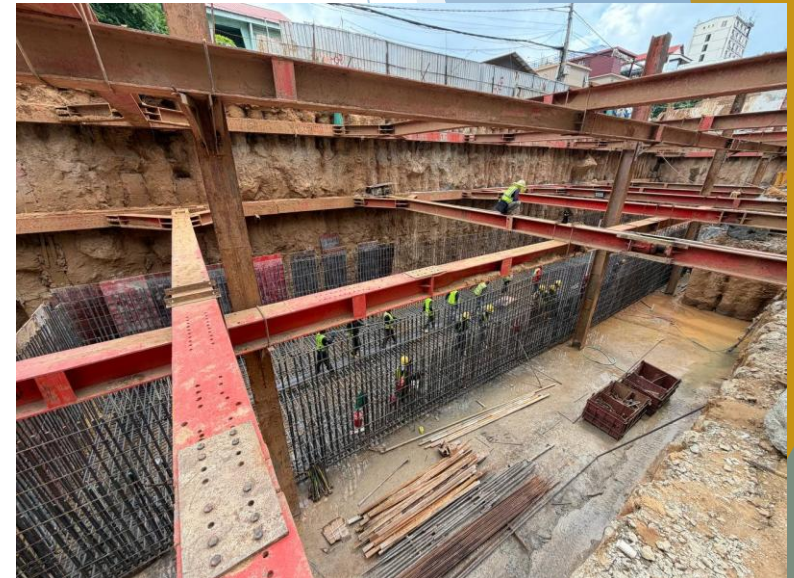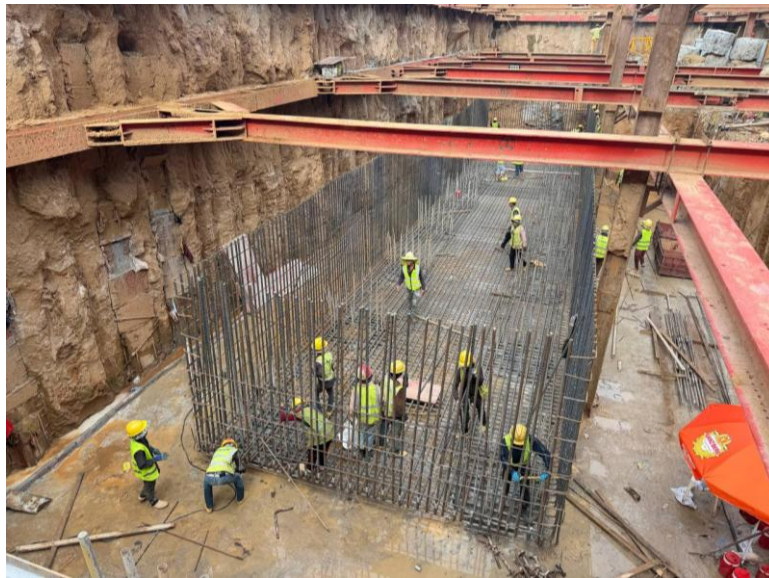

Install Bottom and Side bars of PC4

SITE PHOTOS

II. Structure Work

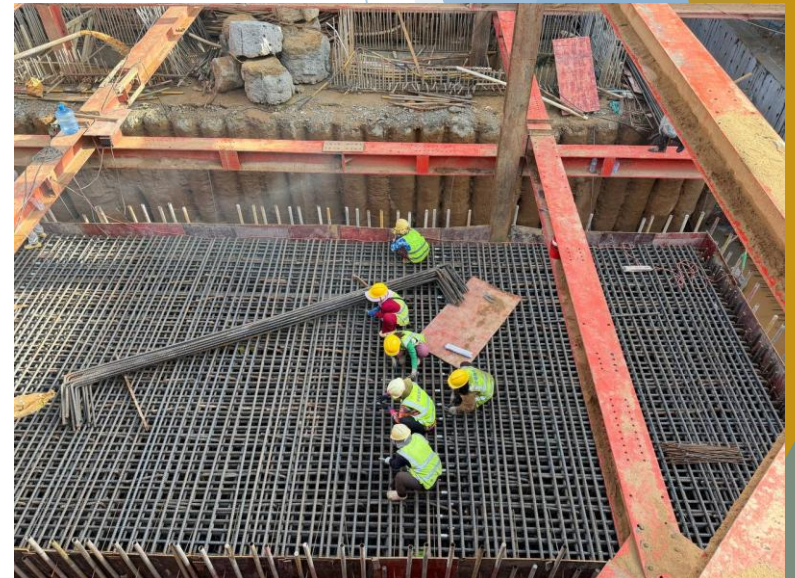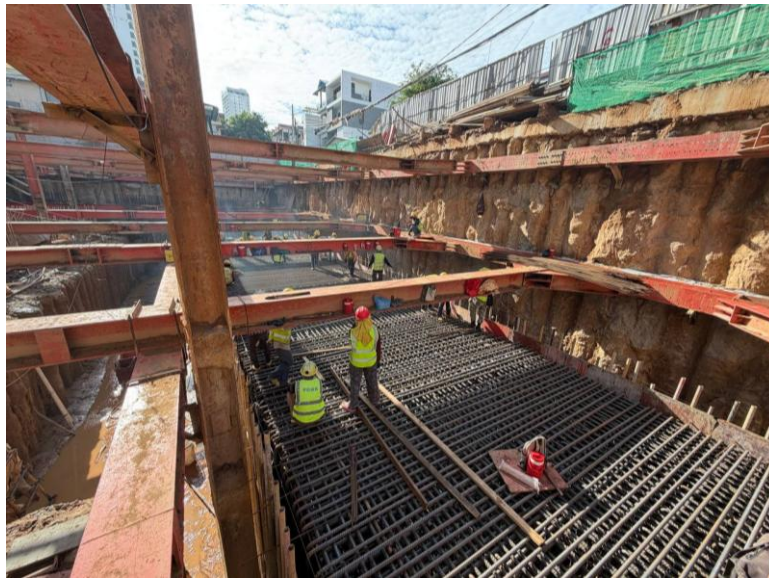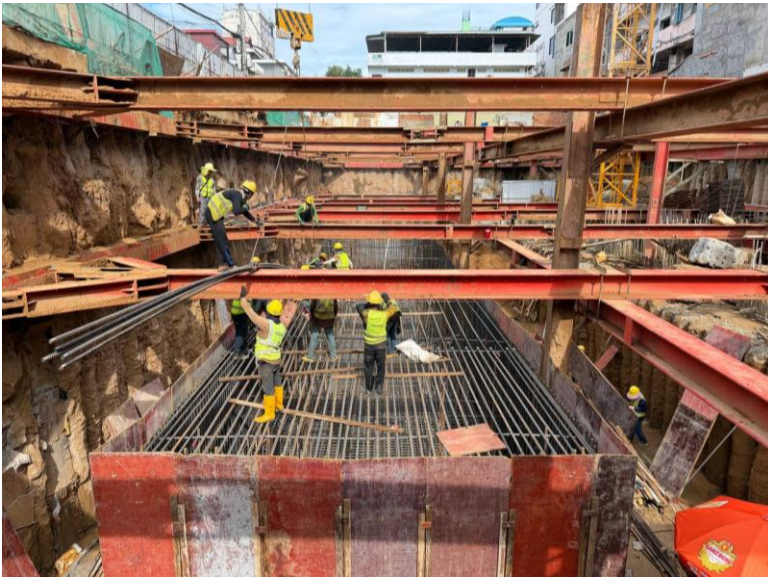


Install Top and Hook bars of PC4

SITE PHOTOS

II. Structure Work




Setting out coordination of columns

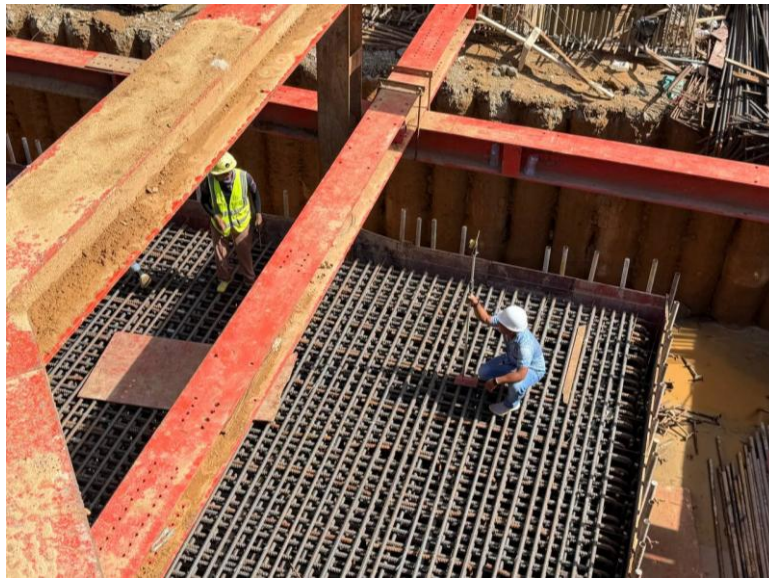


Install starter bars of columns

SITE PHOTOS

II. Structure Work

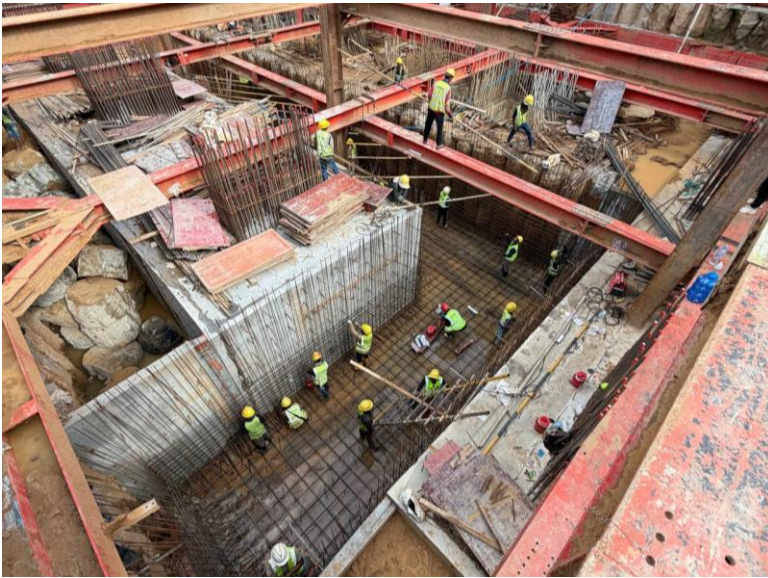



Install rebar of Septic Tank

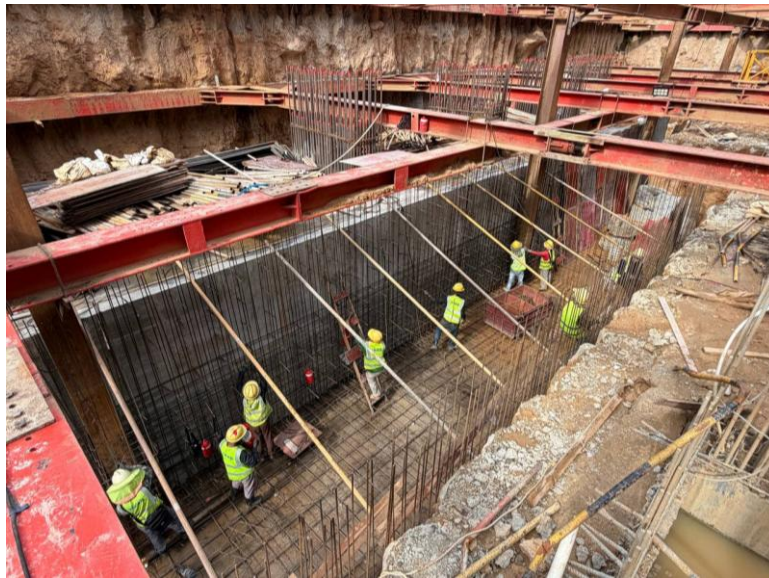

Install formwork of wall

SITE PHOTOS



III. Inspection Work

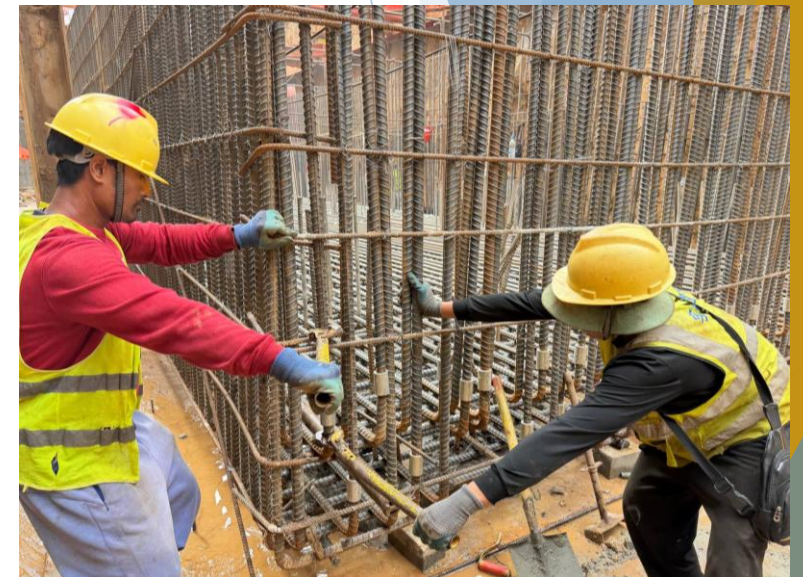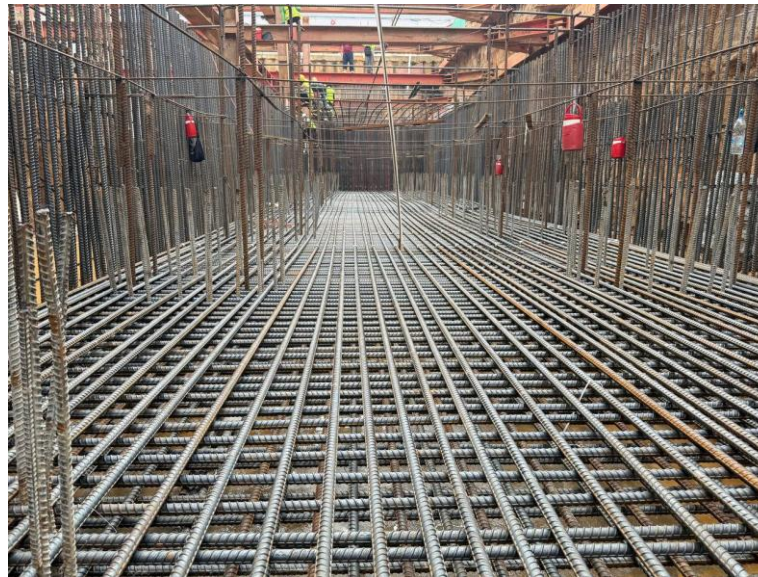

Inspection of Bottom and Side bar of PC4

SITE PHOTOS


III. Inspection Work

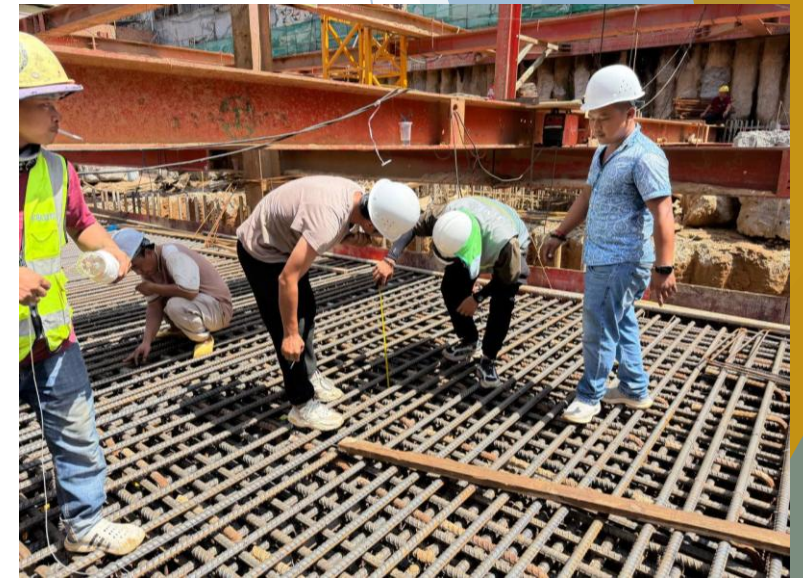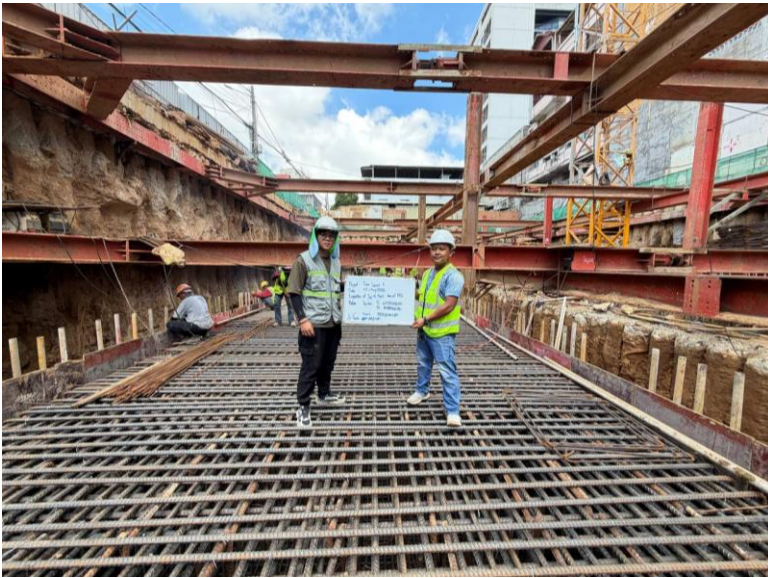

Inspection of Top and Hook bar of PC4

SITE PHOTOS

III. Inspection Work

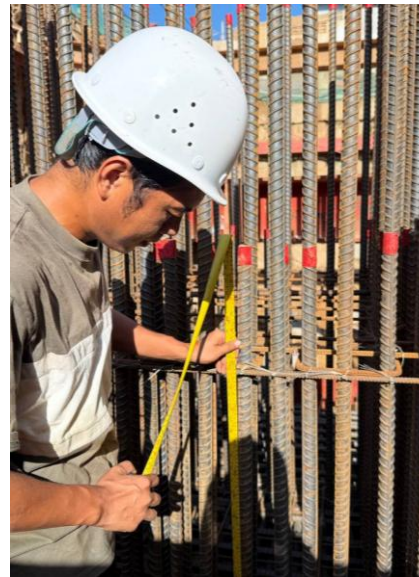

Inspection of starter rebar of columns

SITE PHOTOS

III. Inspection Work



Inspection of rebar of Septic Tank

SITE PHOTOS

IV. Concrete Work




Inspection of concrete



Check slump





Check temperature

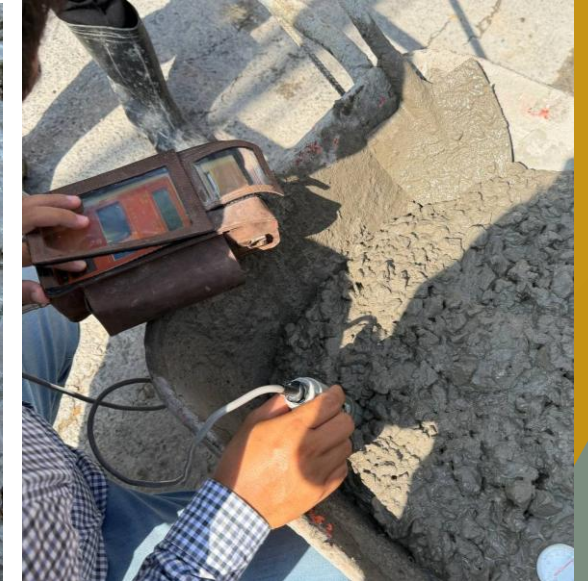

Check Cl- content

SITE PHOTOS


IV. Concrete Work

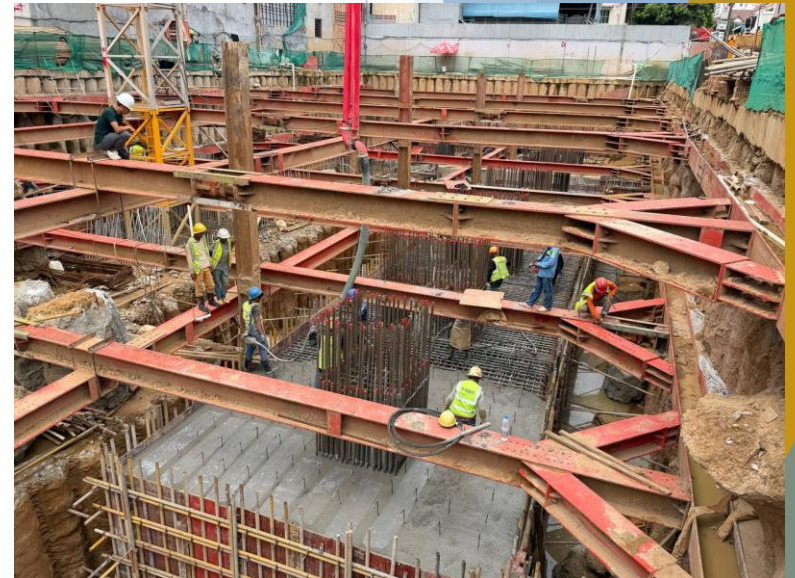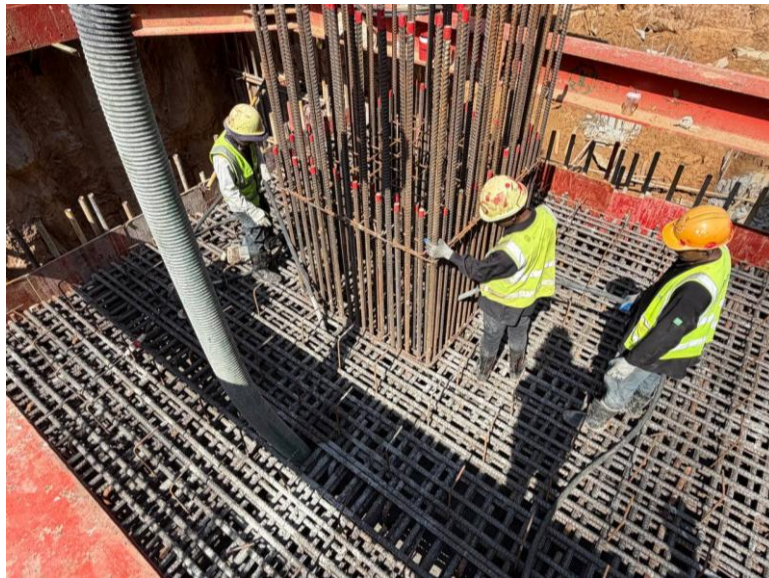

Casting concrete of PC4

SITE PHOTOS

IV. Concrete Work

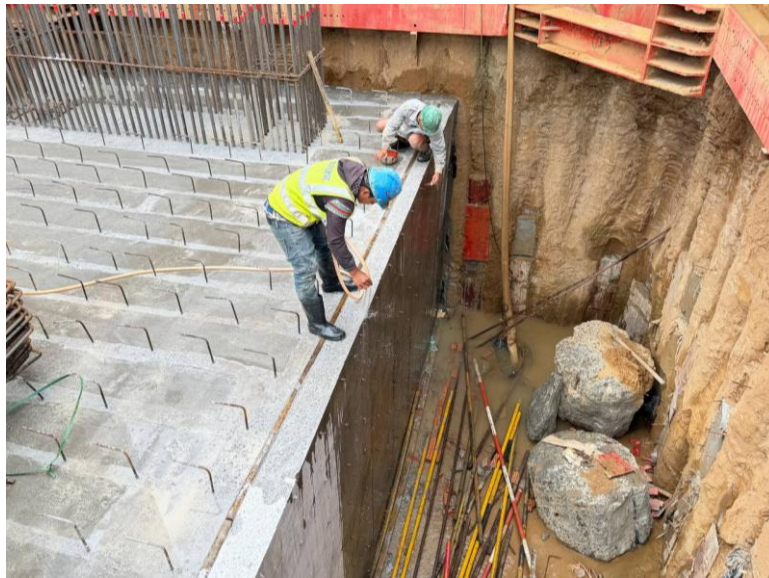

Curing of concrete

SITE PHOTOS

VI. HSE Inspection



Daily site surrounding cleaning



Toolbox meeting

PASSION FOR PROGRESS !

Building Level

50F

High Ground

49F

- Tennis Court
- Sky Boxing
- Sky Gym
- Sky Yoga

48F

- 40M Infinity Skypool
- Amphitheater
- Sky Terrace
- Play Space
- Sky Patio

39F

- Art Gallery
- Art Library
- Floating Bar
- Sky Cinema
- Meeting Room
- Sky Entertainment
- Co-Creation Space

GF

Lobby, Balcony Cafe

40-47F

Duplex Floor

8-38F

Classic Floor

2-7F

Carparking

B1-B2F

Carpark

THANK YOU !



Time Square 8

The Fastest Selling Project

in Phnom Penh

