

TIME SQUARE 410 (8)

MONTHLY REPORT

29.November.2025




LOCATION OF CONSTRUCTION SITE




PROGRESS PLAN OF PILE WORK

- Estimated to be completed on the 10th December 2025

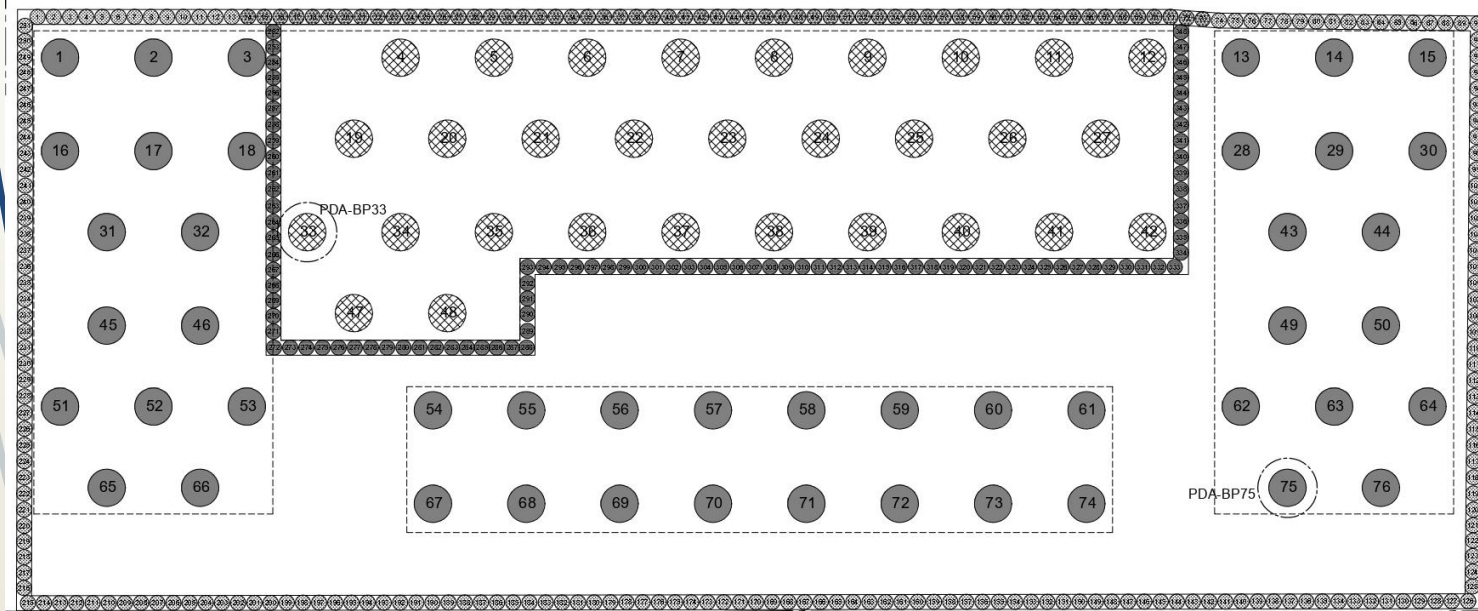


MAIN PILE

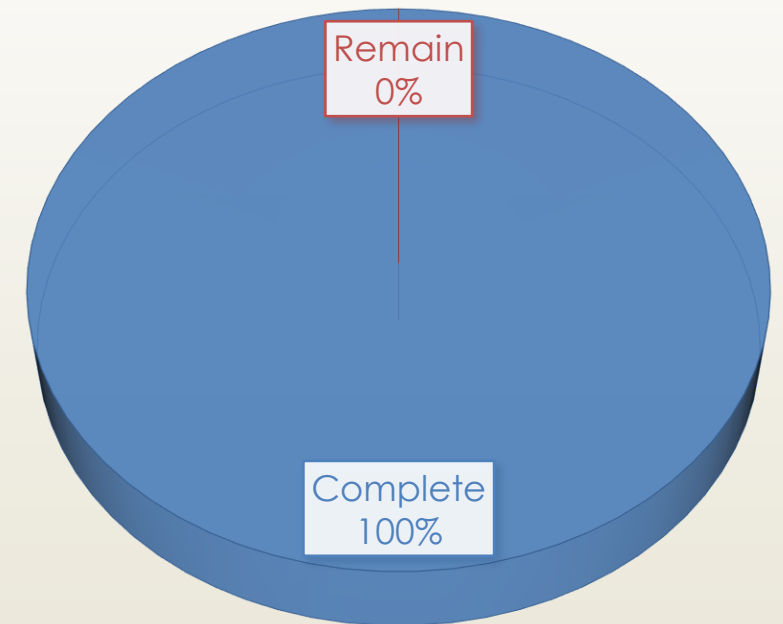

PILE PROGRESS UP TO 29.November.2025


Completed 72/76 Piles

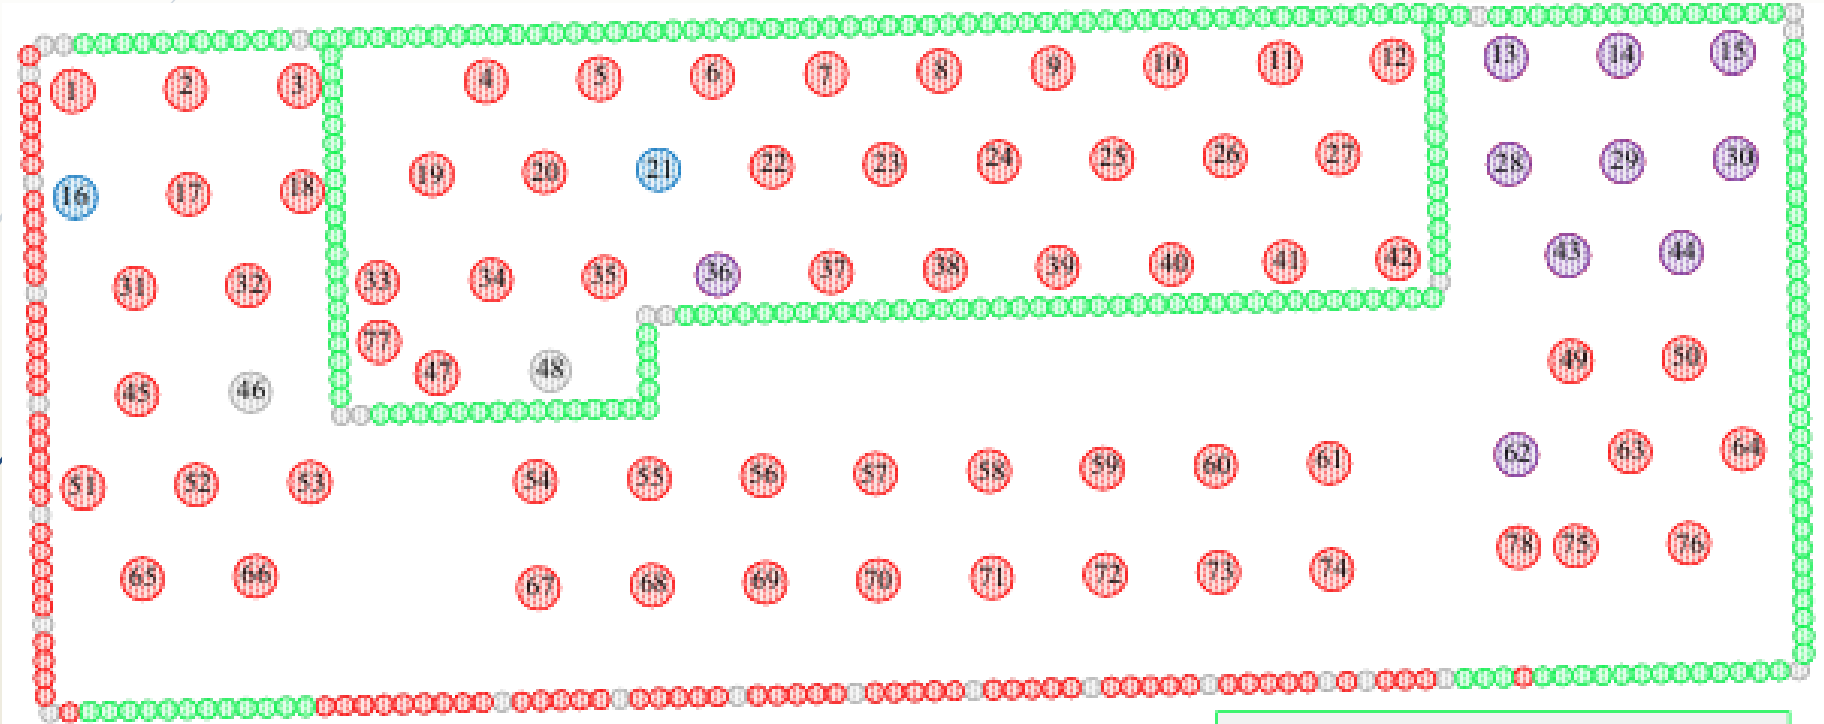

PILE PROGRESS UP TO 29.November.2025


Completed 72/76 Piles

MAIN PILE

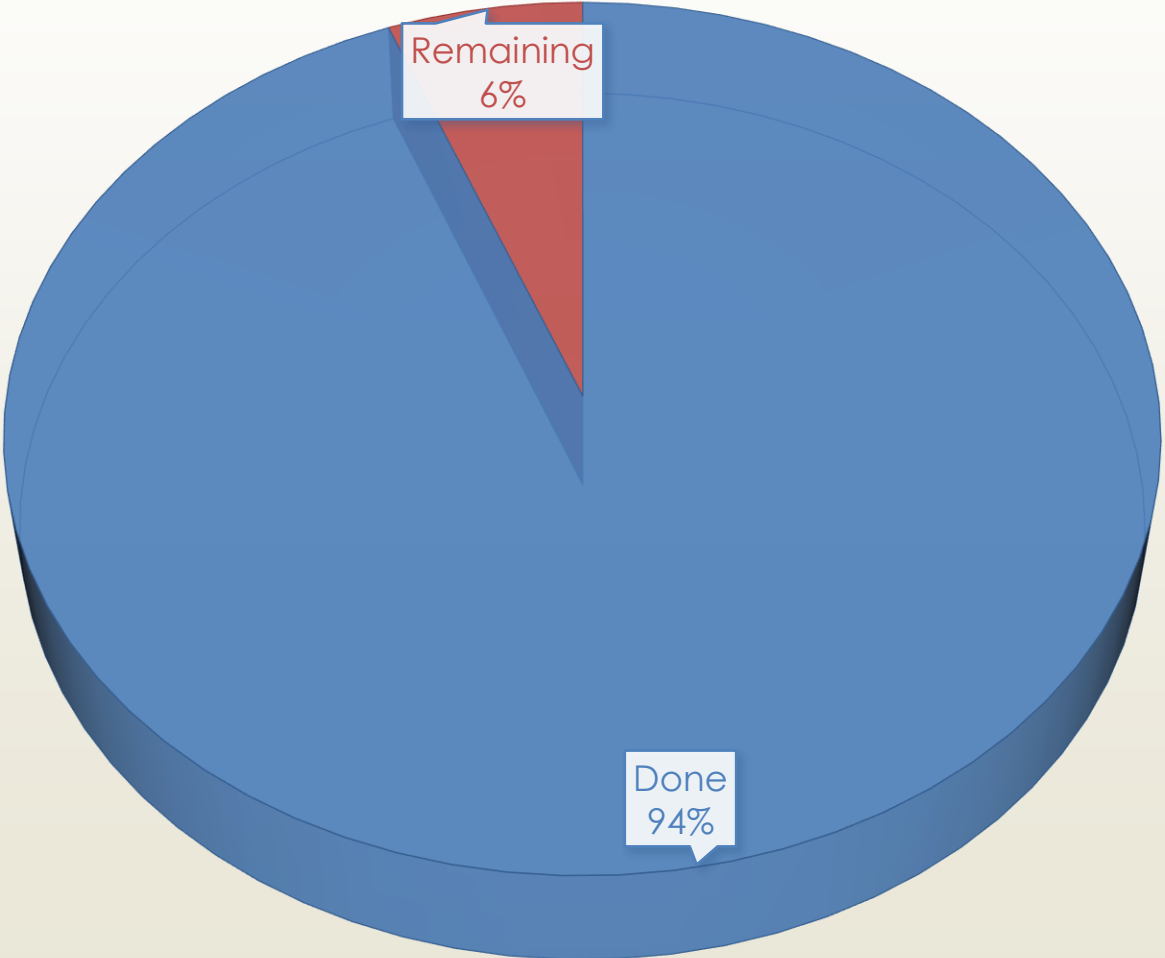

CBP PROGRESS


Completed 328p/328p (Done)

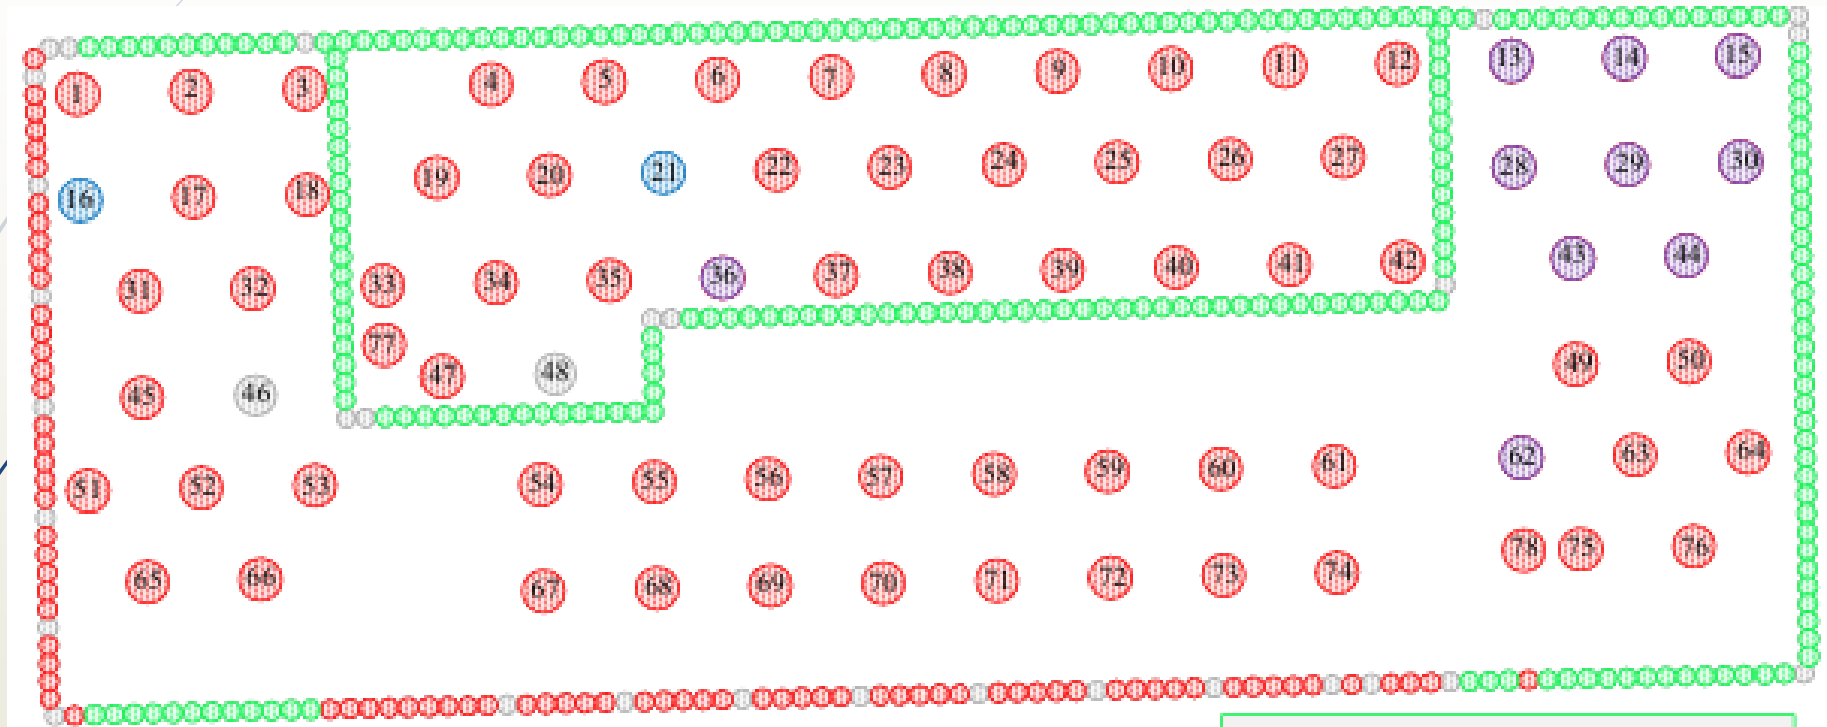

CBP PROGRESS UP

Completed 328p/328p (Done)

CBP PILE

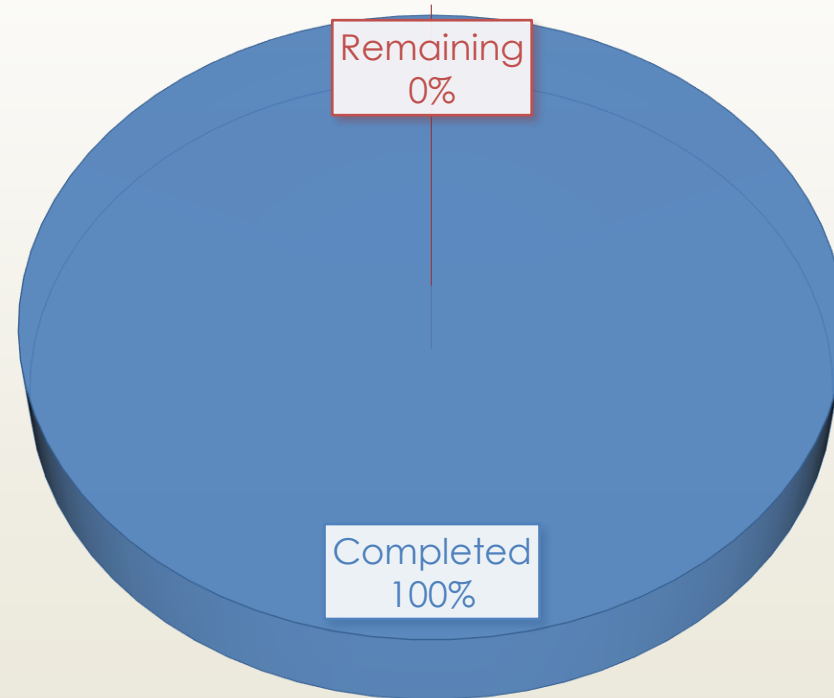

PILE SETTING OUT WORK



DRILLING WORK



REBAR FRABRICATION WORK




BENTONITE SLURRY INSPECTION



Bentonite inspection: Before drilling, before casting concrete.

HSE INSPECTION

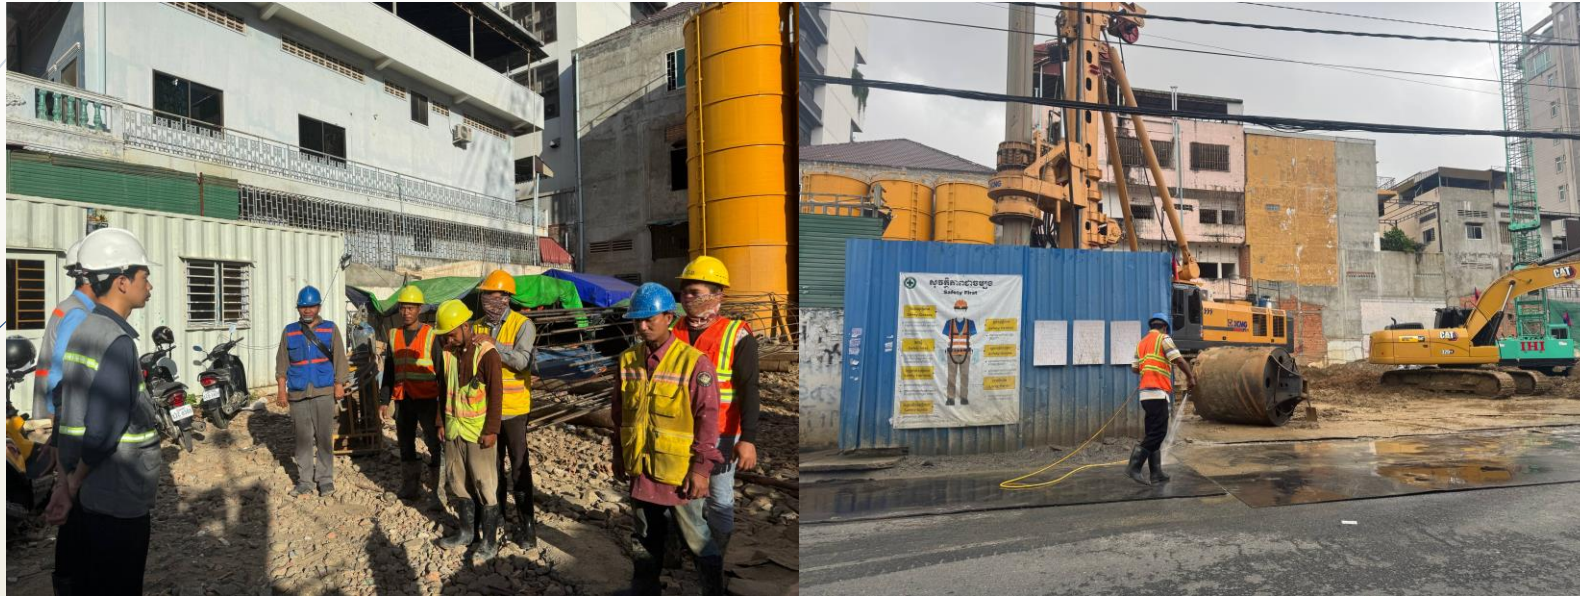

Toolbox meeting: Checking up on safety environment, PPE and front site cleaning .

TOP VIEW




MATERIAL INSPECTION




Sonic Test Progress Up to 29.November.2025

Completed 10p/76p




SONIC TEST

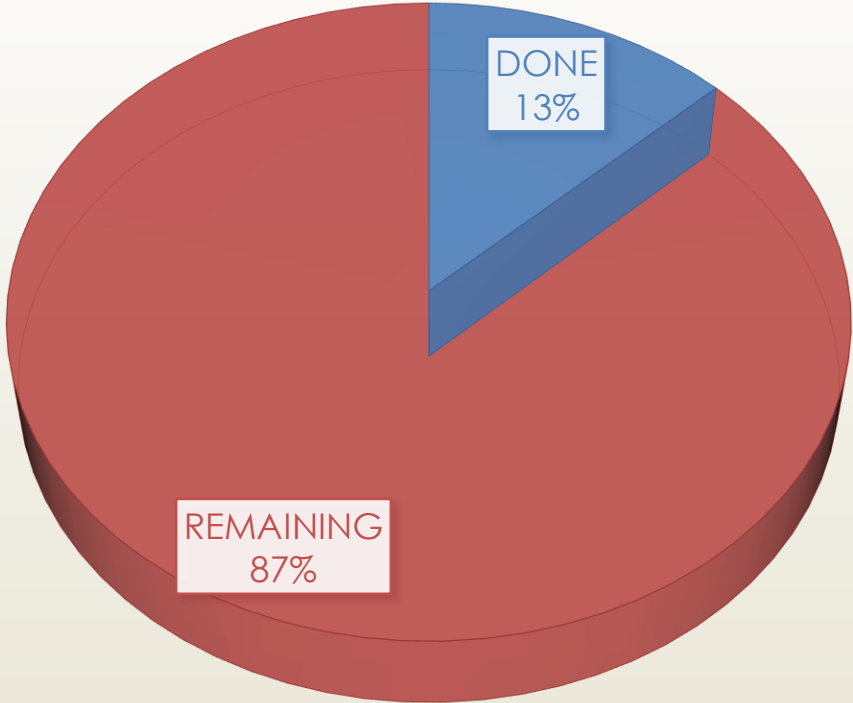

Sonic Test Progress Up to 29.November.2025 Completed 10p/76p

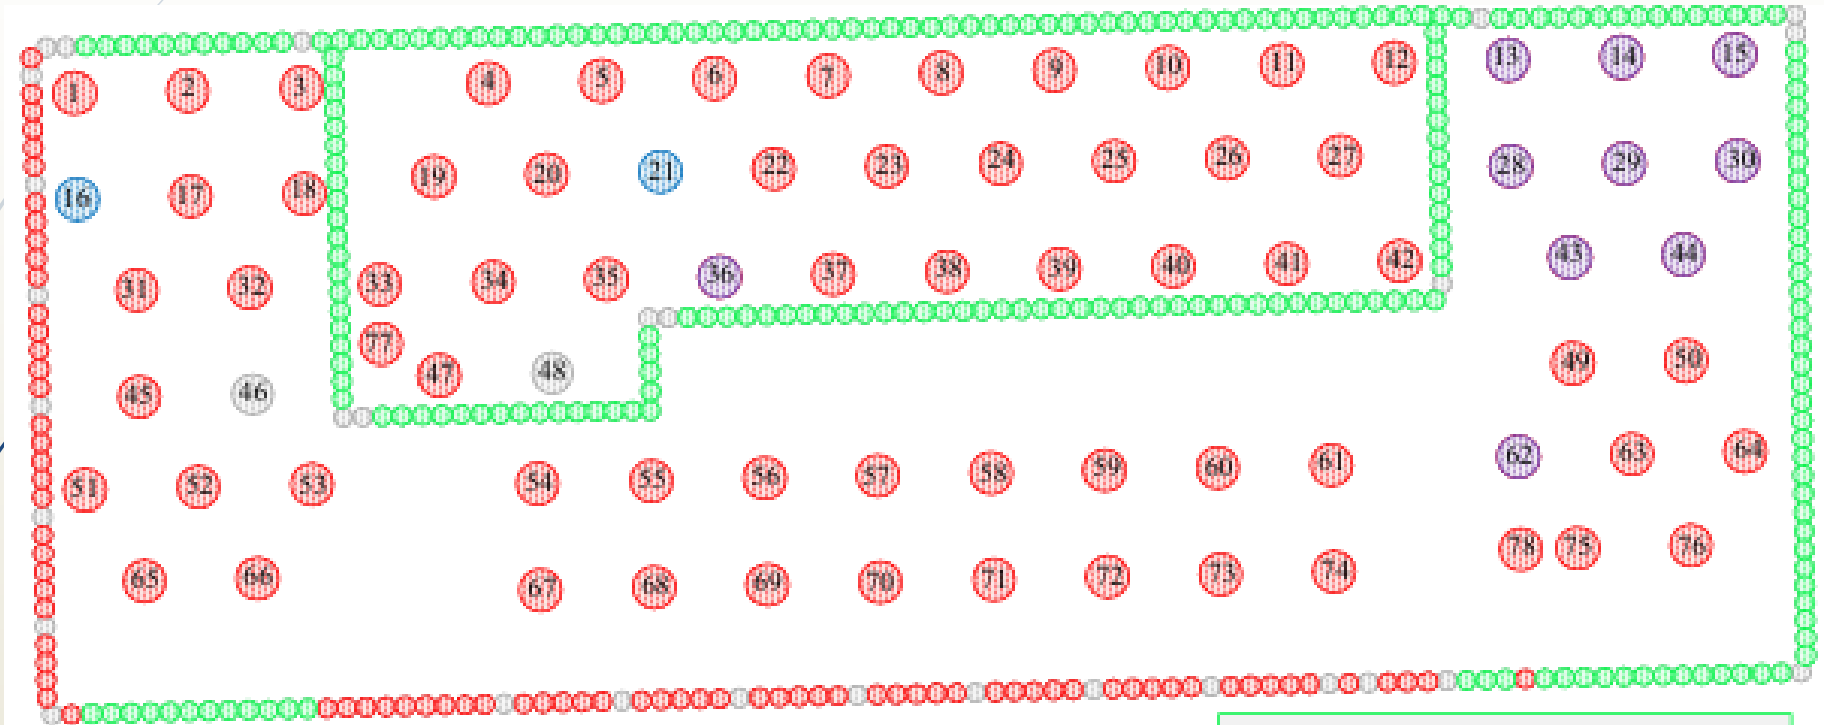

Cross-Hole Sonic Logging Test

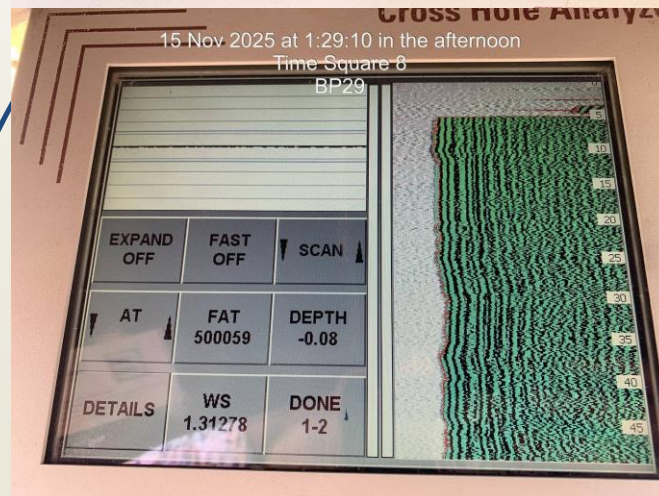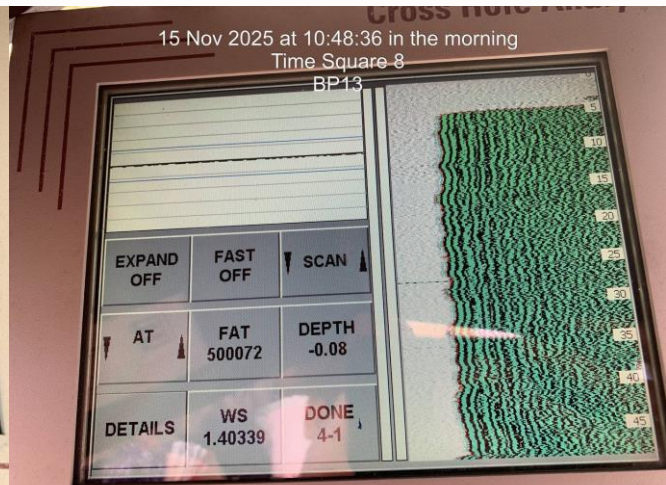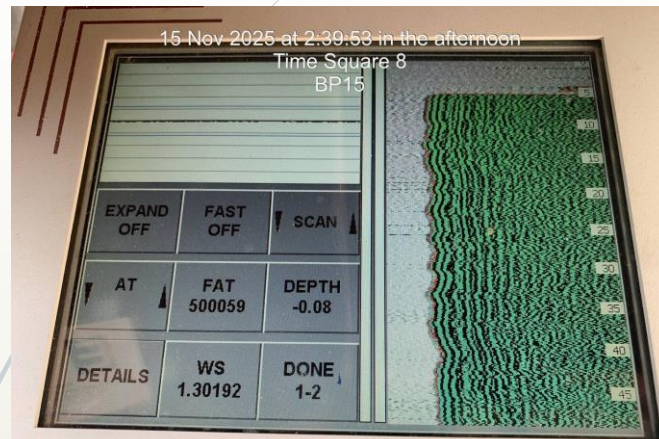



Time Square 8

The Fastest Selling Project

in Phnom Penh



PASSION FOR PROGRESS!

Building Level

50F

High Ground

49F

- Tennis Court
- Sky Gym
- Sky Boxing
- Sky Yoga

48F

- 40M Infinity Skypool
- Sky Terrace
- Sky Patio
- Amphitheater
- Play Space

39F

- Art Gallery
- Floating Bar
- Meeting Room
- Co Creation Space
- Art Library
- Sky Cinema
- Sky Entertainment

GF

Lobby, Balcony Cafe

40-47F

Duplex Floor

8-38F

Classic Floor

2-7F

Carparking

B1-B2F

Carpark

THANK YOU!
