

TIME SQUARE 10 SHV REPORT

09 October 2026

TIME SQUARE 10 SHV LOCATION



TIME SQUARE 10 SHV LOCATION




TIME SQUARE 10 SHV ANOTHER POINT OF VIEW



TIME SQUARE 10 SHV FLOOR PLAN



TOOL BOX MEETING

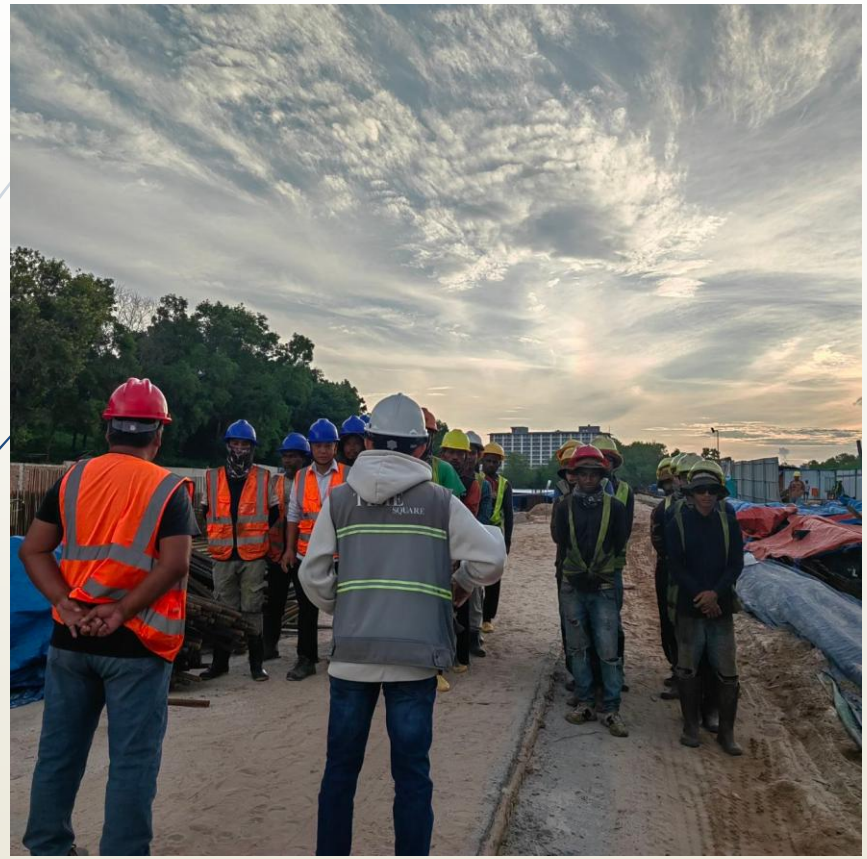




MEETING WITH CONCRETE TEAM







BREAKING PILE-HEAD PROGESS UP TO 09 OCTOBER 2026
177/197pcs

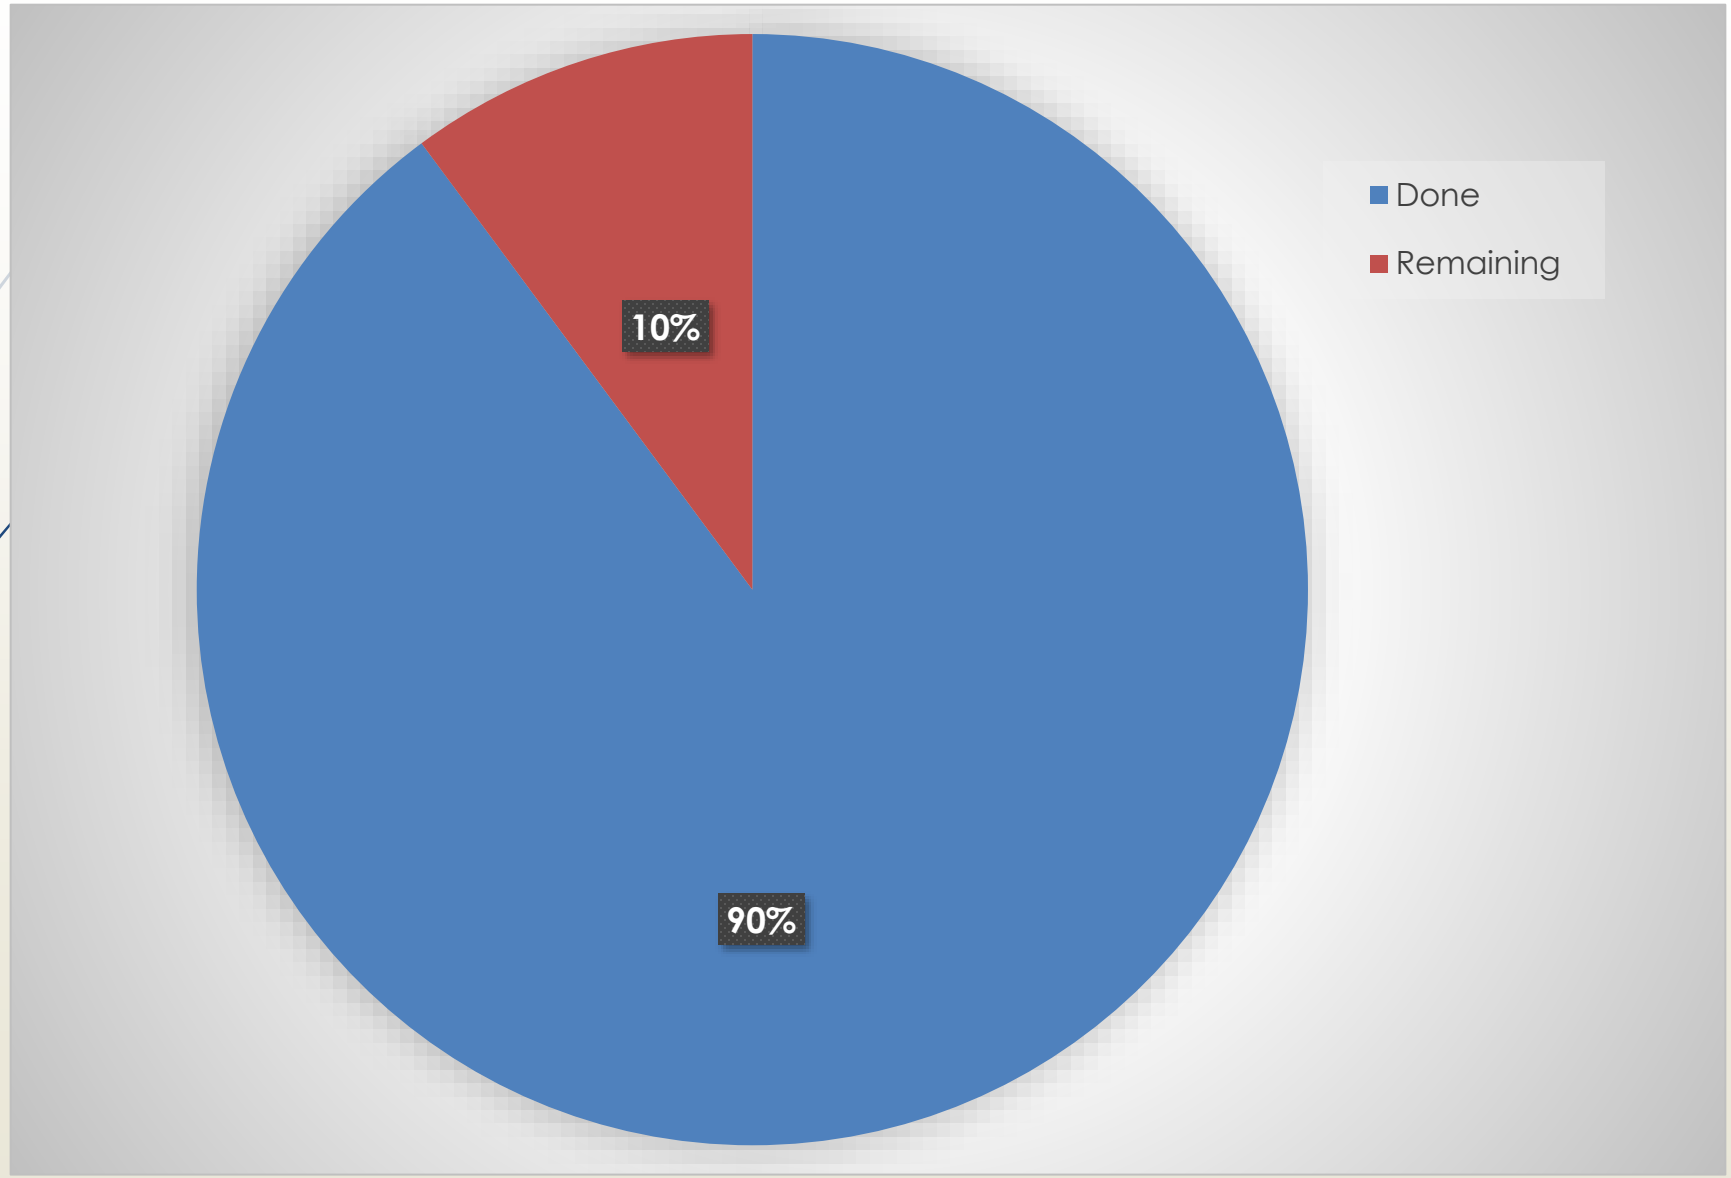

PILECAP FINISHED PROGESS UP TO 09 OCTOBER 2026
21/28pc

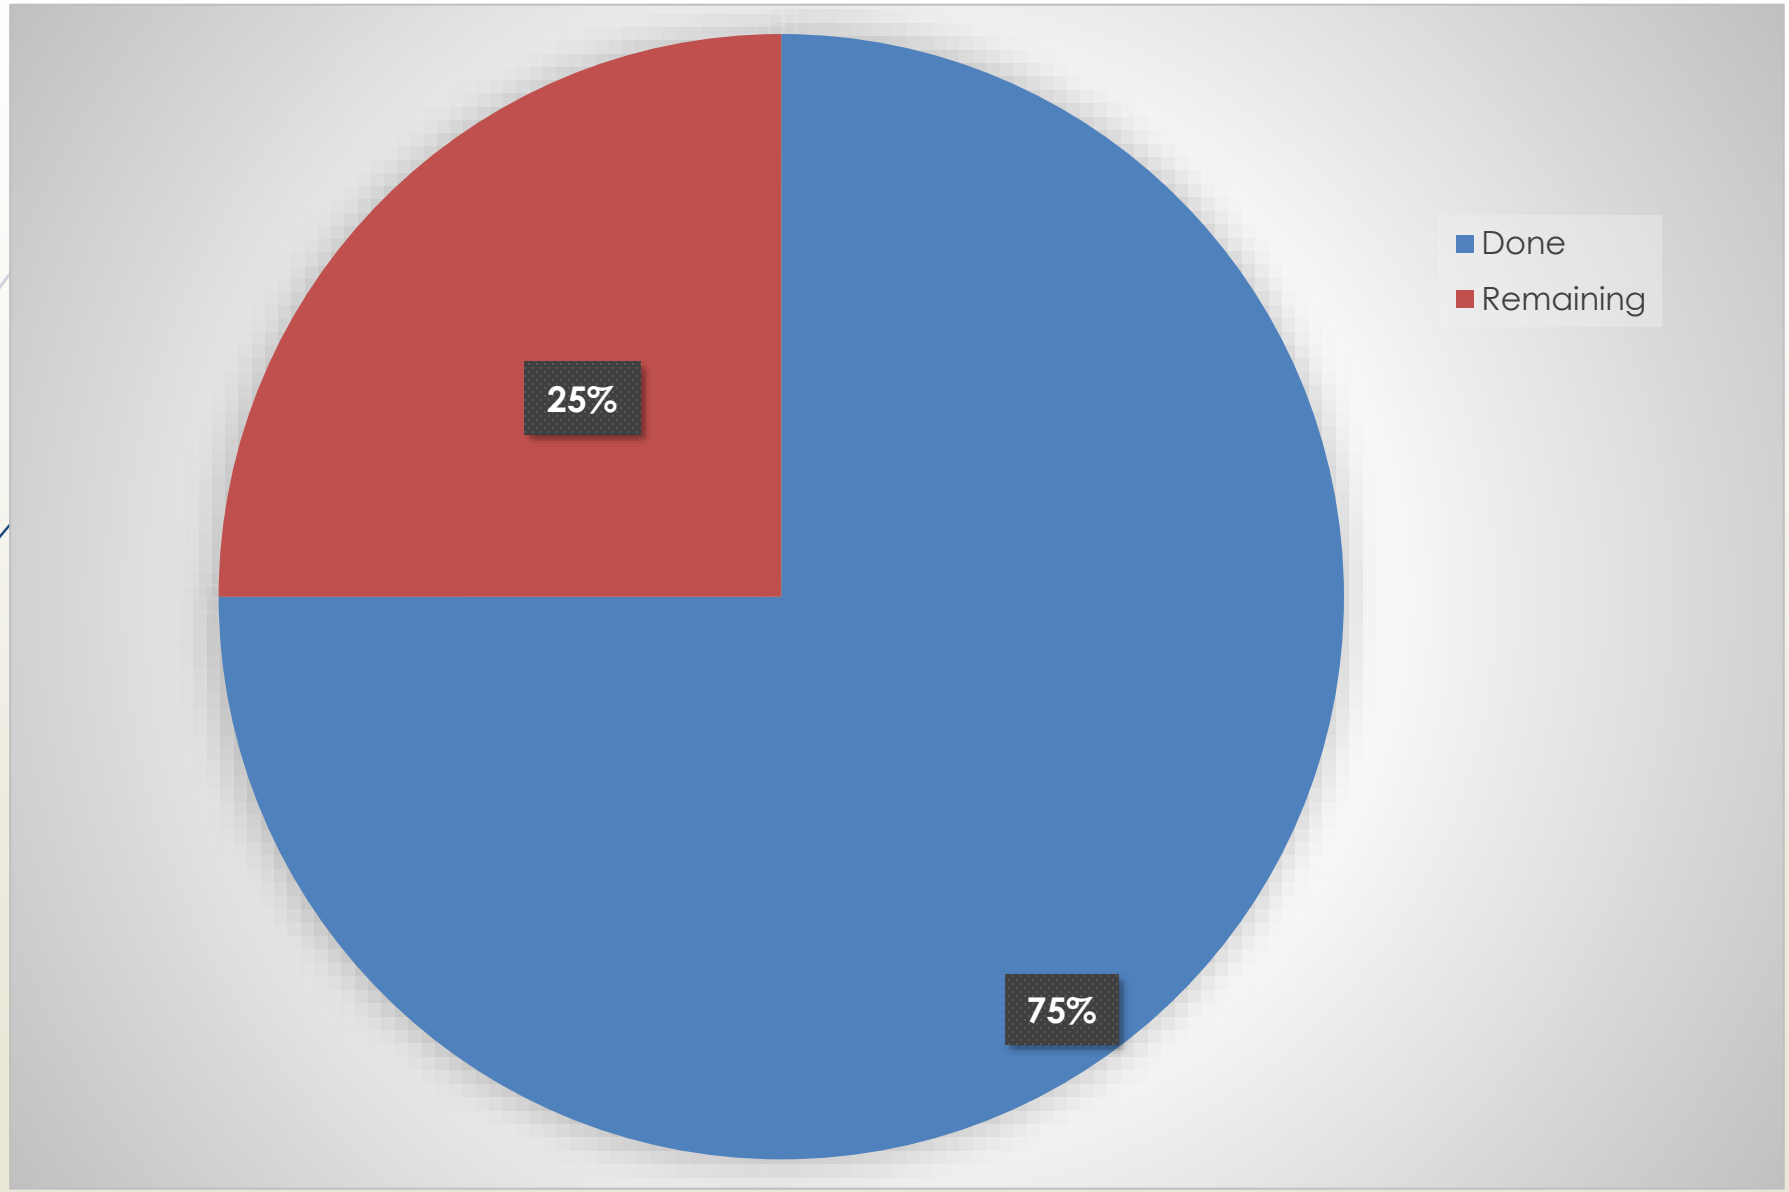

BREAKING PILE-HEAD AND COMPLETED PILECAP PROGESS UP TO 09 OCTOBER 2026

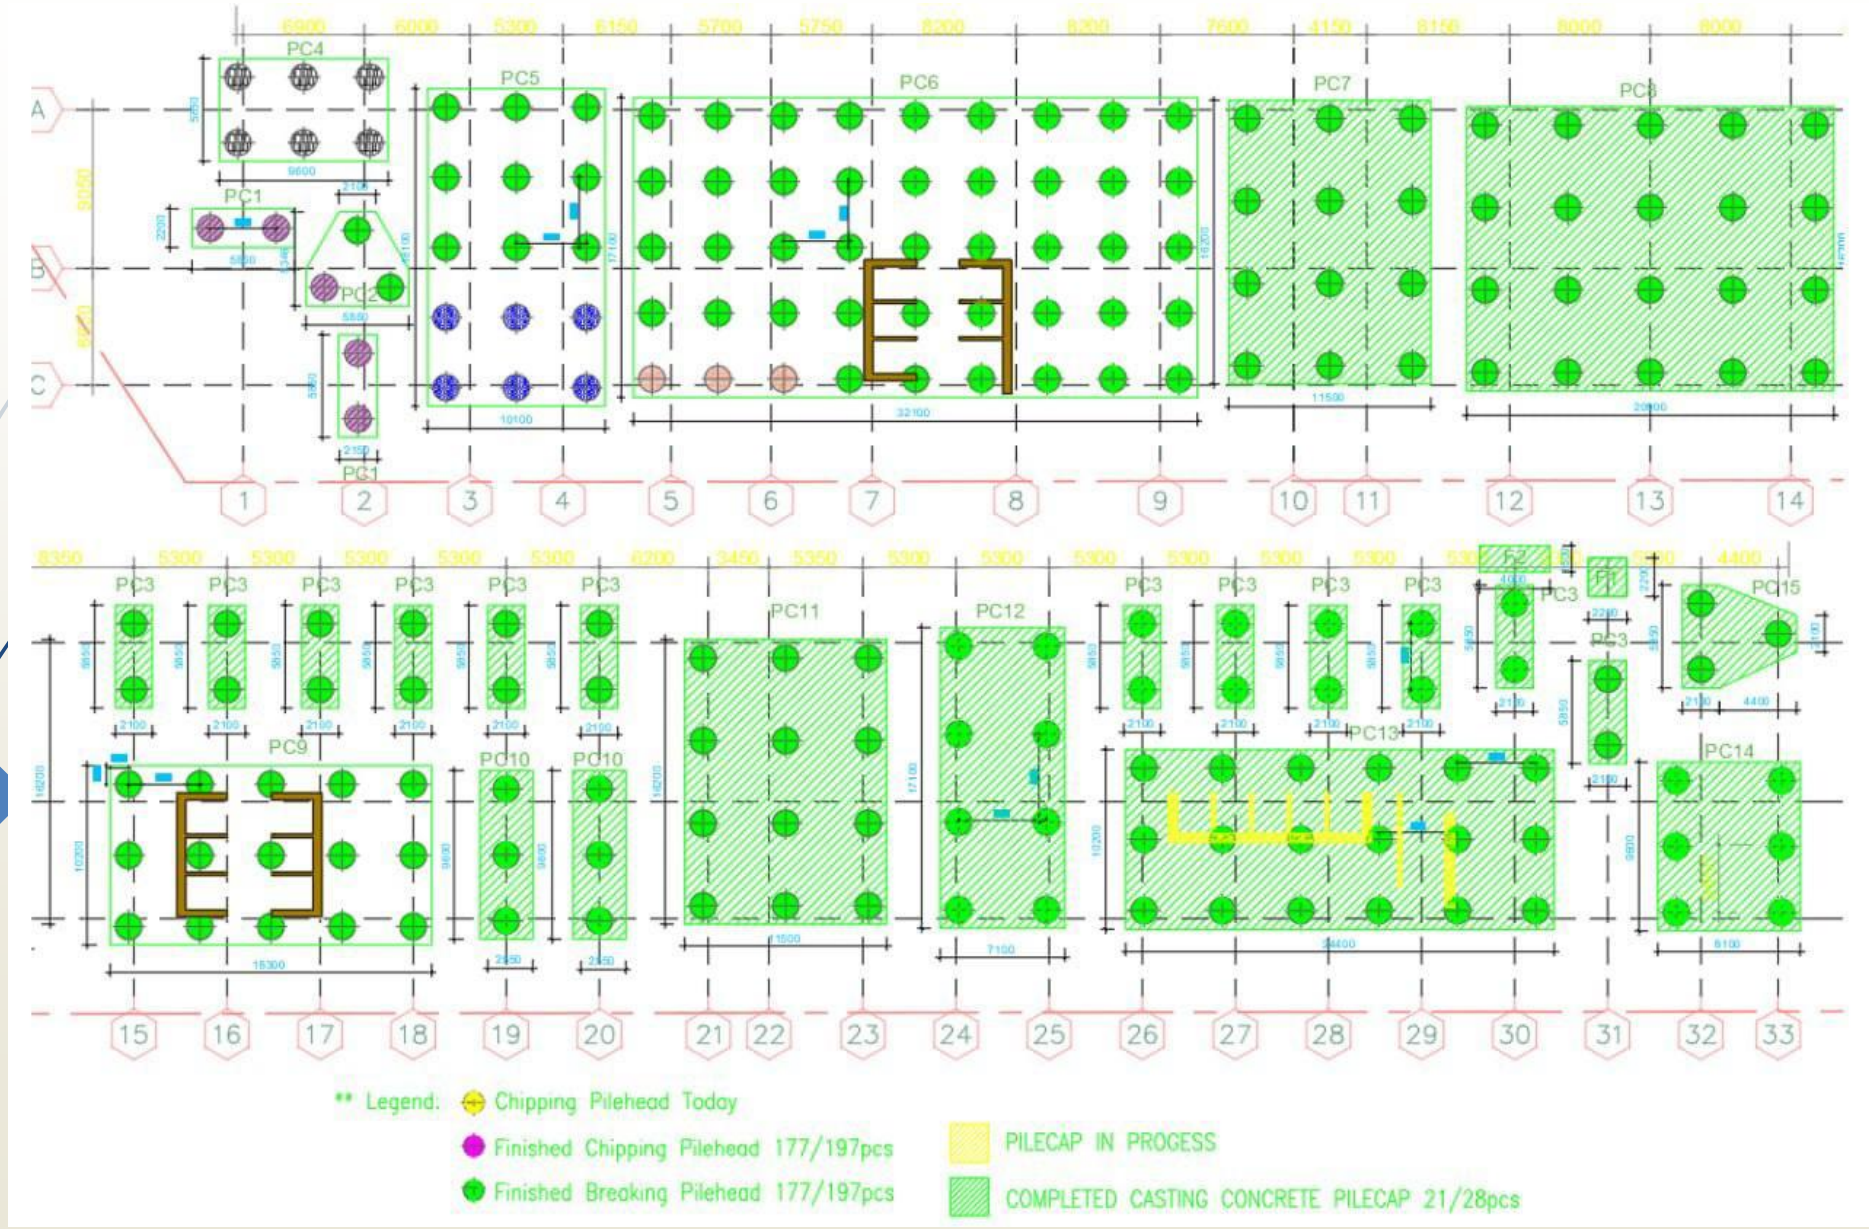

SOIL EXCAVATE FOR PC9 & PC13







CHIPPING PILE-HEAD PC9







INSTALLING GROUNDING SYSTERM







INSPECTION REBAR PC13













INSPECTION CONCRETE PC13












SEPTIC TANK WORK




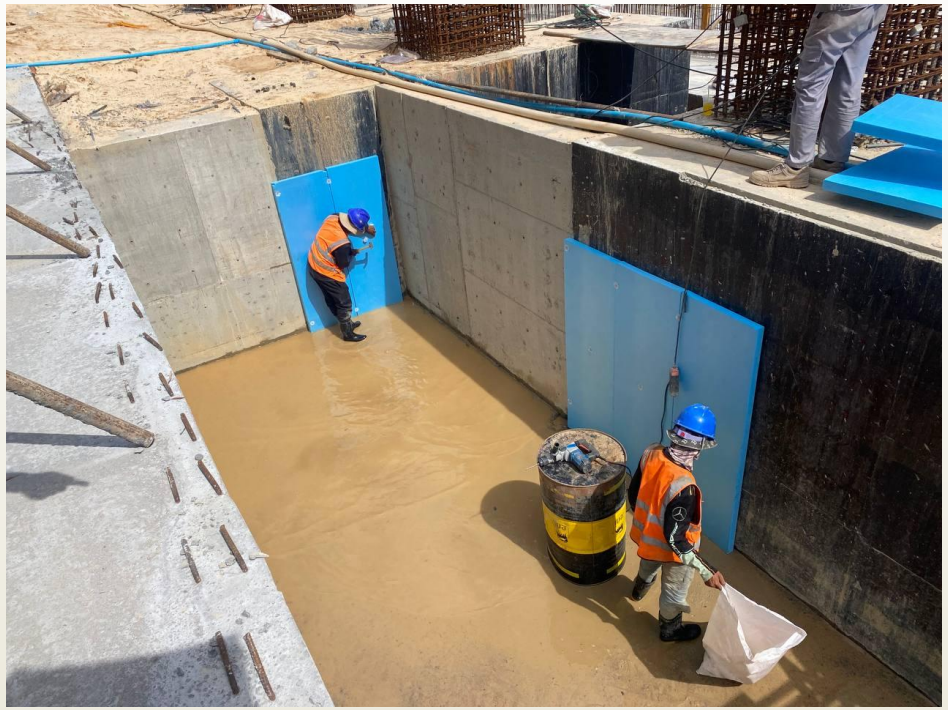

SOIL BACKFILL





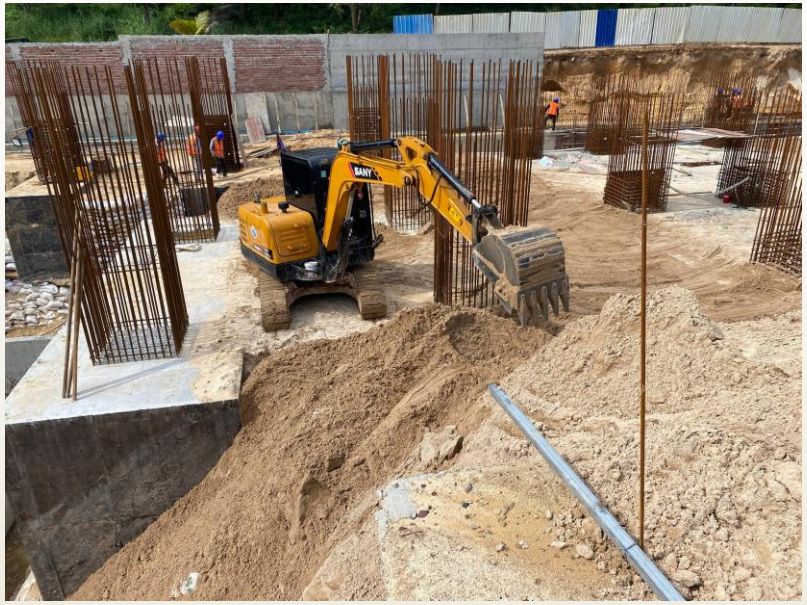

MATERIAL ARRIVED







SITE ENVIRONMENT









PASSION FOR PROGRESS!

TIME SQUARE 10

OCEAN VIEW

THE BEST DAY IN OTRES BEACH

THANK YOU!
