UC88 Wyndham Garden

MONTHLY PROGRESS REPORT SEPTEMBER 2026



Owner	**:**	**CHHUN SAMBATH DEVELOPMENT**
Consultant	**:**	**UC DESIGN BUILD CO., LTD**

No.60 & 62, Street 322, Sangkat Boeung Keng Kang1, Khan Chamkarmon,
Phnom Penh, Cambodia

CONSTRUCTION PROGRESS REPORT

1. Project Information

Project Name : UC88 WYNDHAM GARDEN	UC88 Hotel Residence	Reporting Period	September 2026
Expected Completion	December 2026	Status	On Track

2. Completed Works

Task	Status
Main Ground floor	Completed
Front office finished	Completed
Exterior signage: roof top finished 100%, canopy finished 100% and front glass logo finished 100%.	Completed
luggage room finished	Completed



Floor: North Elevation
Date: 30-September -2026
Work: External Glass & Painting Works



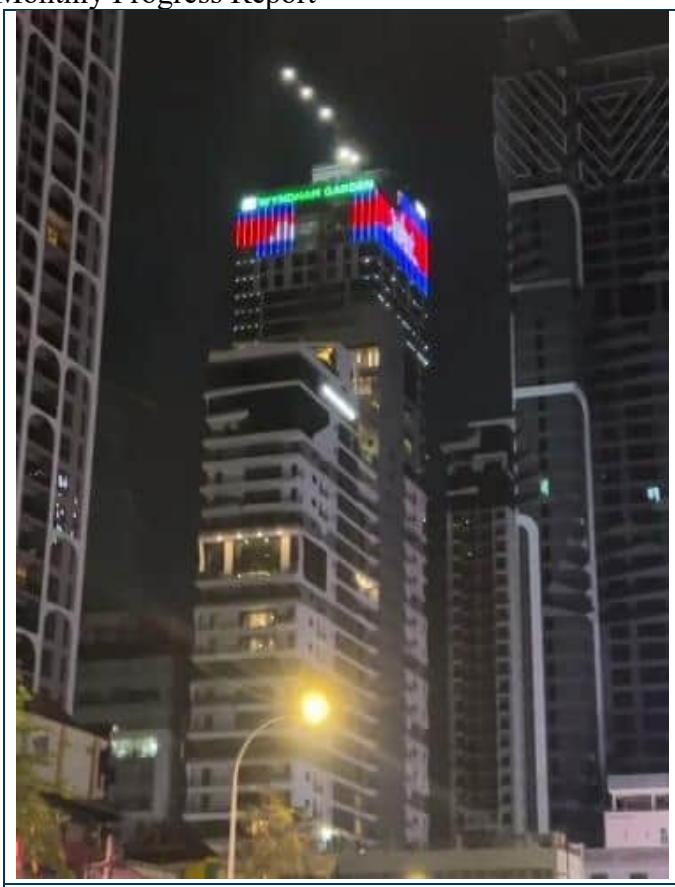
Floor: East Elevation
Date: 30-September -2026
Work: External Glass & Painting Works



Floor: South Elevation
Date: 30-September -2026
Work: External Glass & Painting Works



Floor: West Elevation
Date: 30-September -2026
Work: External Glass & Painting Works

	
Floor: North Elevation	Floor: East Elevation
Date: 30-September -2026	Date: 30-September -2026
Work: External Lighting work	Work: External Lighting work
	
Floor: South Elevation	Floor: West Elevation
Date: 30-September -2026	Date: 30-September -2026
Work: External Lighting work	Work: External Lighting work

Parking (B1th-2th-3th Floor)

- Material store area
- Wall & ceiling putty painting work

	
Floor: B1 Floor	Floor: B1 Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Material store area	Work: Material store area
	
Floor: B1 Floor	Floor: B2 Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall & Ceiling putty painting work	Work: Wall & Ceiling putty painting work
	
Floor: B2 Floor	Floor: B2 Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall & Ceiling putty painting work	Work: Wall & Ceiling putty painting work

	
Floor: B2 Floor	Floor: B3 Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall & Ceiling putty painting work	Work: Wall & Ceiling putty painting work
	
Floor: B3 Floor	Floor: B3 Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall & Ceiling putty painting work	Work: Wall & Ceiling putty painting work
	
Floor: B3 Floor	Floor: B3 Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall & Ceiling putty painting work	Work: Wall & Ceiling putty painting work

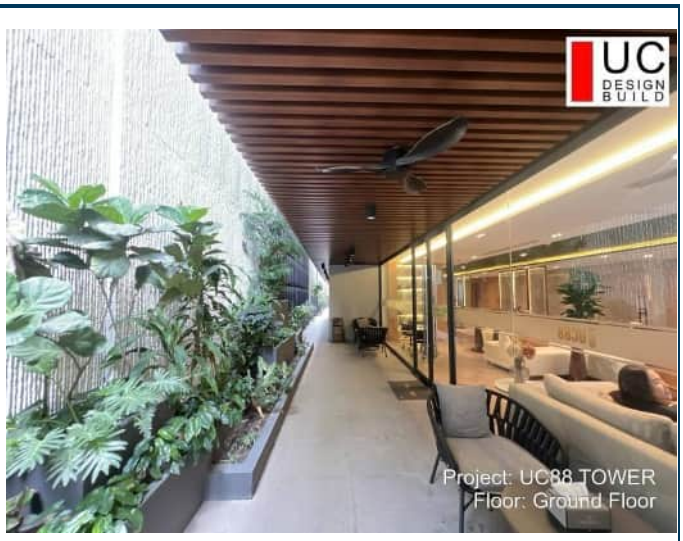
Ground Floor

- Front facade marble work
- Canopy steel and painting work
- Drop off area pavement work
- Interior works & loose furniture completed

	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Front facade marble work	Work: Canopy steel and painting work
	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Drop off area pavement work	Work: Drop off area pavement work
	
Floor: Ground Floor	Floor: Ground Floor
Date 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

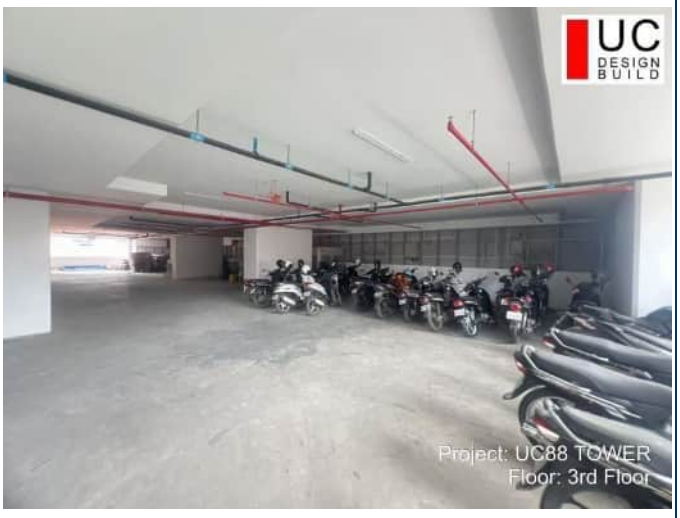
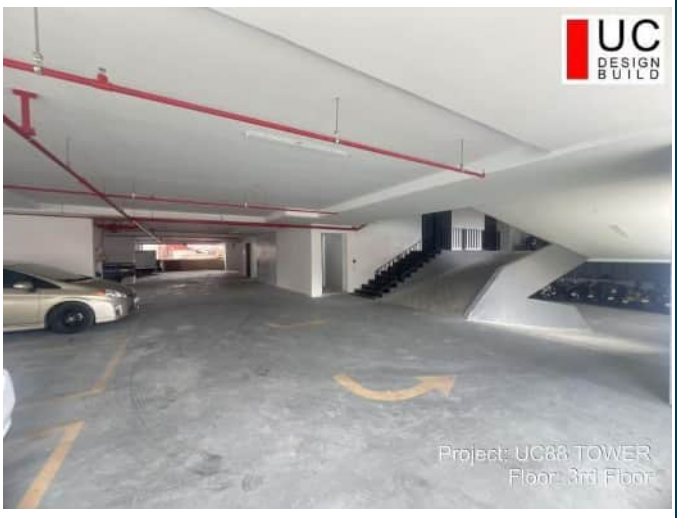
	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Ground Floor	Floor: Ground Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

Parking (2nd – 3nd Floor)

-Material store & parking area

-Parking area

	
Floor: 2nd Floor	Floor: 2nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Material store & parking area	Work: Material store & parking area
	
Floor: 2nd Floor	Floor: 2nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Material store & parking area	Work: Material store & parking area
	
Floor: 3rd Floor	Floor: 3rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Parking area	Work: Parking area

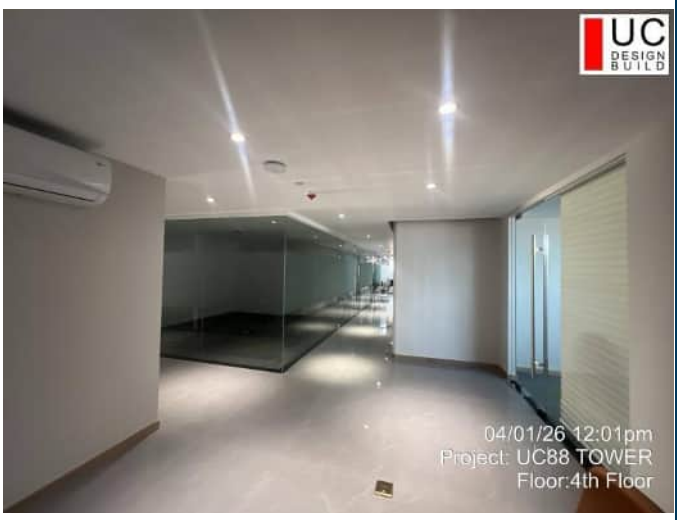
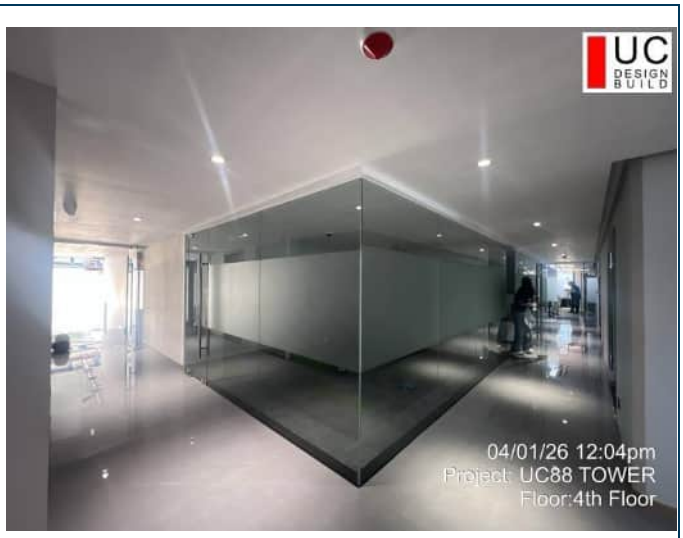
	
Floor: 3rd Floor	Floor: 3rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Parking area	Work: Parking area

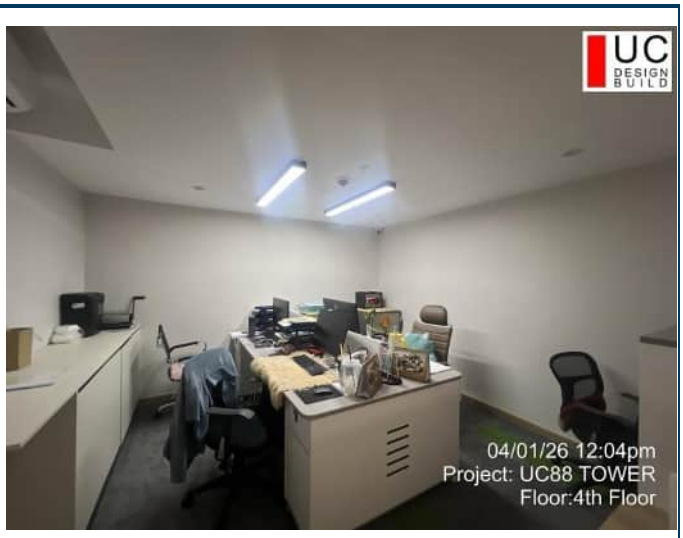
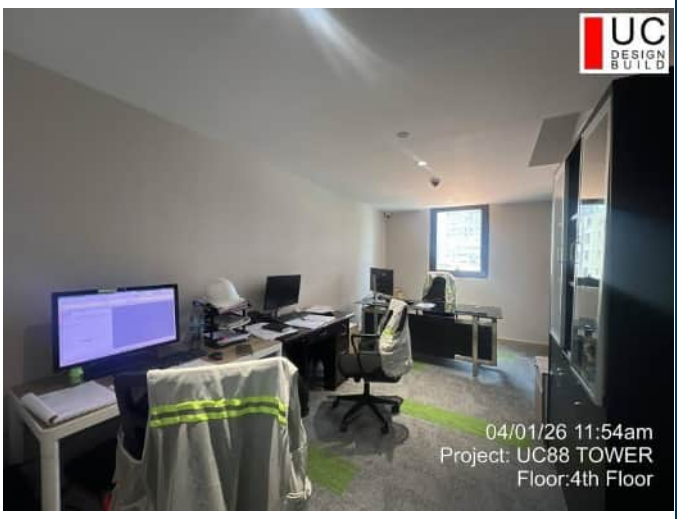
Parking &Hotel office (3Ath Floor)

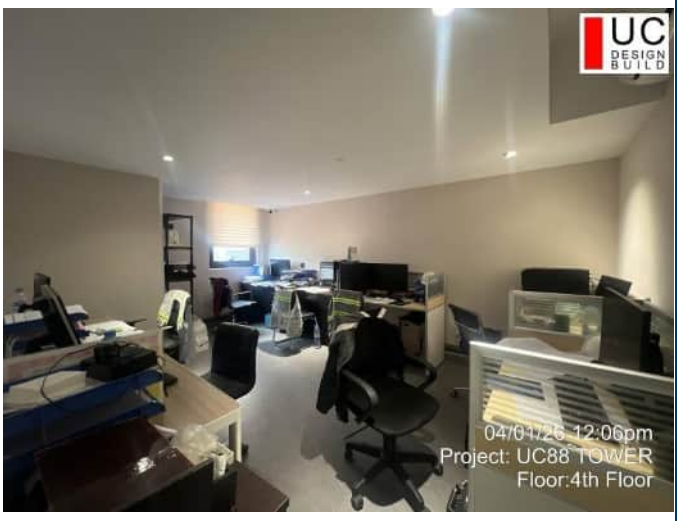
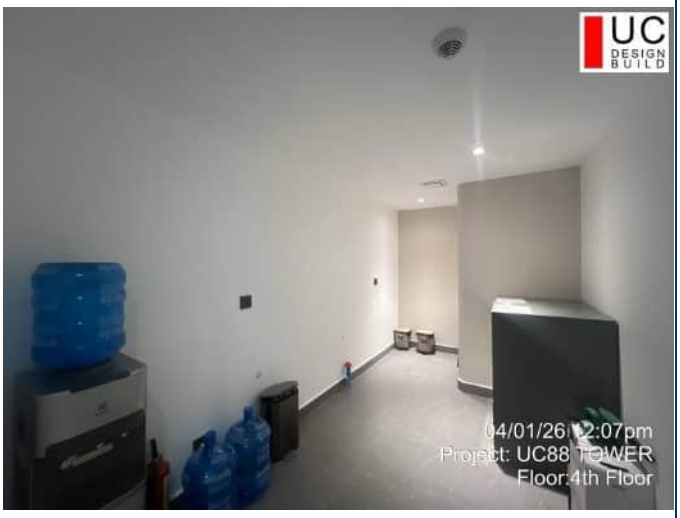
-Parking area

-Finishing & office furniture completed

	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Parking area	Work: Parking area
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing works completed	Work: Finishing works completed
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing works completed	Work: Finishing & Office furniture completed

	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing works completed	Work: Finishing & Office furniture completed
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing works completed	Work: Finishing works completed
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing & Office furniture completed	Work: Finishing & Office furniture completed

	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing & Office furniture completed	Work: Finishing works completed
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing & Office furniture completed	Work: Finishing & Office furniture completed
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing & Office furniture completed	Work: Finishing & Office furniture completed

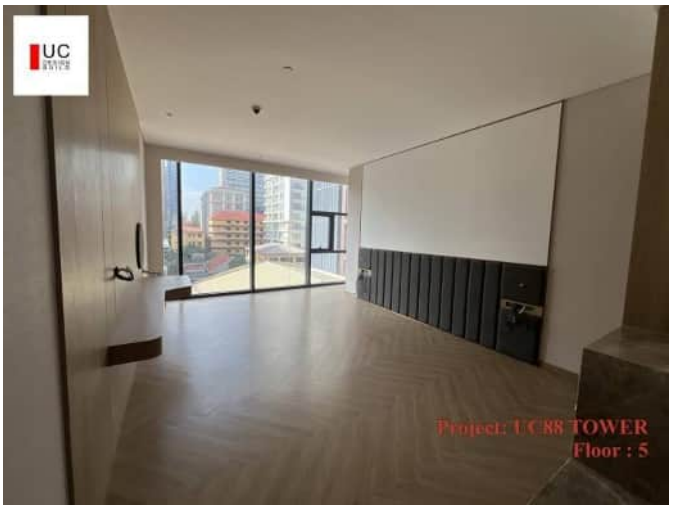
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing & Office furniture completed	Work: Finishing & Office furniture completed
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing & Office furniture completed	Work: Finishing & Office furniture completed
	
Floor: 3Ath Floor	Floor: 3Ath Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing works completed	Work: Finishing works completed

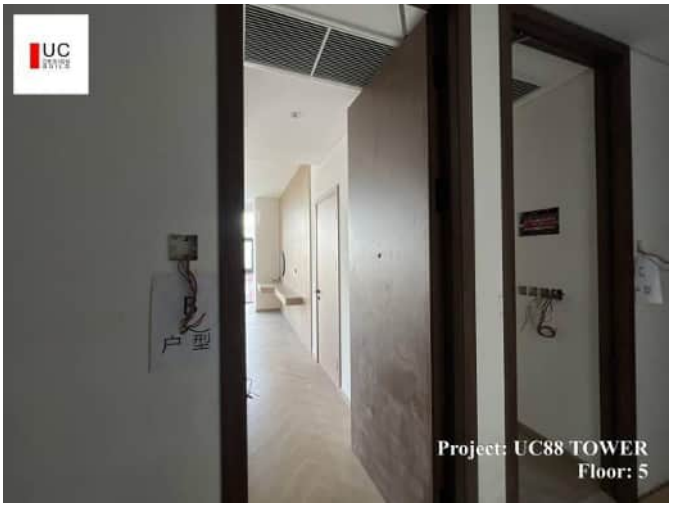
Hotel Floor (5th - 24th Floor)

5th - 19th Floor

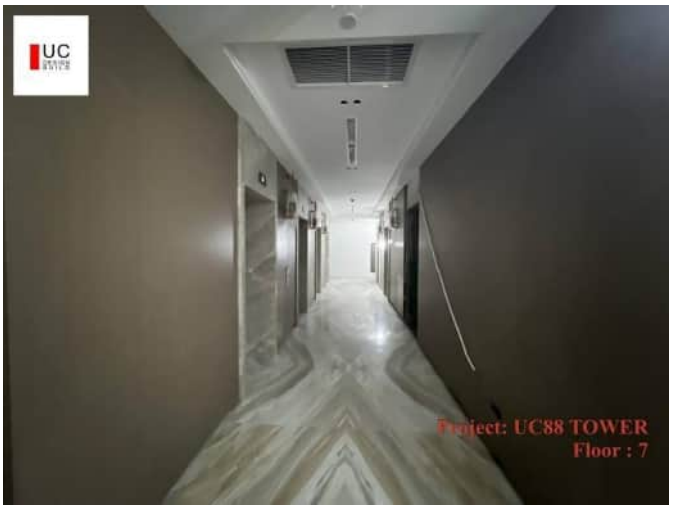
- Build-in work
- Build-in furniture work

	
Floor: 5th Floor	Floor: 5th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work
	
Floor: 5th Floor	Floor: 5th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work
	
Floor: 5th Floor	Floor: 5th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work

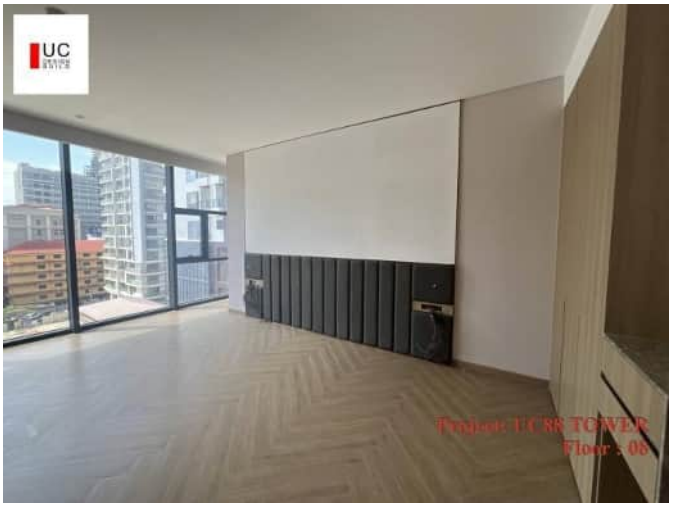
	
Floor: 5th Floor	Floor: 5th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work
	
Floor: 5th Floor	Floor: 5th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work
	
Floor: 5th Floor	Floor: 5th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work

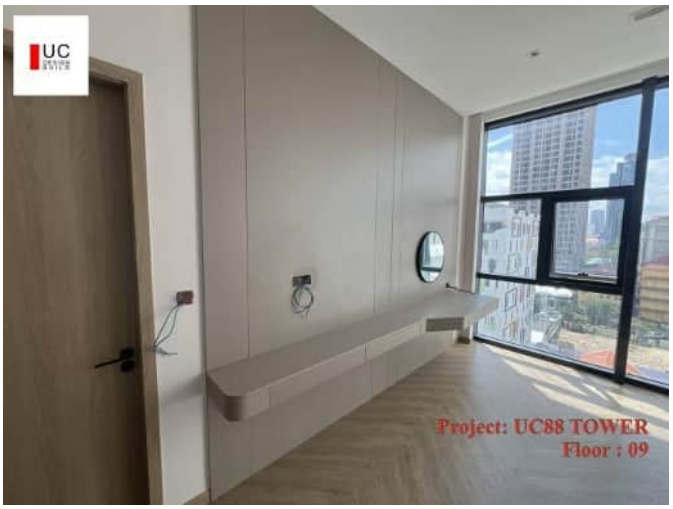
	
Floor: 5th Floor	Floor: 5th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work & Tile grouting work	Work: Build-in work
	
Floor: 6th Floor	Floor: 6th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 6th Floor	Floor: 6th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 6th Floor	Floor: 6th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 6th Floor	Floor: 6th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 6th Floor	Floor: 6th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 6th Floor	Floor: 6th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 6th Floor	Floor: 6th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 7th Floor	Floor: 7th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 7th Floor	Floor: 7th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 7th Floor	Floor: 7th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 8th Floor	Floor: 8th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 8th Floor	Floor: 8th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 8th Floor	Floor: 8th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall & Ceiling putty painting work	Work: Wall & Ceiling putty painting work
	
Floor: 8th Floor	Floor: 8th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

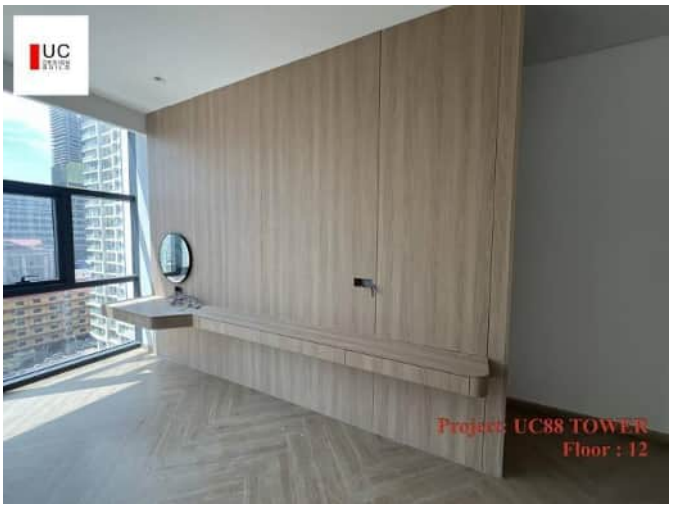
	
Floor: 8th Floor	Floor: 8th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 9th Floor	Floor: 9th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 9th Floor	Floor: 9th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 9th Floor	Floor: 9th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 9th Floor	Floor: 9th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall & Ceiling putty painting work	Work: Build-in furniture work
	
Floor: 9th Floor	Floor: 9th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 10th Floor	Floor: 10th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 10th Floor	Floor: 10th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 10th Floor	Floor: 10th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 10th Floor	Floor: 10th Floor
Date: 30-September -2026	Date 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 11th Floor	Floor: 11th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 11th Floor	Floor: 11th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

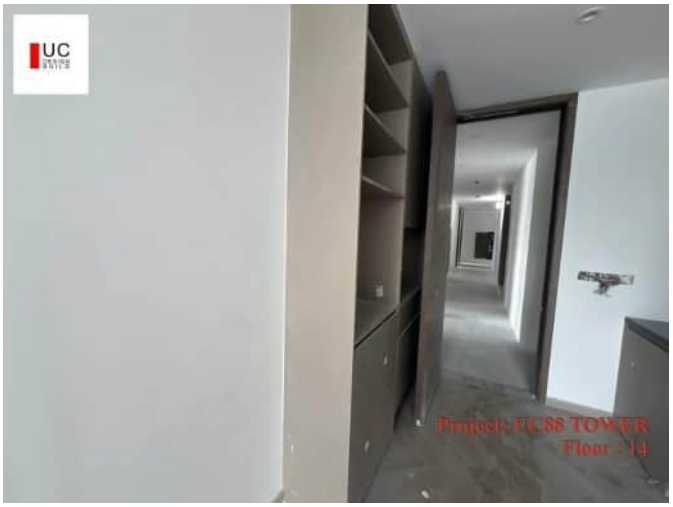
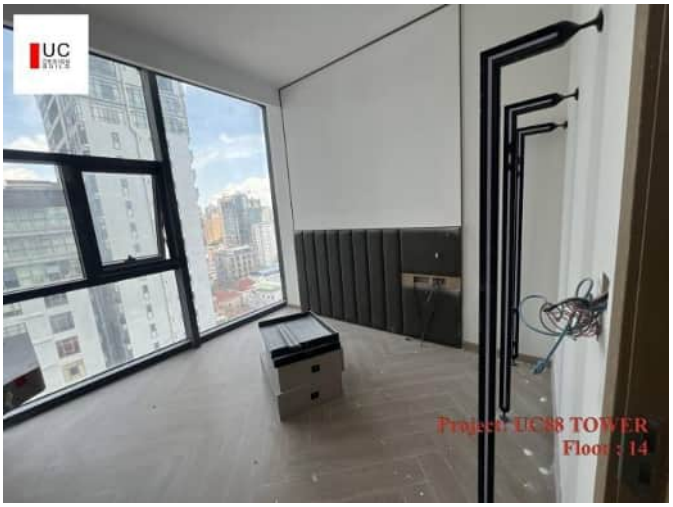
	
Floor: 11th Floor	Floor: 11th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 11th Floor	Floor: 11th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 12th Floor	Floor: 12th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 12th Floor	Floor: 12th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 12th Floor	Floor: 12th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 12th Floor	Floor: 12th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 13th Floor	Floor: 13th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 13th Floor	Floor: 13th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 13th Floor	Floor: 13th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 13th Floor	Floor: 13th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 13th Floor	Floor: 13th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 13th Floor	Floor: 14th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 14th Floor	Floor: 14th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 14th Floor	Floor: 14th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 14th Floor	Floor: 14th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 14th Floor	Floor: 14th Floor
Date : 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 14th Floor	Floor: 14th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 15th Floor	Floor: 15th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 15th Floor	Floor: 15th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 15th Floor	Floor: 15th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 15th Floor	Floor: 15th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

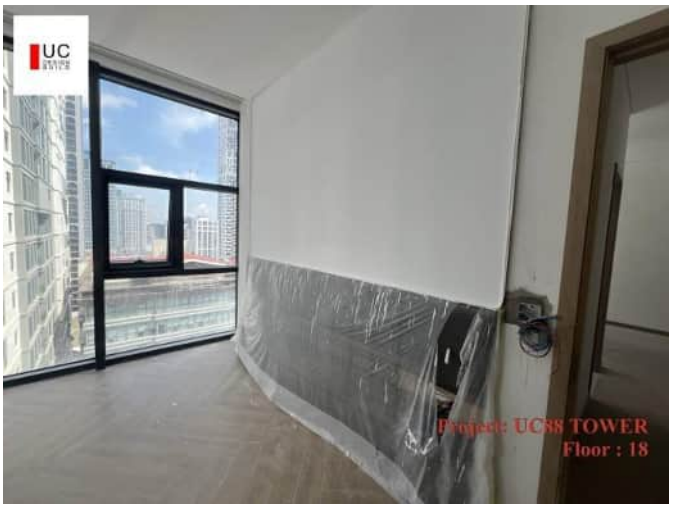
	
Floor: 15th Floor	Floor: 15th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 16th Floor	Floor: 16th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 16th Floor	Floor: 16th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 16th Floor	Floor: 16th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 16th Floor	Floor: 16th Floor
Date: 30-September -2026	Date 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 16th Floor	Floor: 16th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 16th Floor	Floor: 16th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 16th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 16th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 17th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 17th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 17th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

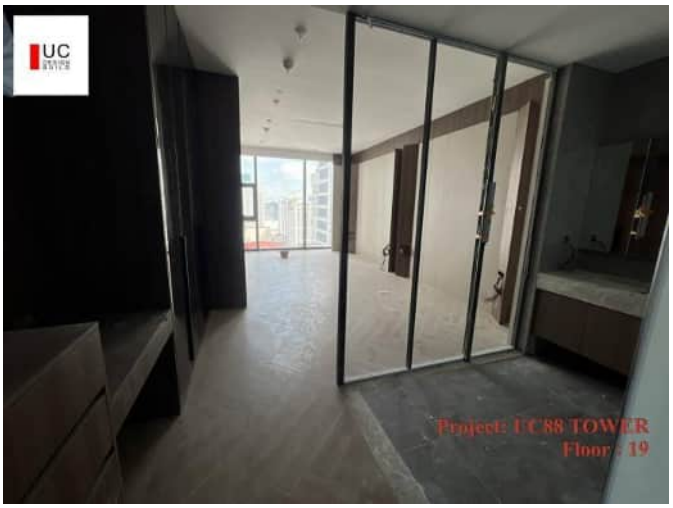
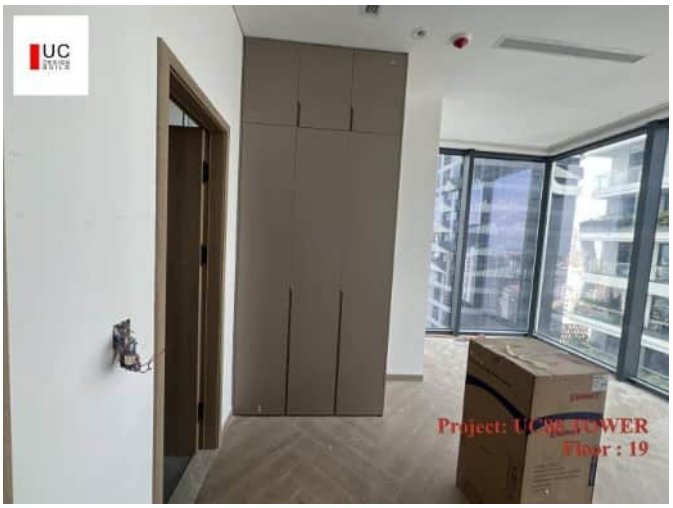
	
Floor: 17th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 17th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 17th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 17th Floor	Floor: 17th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling work	Work: Build-in furniture work
	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 18th Floor	Floor: 18th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 19th Floor	Floor: 19th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

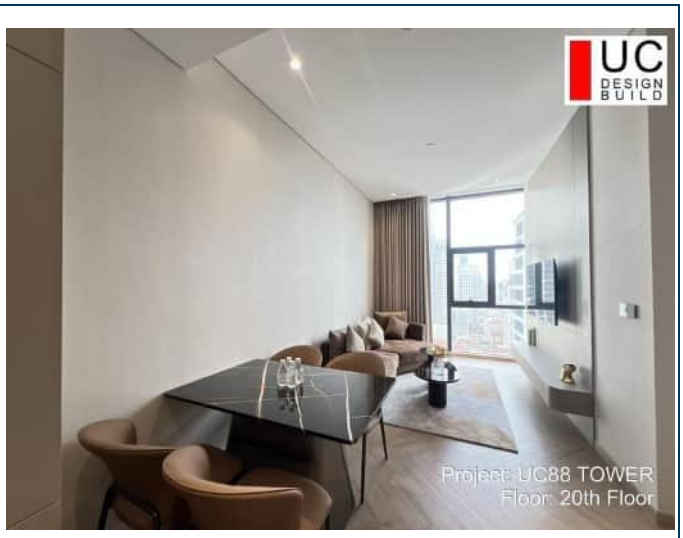
	
Floor: 19th Floor	Floor: 19th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 19th Floor	Floor: 19th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 19th Floor	Floor: 19th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

	
Floor: 19th Floor	Floor: 19th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work
	
Floor: 19th Floor	Floor: 19th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in furniture work	Work: Build-in furniture work

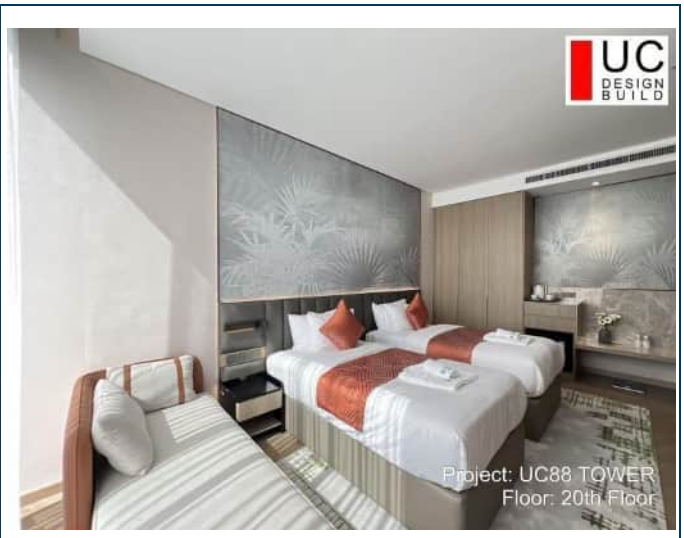
Hotel Floor 20th Floor

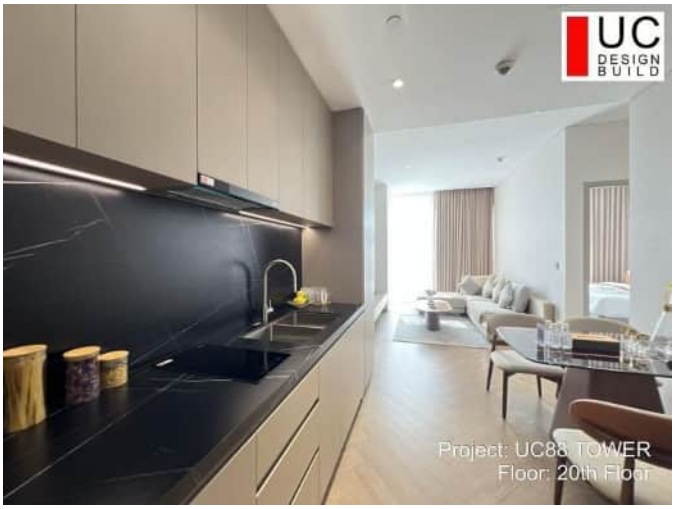
- Interior finishing work
- Interior works & loose furniture completed

	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior finishing works	Work: Interior finishing works
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior finishing works	Work: Interior finishing works
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

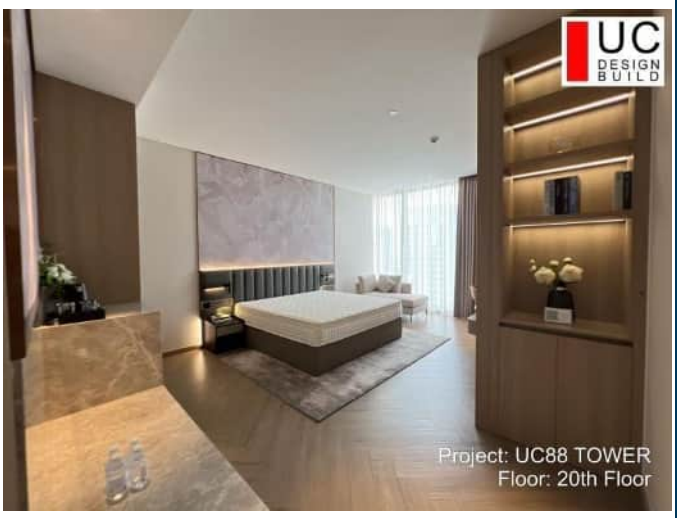
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

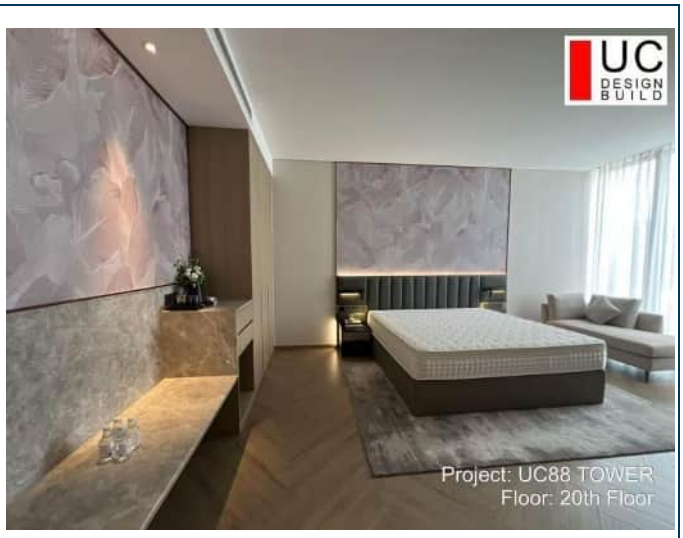
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

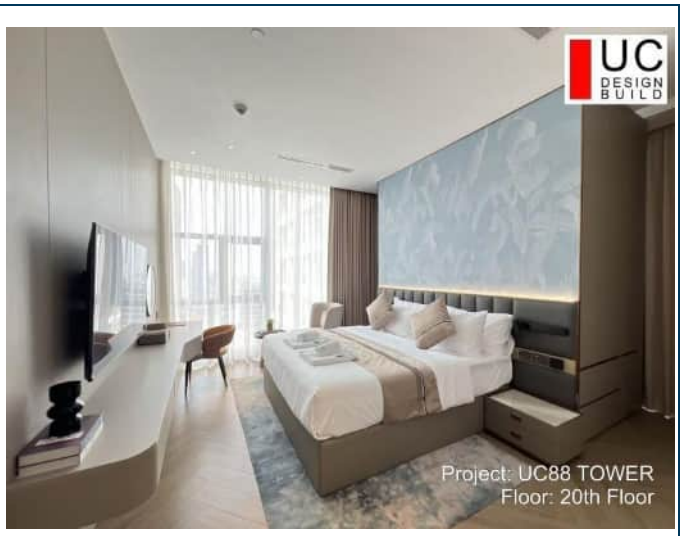
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

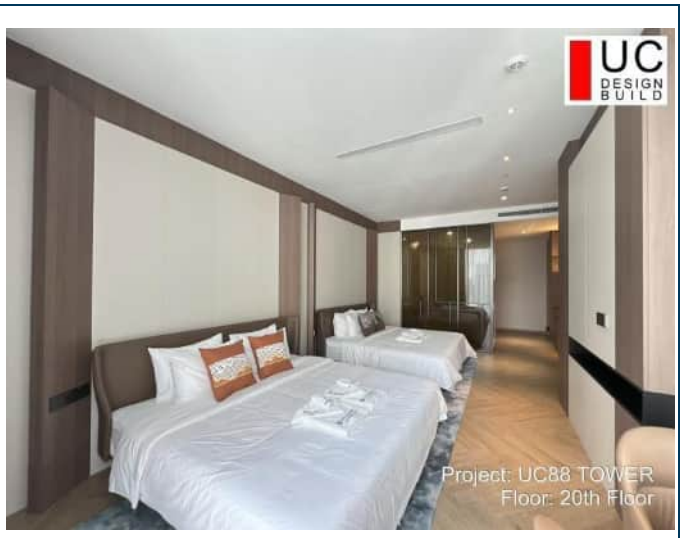
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 20th Floor	Floor: 20th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

Hotel Floor 21th -24th Floor

- Build-in material and accessory arrived
- Ceiling & wall skim coat works
- Tiling works
- Masonry work
- Painting work
- Waterproofing works
- MEP & Ceiling works
- Glass works
- MEP works
- Material store area

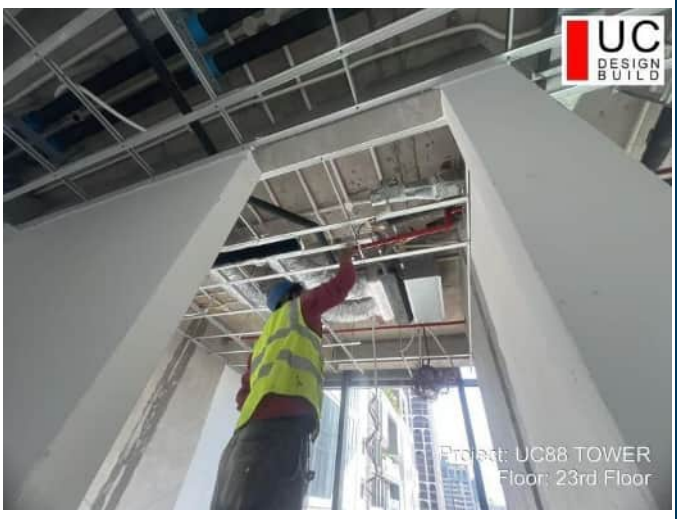
	
Floor: 21st Floor	Floor: 21st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in material and accessory arrived	Work: Build-in material and accessory arrived
	
Floor: 21st Floor	Floor: 21st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Ceiling & wall skim coat works
	
Floor: 21st Floor	Floor: 21st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Ceiling & wall skim coat works

	
Floor: 21st Floor	Floor: 21st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Ceiling & wall skim coat works
	
Floor: 21st Floor	Floor: 21st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Ceiling & wall skim coat works
	
Floor: 21st Floor	Floor: 21st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Tiling works

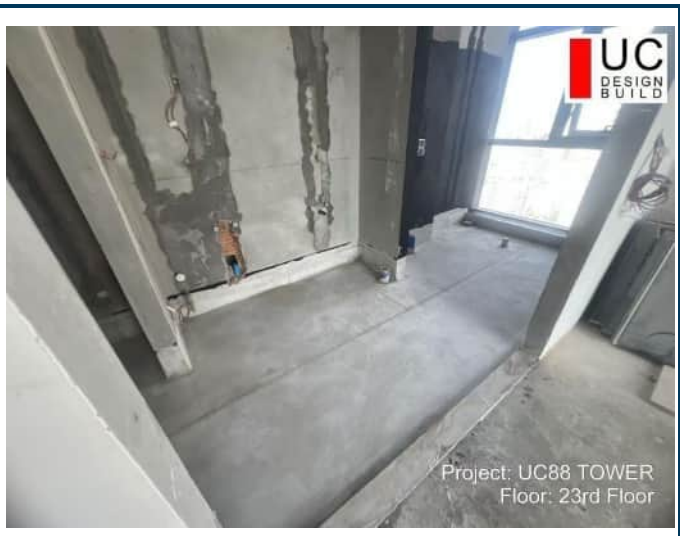
	
Floor: 22nd Floor	Floor: 22nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry works	Work: Masonry works
	
Floor: 22nd Floor	Floor: 22nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry works	Work: Masonry works
	
Floor: 22nd Floor	Floor: 22nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Painting works	Work: Masonry works

	
Floor: 22nd Floor	Floor: 22nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling works	Work: Tiling works
	
Floor: 22nd Floor	Floor: 22nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling works	Work: Tiling works
	
Floor: 22nd Floor	Floor: 22nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling works	Work: Tiling works

	
Floor: 22nd Floor	Floor: 22nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling works	Work: Tiling and waterproofing works
	
Floor: 22nd Floor	Floor: 22nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Waterproofing works	Work: Waterproofing works
	
Floor: 23rd Floor	Floor: 23rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Ceiling & wall skim coat works

	
Floor: 23rd Floor	Floor: 23rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling works	Work: MEP & Ceiling works
	
Floor: 23rd Floor	Floor: 23rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling works	Work: MEP & Ceiling works
	
Floor: 23rd Floor	Floor: 23rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling works	Work: MEP & Ceiling works

	
Floor: 23rd Floor	Floor: 23rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling works	Work: MEP & Ceiling works
	
Floor: 23rd Floor	Floor: 23rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling works	Work: Glass works
	
Floor: 23rd Floor	Floor: 23rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Waterproofing works	Work: Waterproofing works

	
Floor: 23rd Floor	Floor: 23rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Waterproofing works	Work: Waterproofing works
	
Floor: 24th Floor	Floor: 24th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling works	Work: MEP works
	
Floor: 24th Floor	Floor: 24th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP works	Work: Glass works

	
Floor: 24th Floor	Floor: 24th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Material store area	Work: Material store area
	
Floor: 24th Floor	Floor: 24th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Material store area	Work: Material store area

Facilities (25th floor)

-MEP work

-Glass work

	
Floor: 25th Floor	Floor: 25th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP works	Work: MEP works
	
Floor: 25th Floor	Floor: 25th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP works	Work: Glass works
	
Floor: 25th Floor	Floor: 25th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP works	Work: MEP works

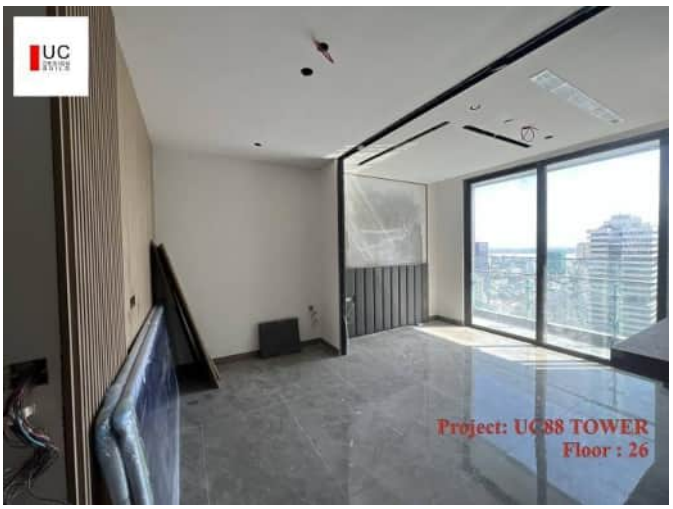
	
Floor: 25th Floor	Floor: 25th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP works	Work: MEP works

Residence Floor (26th - 33thFloor)

26th - 32th Floor

- Build-in work
- Ceiling work
- MEP & ceiling works
- Tiling & ceiling works
- Ceiling & wall skim coat works
- Tiling demolition works
- MEP work
- Masonry work

	
Floor: 26th Floor	Floor: 26th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work
	
Floor: 26th Floor	Floor: 26th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work
	
Floor: 26th Floor	Floor: 26th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work

	
Floor: 26th Floor	Floor: 26th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work
	
Floor: 26th Floor	Floor: 26th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work
	
Floor: 26th Floor	Floor: 26th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Build-in work	Work: Build-in work

	
Floor: 26th Floor	Floor: 26th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling works	Work: Ceiling works
	
Floor: 26th Floor	Floor: 26th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling works	Work: Ceiling works
	
Floor: 27th Floor	Floor: 27th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & ceiling works	Work: MEP & ceiling works

	
Floor: 27th Floor	Floor: 27th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 27th Floor	Floor: 27th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 27th Floor	Floor: 27th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works

	
Floor: 27th Floor	Floor: 27th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 27th Floor	Floor: 27th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 27th Floor	Floor: 27th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works

	
Floor: 27th Floor	Floor: 27th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 28th Floor	Floor: 28th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Ceiling & wall skim coat works
	
Floor: 28th Floor	Floor: 28th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works

	
Floor: 28th Floor	Floor: 28th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 28th Floor	Floor: 28th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 28th Floor	Floor: 28th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works

	
Floor: 29th Floor	Floor: 29th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Ceiling & wall skim coat works
	
Floor: 29th Floor	Floor: 29th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 29th Floor	Floor: 29th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works

	
Floor: 29th Floor	Floor: 29th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 29th Floor	Floor: 29th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 29th Floor	Floor: 29th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works

	
Floor: 30th Floor	Floor: 30th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Tiling & ceiling works
	
Floor: 30th Floor	Floor: 30th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 30th Floor	Floor: 30th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works

	
Floor: 31st Floor	Floor: 31st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling & wall skim coat works	Work: Ceiling & wall skim coat works
	
Floor: 31st Floor	Floor: 31st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 31st Floor	Floor: 31st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works

	
Floor: 31st Floor	Floor: 31st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 31st Floor	Floor: 31st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling & ceiling works	Work: Tiling & ceiling works
	
Floor: 32nd Floor	Floor: 32nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tiling demolition works	Work: Tiling demolition works

	
Floor: 32nd Floor	Floor: 32nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work
	
Floor: 32nd Floor	Floor: 32nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work
	
Floor: 32nd Floor	Floor: 32nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work

	
Floor: 32nd Floor	Floor: 32nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 32nd Floor	Floor: 32nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 32nd Floor	Floor: 32nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work

33thFloor

- Interior finishing work
- Interior work & Loose furniture Completed

	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior finishing works	Work: Interior finishing works
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior finishing works	Work: Interior finishing works
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

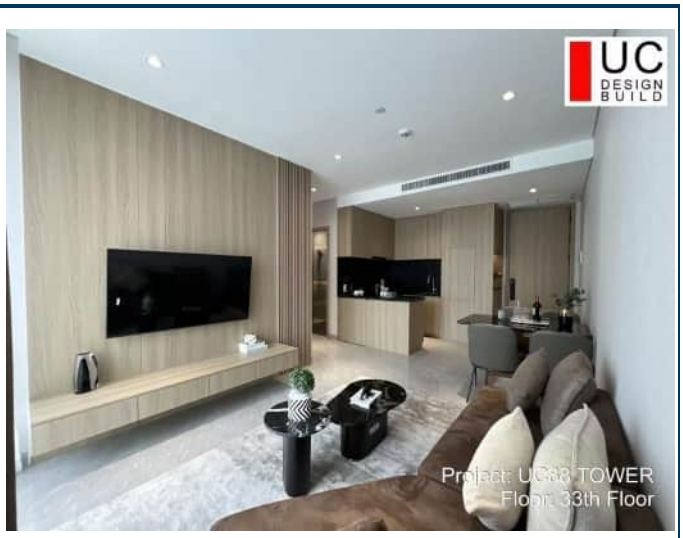
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

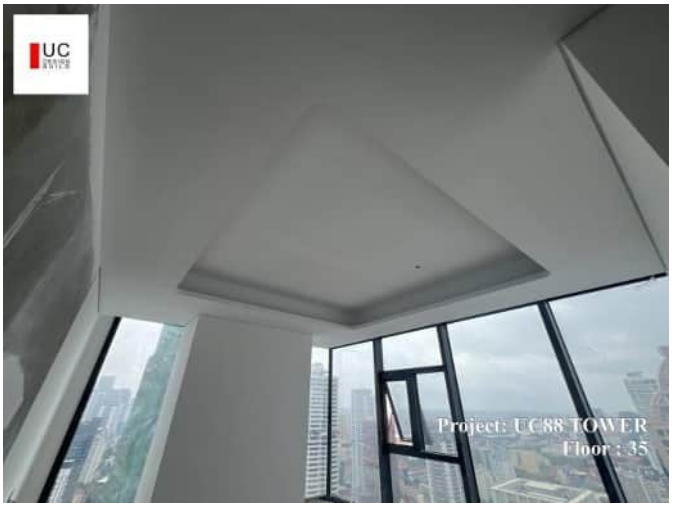
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 33th Floor	Floor: 33th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

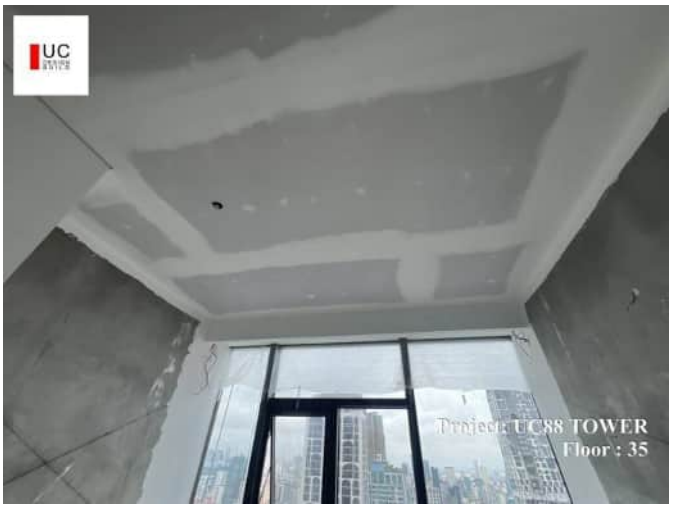
Premium floor (35th - 43th Floor)

35th - 41th Floor

- Ceiling work
- MEP & Ceiling work
- Waterproofing work
- Wall backing & Ceiling frame works
- Masonry work
- MEP & pre waterproofing works
- Glass work
- Tile work
- Floor screeding work

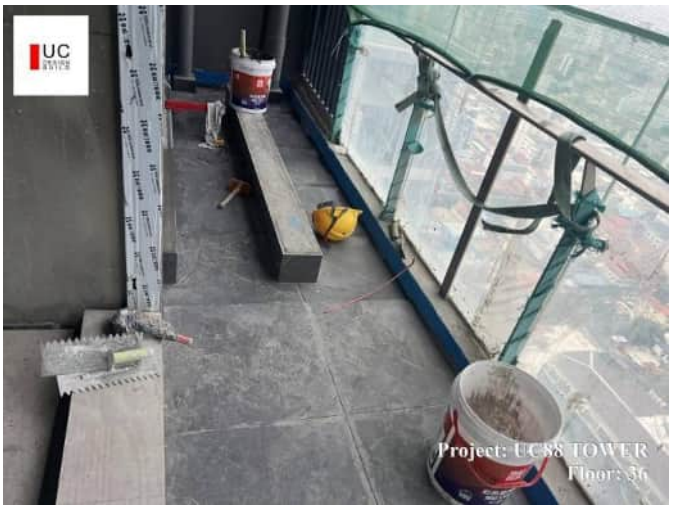
	
Floor: 35th Floor	Floor: 35th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling work	Work: MEP & Ceiling work
	
Floor: 35th Floor	Floor: 35th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling work	Work: MEP & Ceiling work
	
Floor: 35th Floor	Floor: 35th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Waterproofing work	Work: MEP & Ceiling work

	
Floor: 35th Floor	Floor: 35th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling work	Work: Waterproofing work
	
Floor: 35th Floor	Floor: 35th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling work	Work: MEP & Ceiling work
	
Floor: 35th Floor	Floor: 35th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Waterproofing work	Work: MEP & Ceiling work

	
Floor: 35th Floor	Floor: 35th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling work	Work: MEP & Ceiling work
	
Floor: 35th Floor	Floor: 35th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & Ceiling work	Work: MEP & Ceiling work
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work

	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling frame works	Work: MEP work
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works

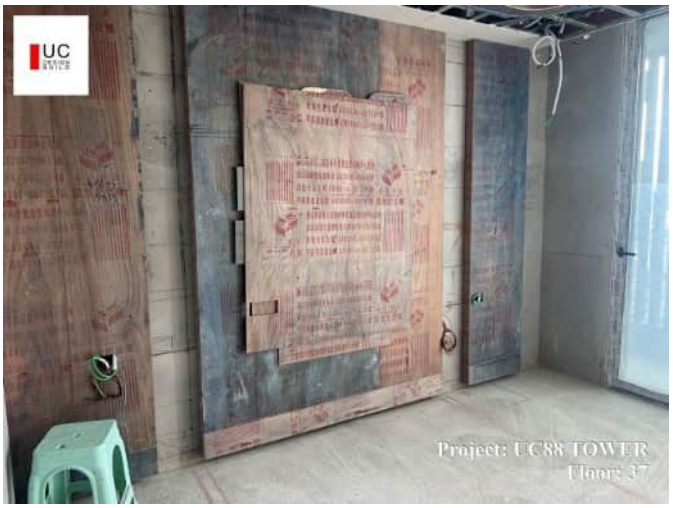
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling frame works	Work: Ceiling frame works
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works

	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP & pre waterproofing works	Work: Masonry work
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works

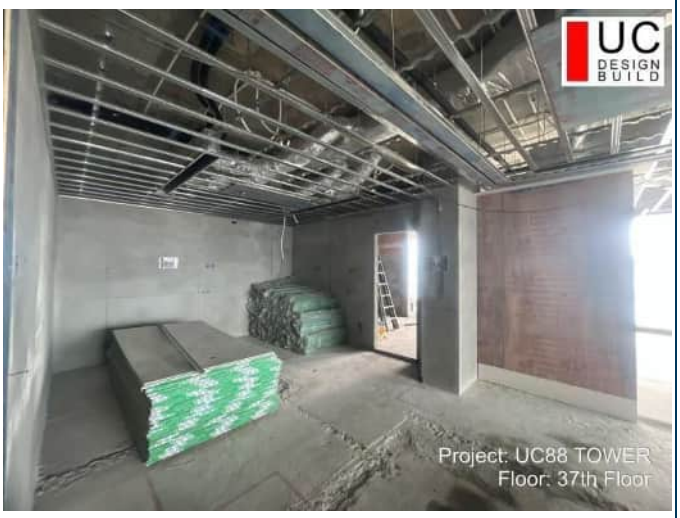
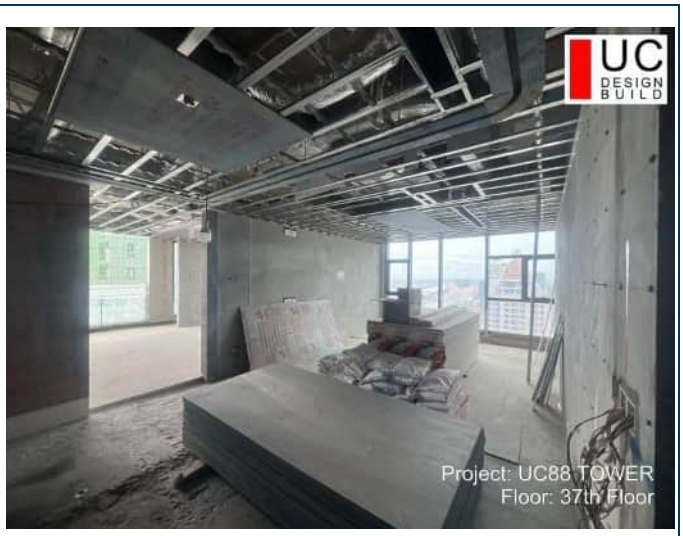
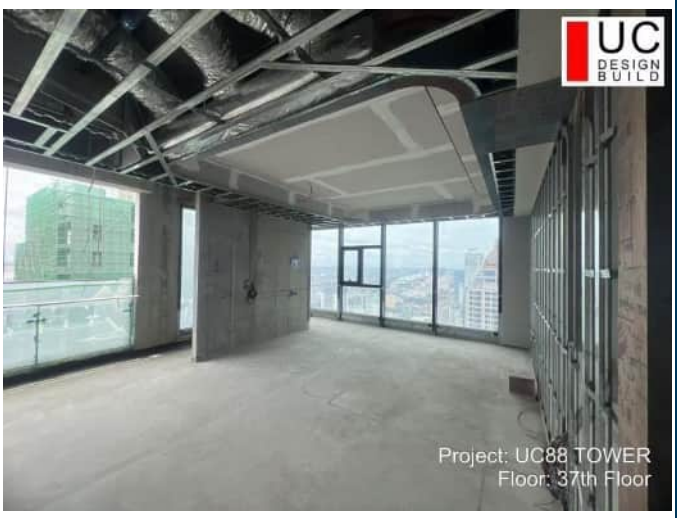
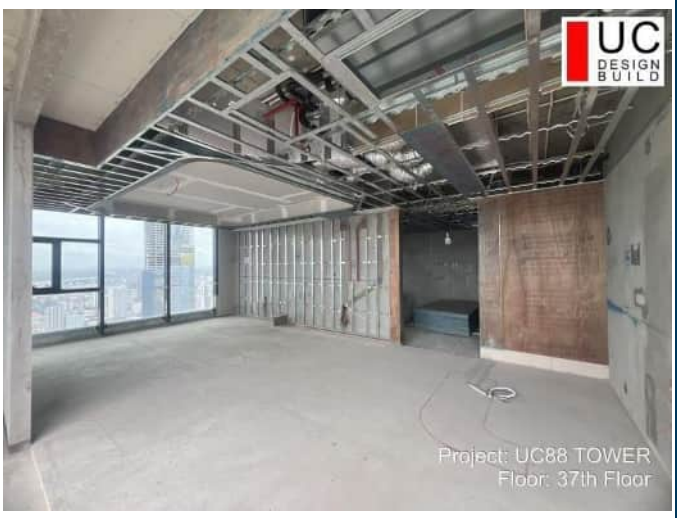
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 36th Floor	Floor: 36th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Wall backing & Ceiling frame works

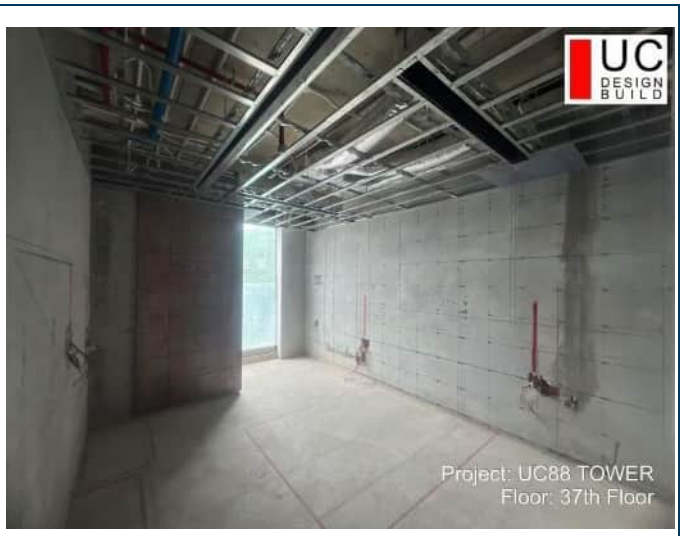
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling works	Work: Ceiling works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling works	Work: Ceiling works

	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling works	Work: Waterproofing work
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Ceiling works	Work: Wall backing & Ceiling frame works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Waterproofing work	Work: Ceiling works

	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Waterproofing work	Work: Wall backing & Ceiling frame works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Waterproofing work
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works

	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Pre-waterproofing work	Work: Ceiling frame works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works

	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works

	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Wall backing & Ceiling frame works	Work: Wall backing & Ceiling frame works
	
Floor: 37th Floor	Floor: 37th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Pre-waterproofing work	Work: Waterproofing work
	
Floor: 38th Floor	Floor: 38th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work

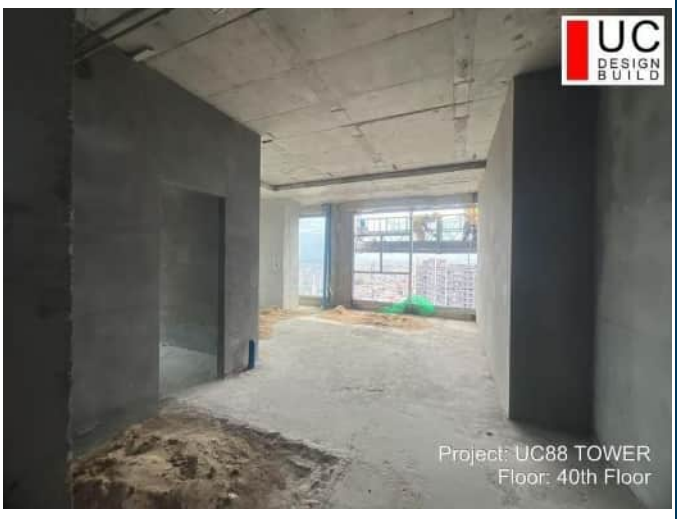
	
Floor: 38th Floor	Floor: 38th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 38th Floor	Floor: 38th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 38th Floor	Floor: 38th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work

	
Floor: 38th Floor	Floor: 38th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 38th Floor	Floor: 38th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work
	
Floor: 38th Floor	Floor: 38th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work

	
Floor: 38th Floor	Floor: 38th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: Masonry work
	
Floor: 39th Floor	Floor: 39th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 39th Floor	Floor: 39th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work

	
Floor: 39th Floor	Floor: 39th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 39th Floor	Floor: 39th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 39th Floor	Floor: 39th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: Masonry work

	
Floor: 39th Floor	Floor: 39th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 39th Floor	Floor: 39th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 40th Floor	Floor: 40th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work

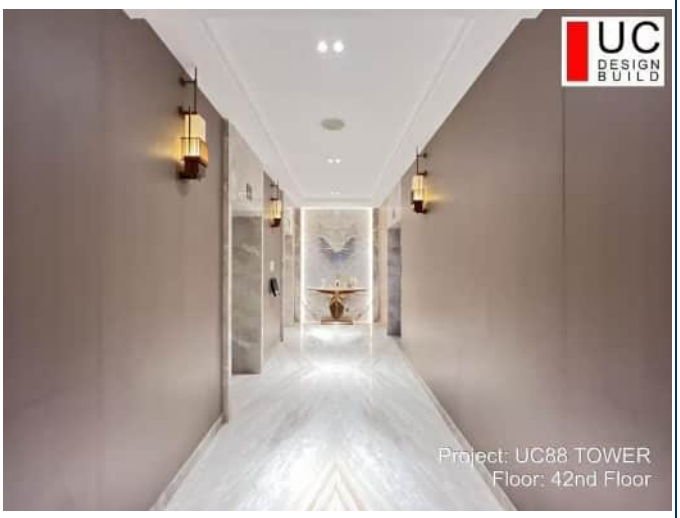
	
Floor: 40th Floor	Floor: 40th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Glass curtain wall works	Work: Masonry work
	
Floor: 40th Floor	Floor: 40th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Glass curtain wall works	Work: Masonry work
	
Floor: 40th Floor	Floor: 40th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Glass work	Work: Glass work

	
Floor: 41st Floor	Floor: 41st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: Waterproof work
	
Floor: 41st Floor	Floor: 41st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: Waterproof work
	
Floor: 41st Floor	Floor: 41st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Waterproof work	Work: Tile work

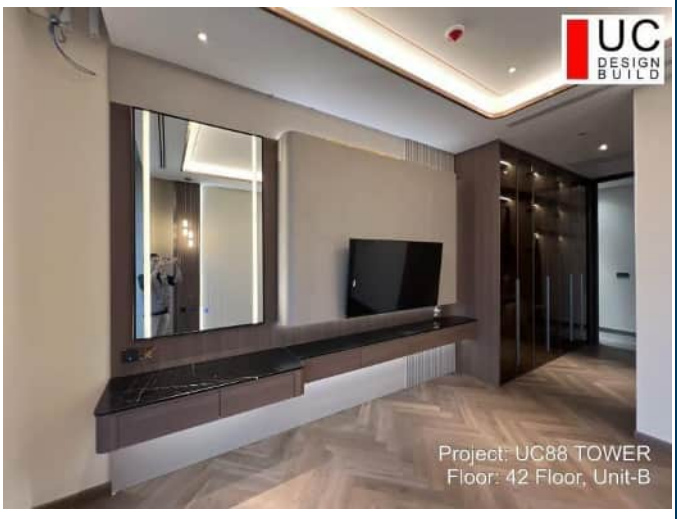
	
Floor: 41st Floor	Floor: 41st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work
	
Floor: 41st Floor	Floor: 41st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Floor screeding work
	
Floor: 41st Floor	Floor: 41st Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Floor screeding work	Work: Floor screeding work

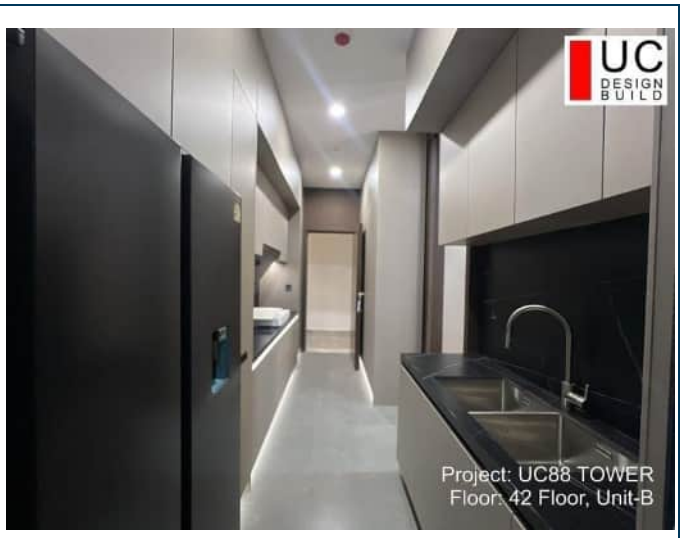
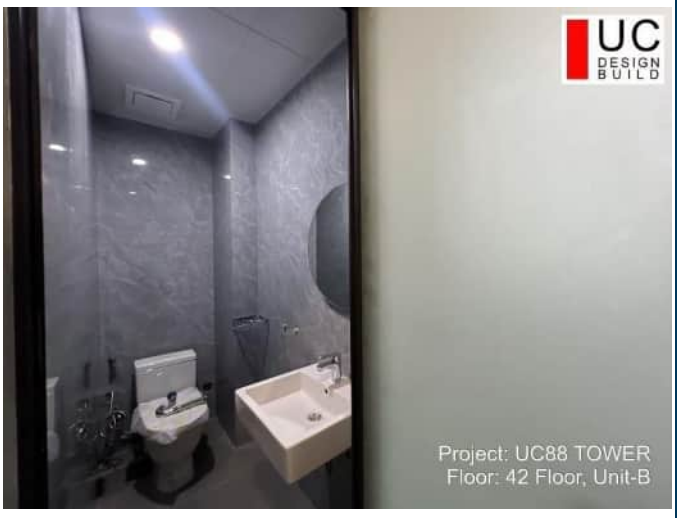
Premium floor 42ndFloor

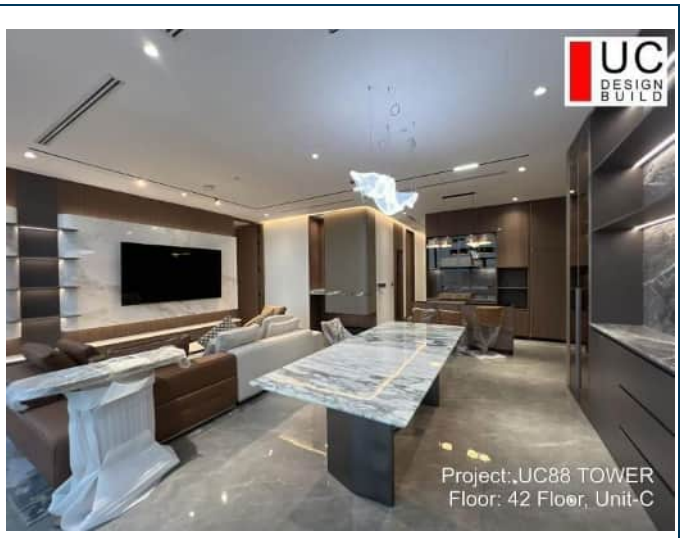
- Interior work & Loose furniture Completed

	
Floor: 42nd Floor	Floor: 42nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing work	Work: Finishing work
	
Floor: 42nd Floor	Floor: 42nd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Finishing work	Work: Finishing work
	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-B	Floor: 42nd Floor, Unit-B
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

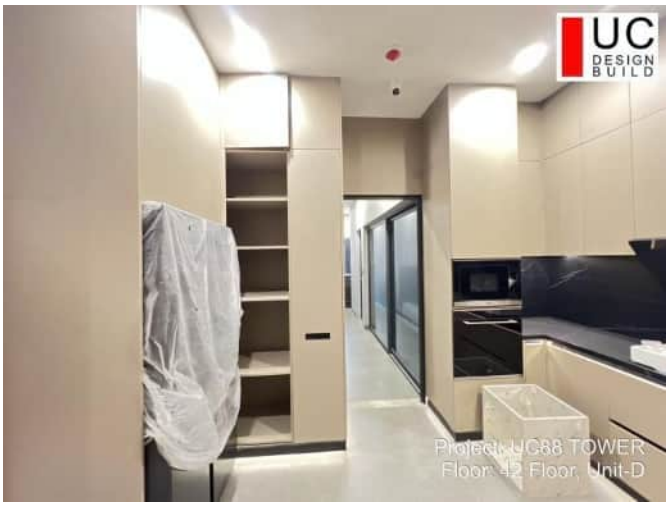
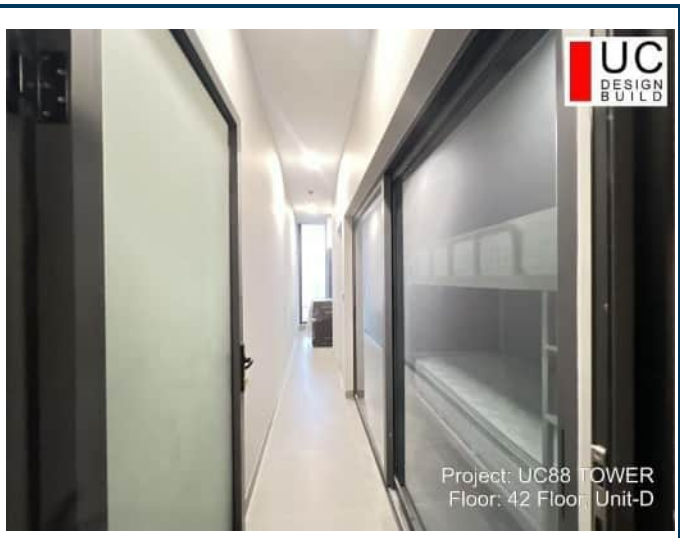
	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-C	Floor: 42nd Floor, Unit-C
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

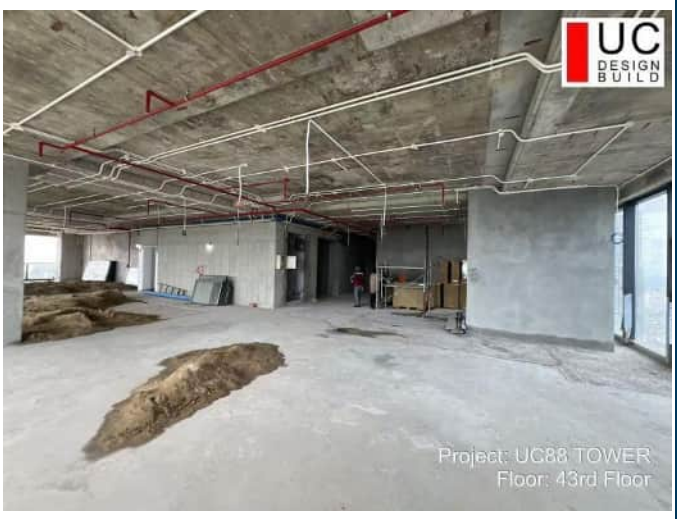
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

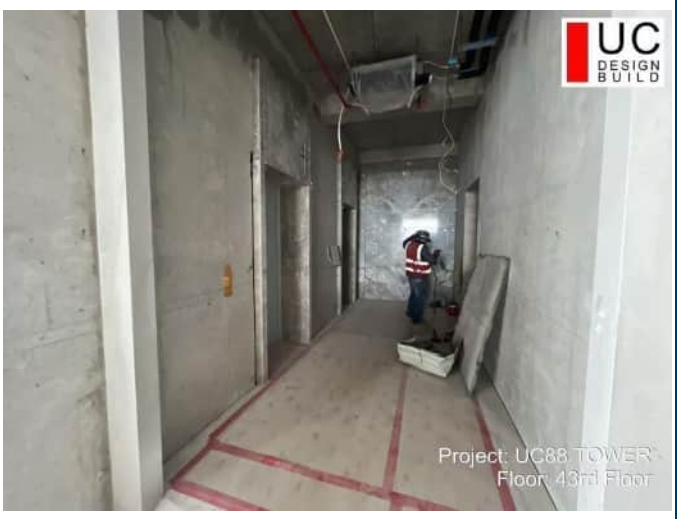
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: 42nd Floor, Unit-D	Floor: 42nd Floor, Unit-D
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

Premium floor 43rd Floor

- MEP work
- Marble work

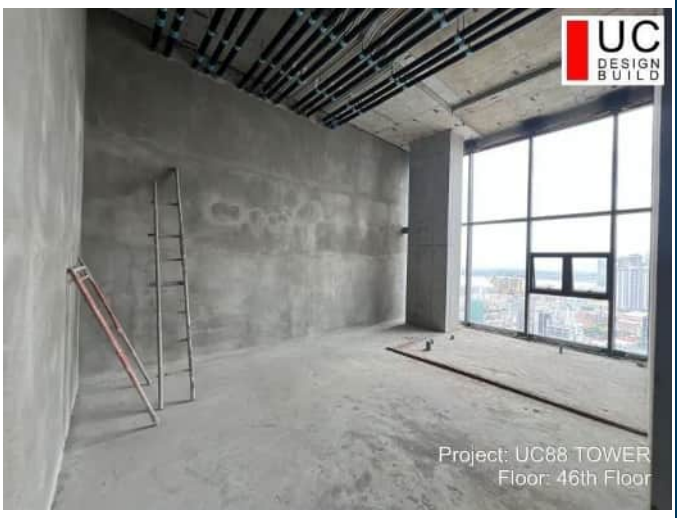
	
Floor: 43rd Floor	Floor: 43rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work
	
Floor: 43rd Floor	Floor: 43rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 43rd Floor	Floor: 43rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: MEP work

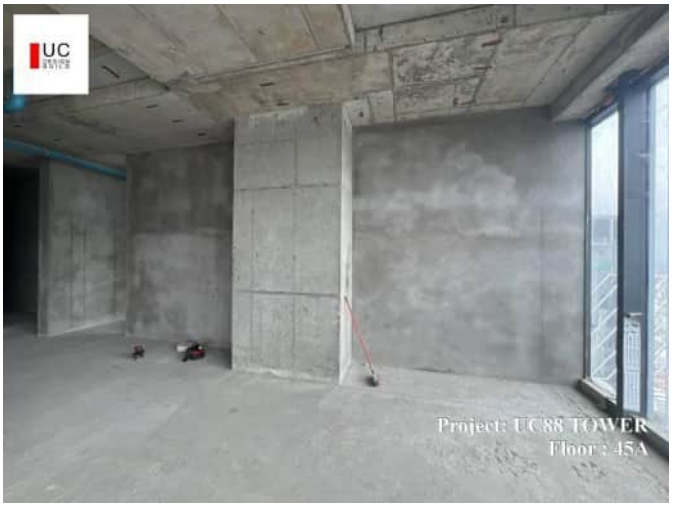
	
Floor: 43rd Floor	Floor: 43rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: MEP work	Work: Masonry work
	
Floor: 43rd Floor	Floor: 43rd Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Marble work	Work: Marble work

Premium duplex penthouse (45th - 46th Floor)

- Glass curtain wall work
- MEP work Masonry work
- Masonry work

	
Floor: 45th Floor	Floor: 45th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Glass curtain wall works	Work: MEP work
	
Floor: 45th Floor	Floor: 45th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 45th Floor	Floor: 45th Floor
Work: 30-September -2026	Work: 30-September -2026
Work: Masonry work	Work: Masonry work

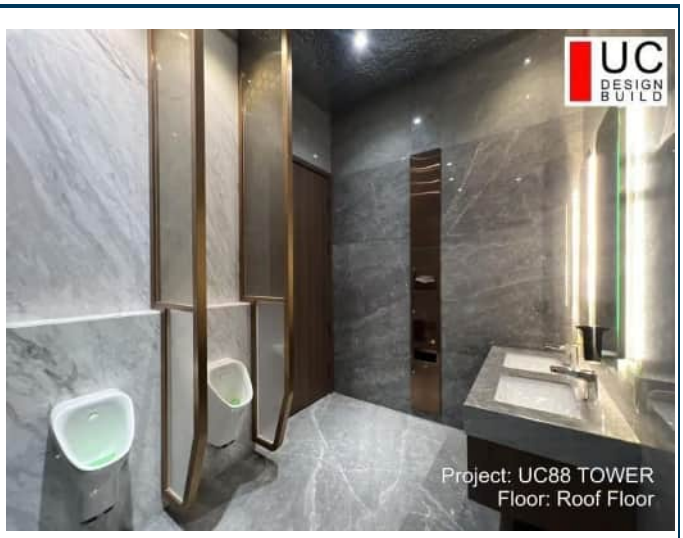
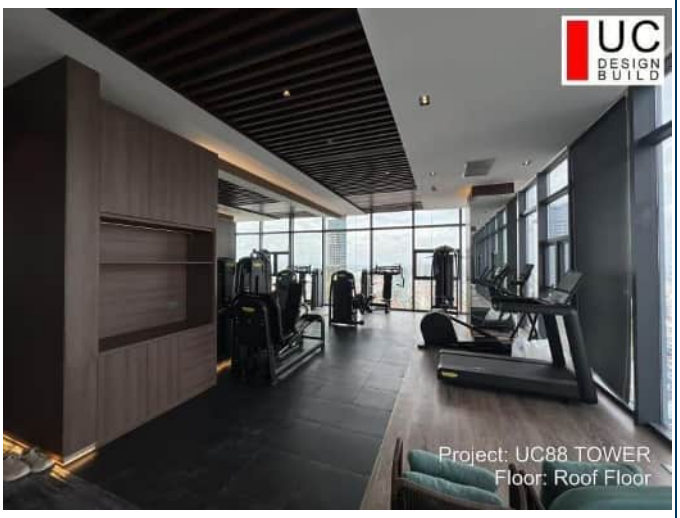
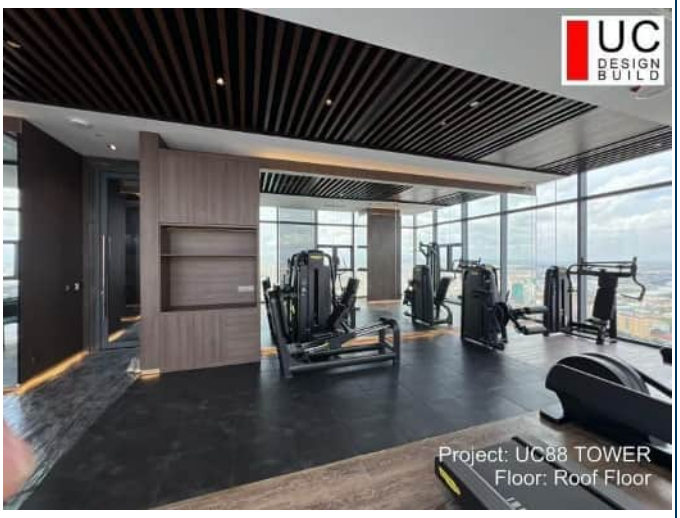
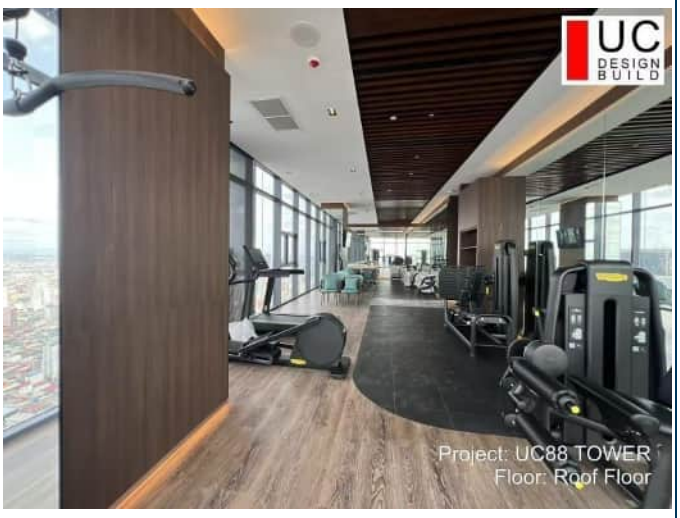
	
Floor: 46th Floor	Floor: 46th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 46th Floor	Floor: 46th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 46th Floor	Floor: 46th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work

	
Floor: 46th Floor	Floor: 46th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 46th Floor	Floor: 46th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work
	
Floor: 46th Floor	Floor: 46th Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Masonry work	Work: Masonry work

Roof top Floor

-Interior work & Loose furniture completed
-Exterior painting work
-Marble work
-Tower crane dismantling work
-Tile work
- Tower crane dismantling work

	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -202630-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

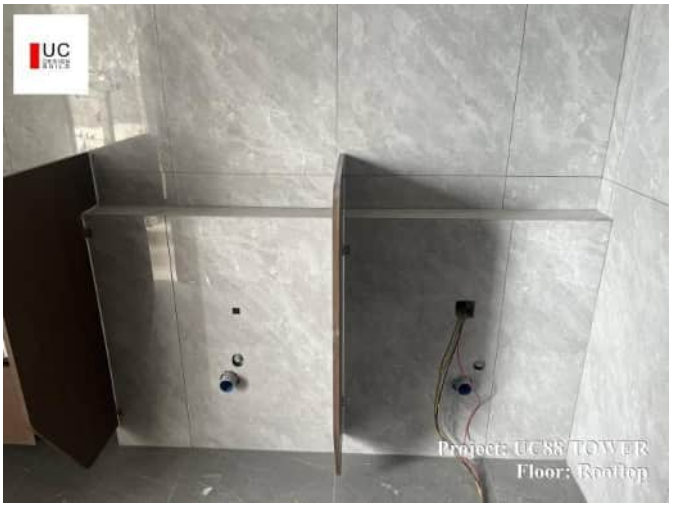
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed

	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Interior works & Loose furniture completed	Work: Interior works & Loose furniture completed
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Exterior painting work	Work: Exterior painting work
	
Floor: Roof Floor	Floor: Roof Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Marble work	Work: Marble work

	
Floor: Roof Top Floor	Floor: Roof Top Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tower crane dismantling work	Work: Tower crane dismantling work
	
Floor: Roof Top Floor	Floor: Roof Top Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tile work	Work: Tile work
	
Floor: Roof Top Floor	Floor: Roof Top Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tile work	Work: Tile work

	
Floor: Helicopter Floor	Floor: Helicopter Floor
Date: 30-September -2026	Date: 30-September -2026
Work: Tower crane dismantling work	Work: Tower crane dismantling work
